

Interstate 605/Katella Avenue Interchange Project Update



I-605  | Katella
INTERCHANGE



Safer. Smarter. Smoother.



Project Overview

- Measure M2 - Project M
- Project included in Next 10 Delivery Plan; advanced by ten years
 - Environmental phase completed in October 2018
 - Design phase completed in September 2024
- Construction estimate \$30 million
 - funded by federal Surface Transportation Block Grant and Measure M2 funds





Project Overview

- Modifies northbound and southbound ramps at Katella Avenue
- Improves operations for all modes (vehicular, bicycle, and pedestrian)
- Closes the gaps in existing bicycle lanes
- Enhances sidewalk connectivity through interchange



Project Improvements

- Provide continuous sidewalks between Coyote Creek Channel and Civic Center Drive
- Add class II bicycle lanes in each direction of Katella Avenue
- Enhance pedestrian safety

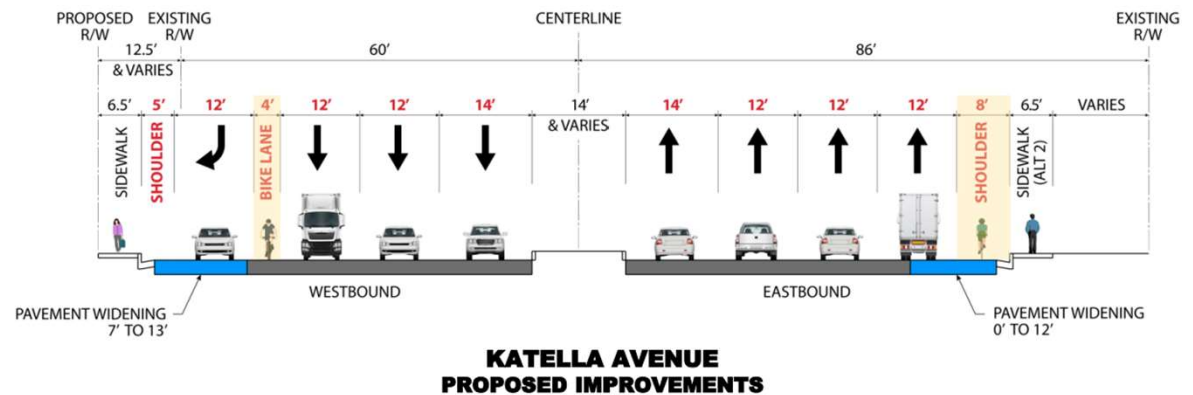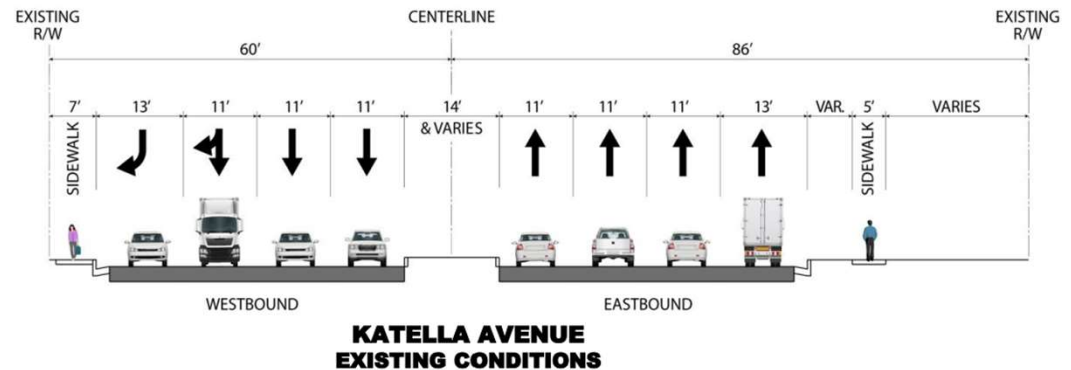

Milestone Schedule



Milestone	Timeframe
Completed Final Design	September 2024
Advertise for Construction	November 2024
Begin Construction	Spring 2025
Complete Construction	Fall 2026

Dates are subject to change.

Public Outreach

- Stakeholder ascertainment
- Briefings and presentations
- In-person/virtual community meetings
- Community booths and events
- Business and school outreach
- Collateral development
- Construction alert
- Social media
- Closures/detour map

