



## MEASURE M2 PROGRESS REPORT

Fourth Quarter of Fiscal Year 2017 – 18 April 1, 2018 through June 30, 2018

Fourth Quarter Highlights:

- Freeway Projects
- Streets and Roads
- Environmental Cleanup & Water Quality
- Freeway Mitigation Program
- Finance Matters
- Program Management Office
- Summary





#### MEASURE M2 PROGRESS REPORT

#### SUMMARY

On November 7, 2006, Orange County voters, by a margin of 69.7 percent, approved the renewal of the Measure M one-half cent sales tax for transportation improvements. Voters originally endorsed Measure M in 1990 with a sunset in 2011. The renewal of Measure M continues the investment of local tax dollars in Orange County's transportation infrastructure for another 30 years to 2041.

As required by the Measure M2 (M2) Ordinance No. 3, a quarterly report covering activities from April 1, 2018 through June 30, 2018 is provided to update progress in implementing the Measure M2 Transportation Investment Plan. On September 25, 2017, the Board of Directors (Board) approved externally rebranding M2 to OC Go to promote OCTA's Measure M awareness and public perception and to avoid confusion with Measure M in Los Angeles County.

To be cost effective and to facilitate accessibility and transparency of information available to stakeholders and the public, Measure M2 progress reports are presented on the Orange County Transportation Authority (OCTA) website. Hard copies are mailed upon request.



The cover photo is signage for the San Juan Capistrano Summer Trolley. OCTA awarded approximately \$6.8 million for six local agency projects in its third call for the Community-Based Transit Circulators Program (Project V). OCTA awarded the San Juan Capistrano Trolley funding to provide summer weekend and special event service.



TABLE OF CONTENTS		
Section	Project	Page
Abbreviations		i
Project Schedules		<u>iii</u>
M2 Delivery Risk Update		<u>1</u>
Next 10 Plan Update		<u>3</u>
Freeway Program (Projects A-N)		<u>7</u>
Interstate 5 (I-5) Projects	[A-D]	<u>7</u>
State Route 22 (SR-22) Projects	[E]	<u>11</u>
State Route 55 (SR-55) Projects	[F]	<u>11</u>
State Route 57 (SR-57) Projects	[G]	<u>12</u>
State Route 91 (SR-91) Projects	[H-J]	<u>13</u>
Interstate 405 (I-405) Projects	[K-L]	<u>16</u>
Interstate 605 (I-605) Projects	[M]	<u>17</u>
Freeway Service Patrol	[N]	<u>17</u>
Streets and Roads (Project O, P and Q)		<u>18</u>
Regional Capacity Program	[O]	<u>18</u>
Regional Traffic Signal Synchronization Program	[P]	<u>21</u>
Local Fair Share Program	[Q]	<u>21</u>
Transit Programs (Projects R, S, T, U, V and W)		<u>23</u>
High Frequency Metrolink Service	[R]	<u>23</u>
Transit Extensions to Metrolink	[S]	<u>27</u>
Metrolink Gateways	[T]	<u>28</u>
Expand Mobility Choices for Seniors and Persons with Disabilities	[U]	<u>29</u>
Community Based Transit/Circulators	[V]	<u>30</u>
Safe Transit Stops	[VV]	<u>31</u>
Environmental (Project X and Freeway Mitigation Program)		<u>32</u>
Environmental Cleanup	[X]	<u>32</u>
Freeway Mitigation Program (part of Projects A - M)		<u>33</u>
Program Management Office		<u>36</u>
M2 Financing and Schedule of Funding		<u>39</u>
Local Fair Share - M2 Funding by Agency		<u>47</u>
Capital Action Plan - Capital Project Status		<u>49</u>



Americans with Disabilities Act	ADA
Annual Eligibility Review	AER
Board of Directors	Board
Burlington Northern Santa Fe	BNSF
California Department of Fish and Wildlife	CDFW
California Department of Transportation	Caltrans
California Transportation Commission	CTC
Capital Action Plan	CAP
Capital Investment Grant	CIG
Chief Executive Officer	CEO
Cost Estimate Review	CER
Congestion Mitigation and Air Quality	CMAQ
Draft Environmental Document	DED
Draft Project Report	DPR
Environmental Cleanup Allocation Committee	ECAC
Environmental Cleanup Program	ECP
Environmental Document	ED
Environmental Impact Report	EIR
Environmental Impact Statement	EIS
Environmental Mitigation Program	EMP
Environmental Oversight Committee	EOC
Federal Highway Administration	FHWA
Federal Transit Administration	FTA
Federal Transportation Improvement Program	FTIP
Freeway Service Patrol	FSP
Full Funding Grant Agreement	FFGA
High Occupancy Vehicle	HOV
Interstate 15	I-15
Interstate 405	I-405
Interstate 5	I-5
Interstate 605	I-605
Invitation for Bids	IFB
Local Faire Share Program	LFSP
Los Angeles – San Diego – San Luis Obispo	LOSSAN
Los Angeles County Metropolitan Transportation Authority	LA Metro
Measure M2 or Renewed Measure M	M2
Memorandum of Understanding	MOU
Metrolink Service Expansion Program	MSEP

i



Notice to Proceed	NTP
Next 10 Delivery Plan	Next 10
Natural Community Conservation Plan/Habitat Conservation Plan	Conservation Plan
Orange County Transportation Authority	OCTA
Orange County Unified Transportation Trust	OCUTT
Pacific Coast Highway	PCH
Plans, Specifications and Estimates	PS&E
Program Management Office	PMO
Project Development Team	PDT
Project Study Report	PSR
Ready to List	RTL
Request for Proposals	RFP
Resource Management Plan	RMP
Right-of-Way	ROW
Riverside County Transportation Commission	RCTC
Santa Ana Regional Transportation Center	SARTC
Senate Bill 1	SB 1
Senior Mobility Program	SMP
Senior Non-Emergency Medical Transportation	SNEMT
Southern California Association of Governments	SCAG
State Route 133	SR-133
State Route 22	SR-22
State Route 241	SR-241
State Route 55	SR-55
State Route 57	SR-57
State Route 71	SR-71
State Route 74	SR-74
State Route 91	SR-91
State Transportation Improvement Program	STIP
State Water Resources Control Board	SWRCB
Southern California Regional Rail Authority	SCRRA
Taxpayer Oversight Committee	TOC














Construction



Conceptual

Environmental

Design, Advertise, & Award



Complete

		2013	2014	2015	2016	2017	20	18	2019	2020	2021	2022	2023	2024	2025
Α	I-5, SR-55 to SR-57														
В	I-5, I-405 to SR-55 (Further Schedule TBD)														
C,D	I-5, Avenida Pico to Avenida Vista Hermosa/Avenida Pico Interchange														
С	I-5, Avenida Vista Hermosa to Pacific Coast Highway (Complete)														
С	I-5, Pacific Coast Highway to San Juan Creek Road														
C,D	I-5, SR-73 to Oso Parkway/Avery Parkway Interchange														
C,D	I-5, Oso Parkway to Alicia Parkway/La Paz Road Interchange														
С	I-5, Alicia Parkway to El Toro Road														
D	I-5, El Toro Interchange (Further Schedule TBD)														
D	I-5, Ortega Interchange (Complete)														
Е	SR-22, Access Improvements (Complete)	Comple	eted in 2	008											
F	SR-55, I-405 to I-5														
F	SR-55, I-5 to SR-91 (Further Schedule TBD)														
G	SR-57 NB, Katella Avenue to Lincoln Avenue (Complete)														
G	SR-57 NB, Orangethorpe Avenue to Yorba Linda Boulevard (Complete)														
G	SR-57 NB, Yorba Linda Boulevard to Lambert Road (Complete)														
G	SR-57 NB, Lambert Road to Tonner Canyon Road (Further Schedule TBD)														
G	SR-57, Orangewood Avenue to Katella Avenue (Further Schedule TBD)														
н	SR-91 WB, I-5 to SR-57 (Complete)														
	SR-91 WB, SR-55 to Tustin Avenue Interchange (Complete)														
1	SR-91, SR-55 to SR-57 (Further Schedule TBD)														
J	SR-91, SR-55 to SR-241 (Complete)														
J	SR-91, SR-241 to SR-71 (Complete)	Comple	eted in 2	011											

Project schedules are based on phase start dates. Shown schedules are subject to change.

<sup>1</sup> Projects managed by local agencies



MEASURE M2 PROJECT SCHEDULES

J       SR-91, SR-241 to 1-15 (Further Schedule TBD)       Image: Complete display to the second display			2013	2014	2015	2016	2017	20	18	2019	2020	2021	2022	2023	2024	2025
I-405, SR-73 to I-605       Image: SR-75 to I																
L       1-405, I-5 to SR-55 (Further Schedule TBD)       Image: Complex of the schedule TBD)       Image: Complex of the schedule TBD)         M       I-605, Katella Interchange (Further Schedule TBD)       Image: Complex of the schedule TBD)       Image: Complex of the schedule TBD)         O       Kraemer Boulevard Grade Separation (Placentia)       Image: Complex of the schedule TBD)       Image: Complex of the schedule TBD)         O       Lakeview Avenue Grade Separation (Anaheim/ Placentia)       Image: Complex of the schedule TBD)       Image: Complex of the schedule TBD)         O       Crangethorpe Avenue Grade Separation (Anaheim/ Placentia)       Image: Complex of the schedule TBD)       Image: Complex of the schedule TBD)         O       Crangethorpe Avenue Grade Separation (Placentia)       Image: Complex of the schedule TBD)       Image: Complex of the schedule TBD)         O       Placentia Avenue Grade Separation (Fullerton) <sup>1</sup> Image: Complex of the schedule TBD)       Image: Complex of the schedule TBD)         O       Tustin Ave/Rose Drive Grade Separation (Irvine)       Image: Complex of the schedule TBD)       Image: Complex of the schedule TBD)       Image: Complex of the schedule TBD)         O       Tustin Ave/Rose Drive Grade Separation (Irvine)       Image: Complex of the schedule TBD)       Image: Complex of the schedule TBD)         R       Sand Canyon Grade Separation (Irvine)       Image: Complex of the schedule TBD)       Image: Complex of th	J	SR-91, SR-241 to I-15 (Further Schedule TBD)														
I-605, Katella Interchange (Further Schedule TBD)       Image: Construction of the second secon	K	I-405, SR-73 to I-605					////			////		////				
Image: TBD)       TBD)         O       Kraemer Boulevard Grade Separation (Placentia)         O       Lakeview Avenue Grade Separation (Anaheim/ Placentia)         O       Crangethorpe Avenue Grade Separation (Anaheim/Placentia)         O       Placentia Avenue Grade Separation (Placentia)         O       Raymond Avenue Grade Separation (Fullerton) <sup>1</sup> O       State College Blvd Grade Separation (Fullerton) <sup>1</sup> O       State College Blvd Grade Separation (Fullerton) <sup>1</sup> O       Tustin Ave/Rose Drive Grade Separation (Anaheim/Placentia)         R       Sand Canyon Grade Separation (Irvine)         R       Sand Canyon Grade Separation (Irvine)         R       San Clemente Beach Trail Safety Enhancements         San Clemente Beach Trail Safety Enhancements       Sand Canyon Metrolink Station Improvements         R       Fullerton Transportation Center Improvements       Sand Sate (ADA) Ramps         R       Crange Transportation Center Metrolink Parking Structure       Structure         Placentia Metrolink Station Improvements and       Sate Sate Sate Sate Sate Sate Sate Sate	L	I-405, I-5 to SR-55 (Further Schedule TBD)														
0       Lakeview Avenue Grade Separation (Anaheim/         0       Placentia)         0       Orangethorpe Avenue Grade Separation (Anaheim/Placentia)         0       Placentia Avenue Grade Separation (Placentia)         0       Placentia Avenue Grade Separation (Fullerton) <sup>1</sup> 0       Raymond Avenue Grade Separation (Fullerton) <sup>1</sup> 0       State College Blvd Grade Separation (Fullerton) <sup>1</sup> 0       State College Blvd Grade Separation (Fullerton) <sup>1</sup> 0       Tustin Ave/Rose Drive Grade Separation (Fullerton) <sup>1</sup> 0       Tustin Ave/Rose Drive Grade Separation (Irvine)         R       Sand Canyon Grade Separation (Irvine)         R       Sand Canyon Grade Crossing Safety         Completed in 2011       Interview         R       Anaheim Canyon Metrolink Station Improvements         R       Anaheim Canyon Metrolink Station Improvements         R       Laguna Niguel/Mission Viejo Metrolink Station Americans with Disabilities Act (ADA) Ramps         Orange Transportation Center Metrolink Parking       Interview         Placentia Metrolink Station Improvements and       Interview	М															
O Placentia)   O Orangethorpe Avenue Grade Separation (Anaheim/Placentia)   O Placentia Avenue Grade Separation (Placentia)   O Placentia Avenue Grade Separation (Fullerton) <sup>1</sup> O Raymond Avenue Grade Separation (Fullerton) <sup>1</sup> O State College Blvd Grade Separation (Fullerton) <sup>1</sup> O Tustin Ave/Rose Drive Grade Separation (Anaheim/Placentia)   O Tustin Ave/Rose Drive Grade Separation (Anaheim/Placentia)   R Sand Canyon Grade Separation (Irvine)   R Sand Canyon Grade Separation (Irvine)   R San Clemente Beach Trail Safety Enhancements   San Clemente Beach Trail Safety Enhancements   R Fullerton Transportation Center Improvements   R Laguna Niguel/Mission Viejo Metrolink Station Americans with Disabilities Act (ADA) Ramps   Orange Transportation Center Metrolink Parking Structure   P Placentia Metrolink Station Improvements and	0	Kraemer Boulevard Grade Separation (Placentia)														
O (Anaħeim/Placentia)   Placentia Avenue Grade Separation (Placentia)   O Raymond Avenue Grade Separation (Fullerton) <sup>1</sup> O State College Blvd Grade Separation (Fullerton) <sup>1</sup> O Tustin Ave/Rose Drive Grade Separation (Fullerton) <sup>1</sup> R Sand Canyon Grade Separation (Irvine)   R Sand Canyon Grade Crossing Safety   Enhancement Completed in 2011   R San Clemente Beach Trail Safety Enhancements   R Fullerton Transportation Center Improvements   R Laguna Niguel/Mission Viejo Metrolink Station Americans with Disabilities Act (ADA) Ramps   O Orange Transportation Center Metrolink Parking   Placentia Metrolink Station Improvements and	0															
Raymond Avenue Grade Separation (Fullerton) <sup>1</sup> State College Blvd Grade Separation (Fullerton) <sup>1</sup> Tustin Ave/Rose Drive Grade Separation (Fullerton) <sup>1</sup> Tustin Ave/Rose Drive Grade Separation (Anaheim/Placentia)   Rail-Highway Grade Crossing Safety   Enhancement   Rail-Highway Grade Crossing Safety   Completed in 2011   Rail-Highway Grade Crossing Safety   Enhancement   Rail-Highway Grade Crossing Safety   Completed in 2011   Rail-Highway	0	(Anaheim/Placentia)														
O State College Blvd Grade Separation (Fullerton) <sup>1</sup> O Tustin Ave/Rose Drive Grade Separation (Anaheim/Placentia)   R Sand Canyon Grade Separation (Irvine)   R Sand Canyon Grade Separation (Irvine)   R Rail-Highway Grade Crossing Safety Enhancement   R San Clemente Beach Trail Safety Enhancements   R Anaheim Canyon Metrolink Station Improvements   R Laguna Niguel/Mission Viejo Metrolink Station Americans with Disabilities Act (ADA) Ramps   P Placentia Metrolink Station Improvements and	0	Placentia Avenue Grade Separation (Placentia)														
O Tustin Ave/Rose Drive Grade Separation (Anaheim/Placentia)   R Sand Canyon Grade Separation (Irvine)   R Rail-Highway Grade Crossing Safety Enhancement   R San Clemente Beach Trail Safety Enhancements   R Anaheim Canyon Metrolink Station Improvements   R Laguna Niguel/Mission Viejo Metrolink Station Americans with Disabilities Act (ADA) Ramps   R Orange Transportation Center Metrolink Parking Structure	0	Raymond Avenue Grade Separation (Fullerton) <sup>1</sup>														
V (Anaheim/Placentia)   R Sand Canyon Grade Separation (Irvine)   R Rail-Highway Grade Crossing Safety Enhancement   R Rail-Highway Grade Crossing Safety Enhancement   R San Clemente Beach Trail Safety Enhancements   R Anaheim Canyon Metrolink Station Improvements   R Fullerton Transportation Center Improvements   R Laguna Niguel/Mission Viejo Metrolink Station Americans with Disabilities Act (ADA) Ramps   R Orange Transportation Center Metrolink Parking Structure   P Placentia Metrolink Station Improvements and	0	State College Blvd Grade Separation (Fullerton) <sup>1</sup>														
R   R   Rail-Highway Grade Crossing Safety   Enhancement   San Clemente Beach Trail Safety Enhancements   San Clemente Beach Trail Safety Enhancements   R   Anaheim Canyon Metrolink Station Improvements   Fullerton Transportation Center Improvements   R   Laguna Niguel/Mission Viejo Metrolink Station   R   Orange Transportation Center Metrolink Parking   Structure   Placentia Metrolink Station Improvements and	0															
R       Enhancement       Complete in 2011       Image: Complete in 2011         R       San Clemente Beach Trail Safety Enhancements       Image: Complete in 2011       Image: Complete in 2011         R       Anaheim Canyon Metrolink Station Improvements       Image: Complete in 2011       Image: Complete in 2011         R       Anaheim Canyon Metrolink Station Improvements       Image: Complete in 2011       Image: Complete in 2011         R       Anaheim Canyon Metrolink Station Improvements       Image: Complete in 2011       Image: Complete in 2011         R       Laguna Niguel/Mission Viejo Metrolink Station Americans with Disabilities Act (ADA) Ramps       Image: Complete in 2011       Image: Complete in 2011         R       Orange Transportation Center Metrolink Parking Structure       Image: Complete in 2011       Image: Complete in 2011         P       Placentia Metrolink Station Improvements and       Image: Complete in 2011       Image: Complete in 2011	R	Sand Canyon Grade Separation (Irvine)														
R       Anaheim Canyon Metrolink Station Improvements       Image: Constraint of the station improvements improvements       Image: Constraint of the station improvements improvements and       Image: Constraint of the station improvements and       <	R		Comple	eted in 2	011											
R       Fullerton Transportation Center Improvements       Image: Context improvements       Ima	R	San Clemente Beach Trail Safety Enhancements														
R       Laguna Niguel/Mission Viejo Metrolink Station Americans with Disabilities Act (ADA) Ramps       Image: Construction Center Metrolink Parking Structure       Image: Construction Center Metrolink Parking 	R	Anaheim Canyon Metrolink Station Improvements														
R       Orange Transportation Center Metrolink Parking       Image: Control of the second sec	R	Fullerton Transportation Center Improvements														
R  Structure    P  Placentia Metrolink Station Improvements and	R															
	R	Structure														
	R	Parking Structure														
R San Clemente Pier Station Lighting	R															
R Laguna Niguel to San Juan Capistrano Metrolink Station Passing Siding Project	R	Station Passing Siding Project														
R Tustin Metrolink Station Parking Structure Completed in 2011	R		Comple	eted in 2	011											
R,T Anaheim Regional Transportation Intermodal Center (ARTIC) <sup>1</sup>	R,T	Center (ARTIC) <sup>1</sup>														
S OC Streetcar	S	OC Streetcar														

Project schedules are based on phase start dates. Shown schedules are subject to change. <sup>1</sup>Projects managed by local agencies



### M2 DELIVERY RISK UPDATE 👻

This section discusses the risks and challenges related to Measure M2 and the 2018 update of the Next 10 Delivery Plan (Next 10) that the Measure M2 Program Management Office (PMO) is monitoring – complete with associated explanations and proposed actions.

	Delivery Risk	Explanation	Proposed Action					
Fina	ancial							
1	The 2018 M2 revenue forecast estimate is \$13.1 billion, which represents a 46 percent decrease in forecasted revenue since M2 adoption. If sales tax revenue continues to be lower than projections, this will further challenge delivery.	Sales tax revenue has been impacted by the recession and changes in consumer spending habits.	The 2018 lower forecast results in greater reliance on external funding to deliver the entire Freeway Program as listed. OCTA will continue to actively pursue available state and federal revenue, and work with the California Department of Transportation (Caltrans) to identify lower cost freeway alternative options for approval.					
2	Senate Bill 1 (SB 1) gas tax repeal (Prop 6) on November 6, 2018 ballot.	While M2 does not rely on gas tax funding, if Prop 6 passes and SB 1 is repealed, there is a likelihood that current state funding commitments in the State Transportation Improvement Program (STIP) for M2 projects would be impacted and could delay M2 freeway delivery schedules.	included a sensitivity run with lower external					
3	Inability to scale the Freeway Program to available revenue and still deliver the promise.	The freeway program includes set project scopes leaving very little flexibility in what is delivered.	-					
4	Delay in receipt of OC Streetcar Full Funding Grant Agreement (FFGA) from the Federal Transit Administration (FTA), could impact the overall delivery schedule.	While the FTA and the Orange County Congressional delegation continue to show strong support for the project, authorization for the New Starts FFGA remains outstanding.						





## MEASURE M2 PROGRESS REPORT

	Delivery Risk	Explanation	Proposed Action
5	Sustain Metrolink train service, as an attractive alternative to driving in Orange County with the limits of available revenue.	Operational cost of Metrolink service continues to grow as system ages, track-sharing arrangements with Burlington Northern Santa Fe Railway (BNSF) are revised, and new air quality requirements. These changes may impact service long term.	Staff will continue to work closely with Metrolink and our partners to ensure cost increases are minimized, while seeking external revenue.
6	The Next 10 Market Conditions Forecast and Risk Analysis identified strong potential for an increasing-cost environment during the Next 10 delivery years.	A construction cost pressure index model was created to provide insight on forecasting capital costs. The index tracks four near-term cost risks: economic trends (building permits and unemployment), material costs, wage pressures, and economic conditions.	OCTA will continue to monitor and track key early warning indicators as recommended and include a program level line item for an economic uncertainty allowance in the freeway cash flow. This is intended to safeguard the program and protect against over-committing during this time of uncertainty.
Org	anizational		
7	Availability of specialized staff, given the scope of the M2 capital program.	External demand for key talent is becoming more of an issue as large infrastructure programs move forward in the region. Timely completion of engineering and construction related support of the capital program is key to reduce project delivery risk.	Expert and timely coordination between OCTA and Caltrans are imperative to manage this risk. Staff is currently working with Caltrans to ensure resource needs are met. Internally OCTA's Human Resources Division continues to implement programs to retain and attract talent.
8	New operational responsibilities with the OC Streetcar.	With the implementation of the OC Streetcar service, OCTA will be increasing its overall role in operations. OCTA holds a strong track record in operating various transportation systems including both a fixed and demand-based bus network.	To ensure success of the OC Streetcar, OCTA hired a streetcar operations manager with proven start-up experience to oversee start-up and daily operations.
Poli	су		
9	New statewide directives create additional hurdles for the Freeway Program in particular.	New directives with greenhouse gas reductions and managed lane corridors focus, may impact approvals for four of the remaining freeway projects with general purpose lanes that are not yet environmentally cleared.	OCTA will work closely with Caltrans to ensure that when freeway improvement projects are reviewed the commitment to Orange County voters is understood.



2



### Next 10 Delivery Plan

Contact: Tami Warren, PMO Manager • (714) 560-5590

On November 14, 2016, the Board approved the Next 10 Delivery Plan (Next 10), providing guidance to staff on delivery of M2 projects and programs between 2017 and 2026. The Next 10 was updated to address and incorporate the 2018 sales tax revenue forecast of \$13.1 billion. The 2018 update of then Next 10 incorporates current revenue projections, bonding assumptions, project costs and schedule, and adjustments ensuring continued delivery of the complete M2 Program by 2041 as promised.

#### Next 10 Plan Deliverables

The Next 10 Plan is based on ten deliverables intended to provide guidance on program and project delivery during the ten-year period 2017 through 2026. With nearly two years of the ten-year plan complete, progress on the ten deliverables and accomplishments to date is provided. Significant progress has been made, with projects completing construction, projects in and advancing towards construction, as well as regular funding allocations to local jurisdictions through programs.

#### 1. Deliver \$3.5<sup>1</sup> billion of freeway improvements approved through construction (Projects A-M).

The M2 freeway program currently consists of 27 projects or project segments. At the point of Next 10 adoption in September 2016, nine projects were completed, and another nine were designated to be complete within the Next 10 time-frame. Together, the segments designated for completion by 2026 make up a \$3.1 billion delivery promise. Since Next 10 adoption, three segments of the Interstate 5 (I-5) between Avenida Vista Hermosa and San Juan Creek Road, opened to traffic in March 2018, adding six miles of carpool lanes. The remaining six segments are in design or construction. Funded with 91 Express Lanes excess revenues, a tenth project, the SR-91 between SR-57 to SR-55 (Project I) was designated a priority project and is now part of Deliverable 1 (planned to be complete by 2029). With this project, OCTA will deliver \$3.5 billion of freeway improvements approved through construction. For more details, see <u>pages iii-iv</u> (Project Schedules) and the project updates contained in the following pages.

## 2. Invest approximately \$715<sup>1</sup> million more in revenues, bringing the completed Freeway Program improvements to \$4.3 billion (Projects A-M).

The final eight remaining project segments (of the 27 total) are on track to be environmentally cleared by 2026, making them "shelf ready" for future advancement. In all, during the Next 10 time-period, approximately \$4.3 billion in freeway improvements promised to the voters in M2 will be completed or underway by 2026. Using the guiding principles adopted by the Board, Deliverable 2 includes approximately \$715 million in funding to move another project (or projects) directly into design and construction if assumptions on revenues and costs hold. For more details, see <u>pages iii-iv</u> (Project Schedules) and the project updates contained in the following pages.

<sup>1</sup> Because Project I is now included with Deliverable 1, the original Deliverable 1 investment increased to \$3.5 billion, and the original Deliverable 2 investment of \$1.2 billion has been reduced to \$715 million. The overall freeway deliverable commitment remains the same at \$4.3 billion.



3. Allocate \$1 billion, with \$400 million in competitive funding to local jurisdictions to expand roadway capacity and synchronize signals (Project O and P) and \$600 million in flexible funding to local jurisdictions to help maintain aging streets or for use on other transportation needs, as appropriate (Project Q).

All seven bridges included in the OC Bridges program are complete. Since the adoption of the Next 10 Plan in November 2016, OCTA awarded approximately \$82 million in competitive funding through the Regional Capacity Program (Project O) and Regional Traffic Signal Synchronization Program (Project P). Additionally, \$98.1 million in Local Fair Share (Project Q) funds have been distributed to local agencies. This brings the total allocation to date to \$180.1 million. On August 13, 2018, the Board approved the release of the 2019 Call for Projects for approximately \$32 million for Project O and \$8 million for Project P and funding recommendations will be presented to the Board by mid-2019. For more details, see the project updates on <u>page 18</u>.

## 4. Extend Metrolink service from Orange County into Los Angeles County, contingent upon cooperation and funding participation from route partners; complete six rail station improvements (Project R).

The Southern California Regional Rail Authority (SCRRA) continues to work on behalf of its members, the Riverside County Transportation Commission (RCTC), Los Angeles County Metropolitan Transportation Authority (LA Metro), and OCTA, to negotiate an agreement with the Burlington Northern Santa Fe (BNSF) Railway for the shared used of their corridor and associated indemnification and liability. This agreement is necessary to secure additional operating slots in order to provide additional passenger rail service on railroad ROW owned by the BNSF. Special counsel has been brought in to assist in these negotiations.

Within this program, funding is provided for rail corridor and station improvements to accommodate increased passenger train service - including station upgrades, parking expansions, and safety enhancements. The Next 10 Plan identifies six projects to be completed by 2026, status shown below. For more details, see the project updates on <u>page 24</u>.

# 5. Complete design and construction, secure vehicles, and begin operating the OC Streetcar (Project S) and work with local agencies to consider recommendations from planning studies to guide development of future transit connections (Project S).

#### OC Streetcar

Activities continue to move forward, including final possession of remaining required ROW, procurement of demolition services, coordination with third parties on utility relocation, finalizing the California Public Utilities Commission safety approvals for the OC Streetcar's grade crossings certification, finalizing the scope of services for the operations and maintenance request for proposals, and continued coordination with the FTA on the status of the FFGA. The streetcar vehicle manufacturing contract has been executed and the notice to proceed has been issued.

The FTA continues to show strong support for the project, and a FFGA is anticipated in 2018. See <u>page 27</u> for more information.

#### Harbor Corridor Transit Study

A final staff report was presented to the OCTA Transit Committee on June 14, 2018 and to the Board on



June 25, 2018. Based on the comments received from the participating cities, service speed and amenity improvements (including off-board fare collection, all-door boarding, transit signal priority, and queue jumps) were identified for the existing bus routes on Harbor Boulevard, with implementation dates to be determined in the near future.

#### OC Transit Vision

The draft Transit Master Plan was presented to the Board in February 2018. The plan included an action plan which was divided into short, medium and long-term recommendations. The Board directed staff to consider the plan in the upcoming Long-Range Transportation Plan process. Staff will be advancing many of the short-term action plan items over the next year.

## 6. Provide up to \$115 million in funding to expand mobility choices for seniors and persons with disabilities (Project U).

Approximately \$20.2 million has been provided for the Senior Mobility Program (SMP), the Senior Non-Emergency Medical Transportation Program (SNEMT), and the Fare Stabilization Program since the Next 10 Plan adoption. See <u>page 29</u> for more information.

## 7. Work with local agencies to develop a plan for the next community circulator projects to provide grant opportunities for local agencies to implement effective local transit services (Project V).

In December 2017, OCTA staff requested letters from local agencies to determine interest for a future round of Project V funding. OCTA received 13 letters of interest and in February 2018, the Board initiated a 2018 Project V Call for Projects. On June 25, 2018 the Board awarded \$6.8 million to fund six Community-Based Transit Circulators Projects. For additional details and information on current project program performance and service see <u>page 30</u>.

## 8. Allocate up to \$7 million in funding to improve the top 100 busiest bus stops and support the modernization of the bus system to enhance the customer experience (Project W).

To date, the Board has approved up to \$1.2 million to support 51 city-initiated improvements and \$370,000 for OCTA initiated improvements. The City of Anaheim postponed development of eight stops and will move forward in a future funding cycle. Of the remaining 43 stops, 14 stops have been completed and the remaining 29 stops are in the project closeout process. Closeout of all projects is anticipated next quarter. OCTA initiated improvements were originally programmed to support the "Text for Next" program. However, these funds were ultimately reallocated (in 2015) to support OCTA's mobile ticketing application (app) development. A meeting is scheduled with local agencies on August 17, 2018, to gage interest and need for the next cycle of Project W funding. For additional details see <u>page 31</u>.

# 9. Ensure the ongoing preservation of purchased open space (Preserves) which provides comprehensive mitigation of the environmental impacts of freeway improvements and higher-value environmental benefits in exchange for streamlined project approvals (Projects A-M).

The Freeway Mitigation Program Preserves includes seven properties (1,300 acres), and 12 restoration projects (350 acres). TIn 2017, OCTA received biological resource permits after completing a state and federal Natural Community Conservation Plan/Habitat Conservation Plan (Conservation Plan) for the Environmental



Mitigation Program (EMP), allowing streamlined project approvals for the freeway improvement projects. The Conservation Plan also includes a streamlined process for coordination for streambed alternation agreements. In January 2018, the OCTA secured programmatic permits and assurances for federal and state clean water permitting requirements. Receipt of these permits represent the culmination of years of collaboration and support by the Board, environmental community, and regulatory agencies.

To ensure ongoing preservation of the open space, an endowment was established to pay for the long-term management of the Preserves. The second deposit into the endowment was made in August 2017, and approximately \$2.9 million on will be deposited an annual basis. For more details, see the project updates on page 32.

10. Work with the Environmental Cleanup Allocation Committee (ECAC) to develop the next tiers of water quality programs, with a goal of providing \$40 million in grants to prevent the flow of trash, pollutants, and debris into waterways from transportation facilities. In addition, focus on improving water quality on a regional scale that encourages partnerships among the local agencies as part of the Environmental Cleanup Program (ECP) (Project X).

Since adoption of the Next 10 Plan in November 2016, OCTA issued two calls for Tier 1 ECP projects. The Board awarded approximately \$5.59 million to fund 28 Tier 1 projects. Staff is working with the ECAC and the County of Orange to determine the best timing for the next Tier 2 call based on projected cash flow and local jurisdictions' interest in potential viable Tier 2 projects. For more details, see the project updates on page 33.



## INTERSTATE 5 (I-5) PROJECTS -

Segment: I-5, Between SR-55 and SR-57

Status: Design complete. Construction package advertised for bids.

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project will increase high occupancy vehicle (HOV) capacity by adding a second HOV lane in both directions along I-5 between SR-55 and SR-57 in Santa Ana. Last quarter, the project received federal authorization (E-76) allowing it to be advertised for construction. The project was advertised for bids on March 19th with Bid Opening held on May 8th. However, the three Lowest Bidders were deemed "unresponsive" as each did not meet the bidding requirements. Additionally, after the quarter ended, the remaining five bidders pulled out due to concerns over guaranteeing their low bids. Due to changes in scope, the replacement of STIP funds with Congestion Mitigation and Air Quality (CMAQ) funds, and the need to re-advertise for construction bids, this project is marked "red" in the Capital Action Plan (CAP) signifying a delay of over three months beyond the original schedule. Construction is expected to begin in late-2018.

#### Segment: I-5, I-405 to SR-55

Status: Environmental Phase Underway - 89% Complete

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project will add one general purpose lane in each direction of the I-5 corridor and improve interchanges in the area between SR-55 and SR-133 (near the El Toro "Y" and I-405) in Tustin and Irvine. The environmental study will consider the addition of one general purpose lane on I-5 between just north of I-405 to SR-55. Additional features of Project B include the addition of auxiliary lanes in some areas and re-established in other areas within the project limits. During the quarter, the consultant continued working on the Draft Environmental Document (DED) and the Draft Project Report (DPR), and obtained Caltrans approval. To limit community impacts, this project will require the preparation of a Fact Sheet to address design variations due to tight ROW constraints and the Fact Sheet process is in progress. The DED was circulated from mid-May and held two open house format public hearings in late May. The final ED is expected to be complete in early 2019. This project is marked "red" in the CAP, signifying a delay of over three months beyond the original schedule. As part of the 2018 STIP process, based on congestion considerations and project readiness status, OCTA pursued funding for the design phase of this project. On March 21, 2018, the California Transportation Commission (CTC) approved \$12.628 million for design phase work of this project in Fiscal Year 2022-23. This is the first STIP cycle in more than ten years which allowed advancement of future STIP cycle funds to be used for pre-construction activities, enabled due to the passage of SB 1.

PROJECT A

**PROJECT B** 



## I-5, Avenida Pico to San Juan Creek Road is one project broken into three segments, as described below.

#### Segment: I-5, Avenida Pico to Avenida Vista Hermosa/Avenida Pico Interchange

Status: Construction Underway - 99% Complete

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This segment added a carpool lane in each direction on I-5 between Avenida Pico and Avenida Vista Hermosa in San Clemente, and included major improvements through reconstruction of the Avenida Pico Interchange (part of Project D). The project also includes the addition of bicycle lanes in both directions of Avenida Pico. Construction began in February 2015. Construction of the carpool lanes were completed and all three segments of the I-5 between Avenida Pico to San Juan Creek were opened to traffic on March 13, 2018. During the quarter, the contractor worked on the punchlist items with the goal to reach relief of maintenance in July 2018.

#### Segment: I-5, Avenida Vista Hermosa to Pacific Coast Highway

Status: PROJECT COMPLETE



PART OF PROJECT D

Contact: Rose Casey, Capital Projects • (714) 560-5729


**Summary:** This segment added a carpool lane in each direction of I-5 between Avenida Vista Hermosa and Pacific Coast Highway (PCH) in San Clemente, and also reconstructed on and off ramps at Avenida Vista Hermosa and Camino de Estrella. Construction began in September 2014 and relief of maintenance was obtained in July 2017 signifying completion. Construction of the carpool lanes were completed and all three segments of the I-5 between Avenida Pico to San Juan Creek were opened to traffic on March 13, 2018. The one-year plant establishment period is ongoing until July 2018.

#### Segment: I-5, Pacific Coast Highway to San Juan Creek Road

Status: Construction Underway - 99% Complete

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This segment added one carpool lane in each direction of the I-5 between PCH and San Juan Creek Road in the Cities of San Clemente, Dana Point, and San Juan Capistrano. Project improvements also reconstructed on and off ramps at PCH/Camino Las Ramblas. Construction began in March 2014. Construction of the carpool lanes were completed and all three segments of the I-5 between Avenida Pico to San Juan Creek were opened to traffic on March 13, 2018. During the quarter, the contractor worked on punchlist items with the goal to reach relief of maintenance in July 2018.



I-5, SR-73 to El Toro Road is one project broken into three segments, as described below. The OCTA cost estimate for this project is \$557.11 million, which is above the \$500 million threshold for a "Major Project" designation, as determined by the Federal Highway Administration (FHWA). Major projects require a Cost Estimate Review (CER) workshop, and a CER was conducted by the FHWA, Caltrans, and OCTA in February 2018. The CER estimates that the project may require additional funding up to \$55.75 million. While OCTA estimates indicate the project funding need may be lower, FHWA requirements necessitates that OCTA demonstrate sufficient funding. In June, the Board authorized an increase of \$55.75 million to the project, increasing support costs up to \$612.86 million. The segment from Oso Parkway to Alicia Parkway is scheduled for advertisement for construction bids in August 2018. Cost estimates for the other segments of the I-5 Improvement Project, which are scheduled for advertisement next year, will be revisited after Segment 2 construction bid opening.

#### Segment: I-5, SR-73 and Oso Parkway/Avery Parkway Interchange

Status: Design Phase Underway - 95% Complete

Contact: Rose Casey, Capital Projects • (714) 560-5729


**Summary:** This project will make improvements along I-5 between SR-73 and Oso Parkway in the Cities of Laguna Hills, Laguna Niguel, and Mission Viejo. The proposed improvements include the addition of a generalpurpose lane in each direction and reconstruction of the Avery Parkway Interchange (part of Project D). During the quarter, the consultant continued working on ROW appraisals and coordinated with utility agencies. Staff continued to coordinate with Caltrans to finalize and approve the required Fact Sheet. It is anticipated that the 100 percent Plans, Specifications, and Estimates (PS&E) will be submitted to Caltrans on August 1, 2018. The plans identify a higher cost estimate due to unit price increases, rise in Caltrans support costs, and schedule changes to address bird nesting season restrictions. Due to extended ROW coordination, this project is marked "red" in the CAP, signifying a delay. On March 21, 2018, the CTC approved the 2018 STIP update and programmed approximately \$31.166 million over Orange County's share target. To maintain CTC funding limits in the next few years, STIP funding in this project was replaced with M2 funds and a small portion of the STIP funds were programmed for the future landscaping project. This is the first STIP cycle in more than ten years which allowed advancement of future STIP cycle funds to be used for pre-construction activities, enabled due to the passage of SB 1.

#### Segment: I-5, Oso Parkway to Alicia Parkway/La Paz Road Interchange

Status: Design Complete. Construction bid package preparation underway.

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project will make improvements along I-5 between Oso Parkway and Alicia Parkway in the Cities of Mission Viejo, Laguna Hills, and Lake Forest. The proposed improvements include the addition of a general-purpose lane in each direction and reconstruction of the La Paz Road Interchange (Part of Project D).



Major activities this quarter included Certification of the ROW phase and achieving Ready-to-List (RTL) status. Staff also continued coordination of the service contract with SCRRA/Metrolink, and with Caltrans on ROW and utilities. OCTA and Caltrans are preparing the Draft Financial Plan and Draft Project Management Plan, in accordance with the FHWA's "Major Project" Guidance. The consultant continues to coordinate with three regulatory agencies to ensure all permits will be in place ahead of Advertisement, which is now scheduled for October 2018. Due to extended ROW coordination, this project is marked "red" in the CAP, signifying a delay of over three months beyond the original schedule. This project is anticipated to begin construction in early 2019.

#### Segment: I-5, Alicia Parkway to El Toro Road

Status: Design Phase Underway - 95% Complete

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project will make improvements along I-5 between Alicia Parkway to El Toro Road in the Cities of Lake Forest, Laguna Hills, Laguna Woods and Mission Viejo, including the extension of the second HOV lane from El Toro Road to Alicia Parkway. Major activities this quarter included continued coordination with Caltrans, Orange County Parks and Orange County Flood Control regarding the planned work at Aliso Creek. Further coordination with the Army Corps of Engineers and the State Department of Fish and Wildlife. In this quarter the Design consultant received the second round of comments from Caltrans regarding the final ROW mapping, (previously submitted in April 2018). Due to extended ROW coordination with Caltrans and delayed design start date, this project is marked "red" in the CAP, signifying a delay of over three months beyond the original schedule. The 100 percent Design Submittal is now anticipated for April 2019. On March 21, 2018, the CTC approved the 2018 STIP update and programmed approximately \$31.166 million over Orange County's share target. STIP funds increased from \$58.911 million to \$69.111 million for this segment, but the segment is programmed in the STIP three years later than requested. Staff will work with the CTC staff and Caltrans to seek methods to maintain the existing schedule. This is the first STIP cycle in more than ten years which allowed advancement of future STIP cycle funds to be used for pre-construction activities, enabled due to the passage of SB 1.

PROJECT D

This project will update and improve key I-5 interchanges at Avenida Pico, Ortega Highway, Avery Parkway, La Paz, and at El Toro Road. Three interchange improvements at La Paz, Avery Parkway, and Avenida Pico are part of Project C.

Segment:	I-5, El	Toro Interchange
----------	---------	------------------

Status: Environmental Phase Underway - 30% Complete

Contact: Rose Casey, Capital Projects • (714) 560-5729

Summary: This project includes four build alternatives that consider modifications to the existing interchange, 10



which range from a I-5 southbound direct connector to El Toro Road to modifications in how existing off ramp intersections operate. Work began in May 2017. Work during the quarter included completion of traffic studies for each of the four build Alternatives. The Value Analysis Final Report was sent to all attendees in February 2018. Caltrans provided an update to the OCTA Board in March 2018 and is scheduled to provide the next update in October. A Public Scoping Meeting is scheduled for July 25th in Laguna Woods City Hall. The environmental phase is anticipated to be completed in late 2019.

#### Segment: I-5, Ortega Highway Interchange

Status: PROJECT COMPLETE

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** Construction began in February 2013 to reconstruct the SR-74 Ortega Highway Bridge over I-5, and improve local traffic flow along SR-74 and Del Obispo Street in the City of San Juan Capistrano. All lanes on the new bridge were opened to traffic on September 4, 2015. A dedication ceremony was held on October 1, 2015. The project was officially completed on January 15, 2016.

## STATE ROUTE 22 (SR-22) PROJECTS -

Segment: SR-22 Access Improvements

Status: PROJECT COMPLETE

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** Completed in 2008, Project E made improvements at three key SR-22 interchanges (Brookhurst Street, Euclid Street, and Harbor Boulevard) in the City of Garden Grove to reduce freeway and street congestion in the area. This M2 project was completed early as a "bonus project" provided by the original Measure M (M1).

## STATE ROUTE 55 (SR-55) PROJECTS -

Segment: SR-55, I-405 to I-5

Status: Design Phase Underway - 30% Complete

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project will widen SR-55 in the Cities of Irvine, Santa Ana, and Tustin. Through a cooperative agreement, Caltrans completed a portion of the 35 percent design work in May 2018 and is responsible for developing and seeking approval of the required Fact Sheet addressing necessary design variations on the project. The Supplemental Fact Sheet was initiated in June 2018. OCTA consultant was also involved in the delivery of the 35 percent design work in cooperation with Caltrans. The ROW cooperative agreement between





**PROJECT F** 



OCTA and Caltrans was executed in June 2018. ROW and utility coordination have been initiated and are ongoing. The project is anticipated to be ROW Certified and RTL in December 2020. On March 21, 2018, the CTC approved the 2018 STIP update and programmed approximately \$31.166 million over Orange County's share target. OCTA received \$12.628 million for this segment, however the segment is currently programmed in the STIP one year later than requested. This is the first STIP cycle in more than ten years which allowed advancement of future STIP cycle funds to be used for pre-construction activities, enabled due to the passage of SB 1. Staff will work with the CTC staff and Caltrans to seek methods to maintain the existing schedule.

#### Segment: SR-55, I-5 to SR-91

Status: Environmental Phase Underway - 49% Complete

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project will study SR-55 between I-5 and SR-91 in the Cities of Santa Ana, Tustin, Orange and Anaheim. The environmental study will consider the addition of one general purpose lane in each direction between SR-22 and the I-5, and provide operational improvements between SR-22 and SR-91. During the quarter, the consultant continued working on technical studies and obtained approval on a number of technical studies. The environmental phase is anticipated to be complete in early 2020.

## STATE ROUTE 57 (SR-57) PROJECTS -

Segment: SR-57 Northbound, Katella to Lincoln Avenue



Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project increased capacity and improved operations on northbound SR-57 between Katella Avenue and Lincoln Avenue in the City of Anaheim with the addition of a new 3-mile general purpose lane, onand off-ramp improvements, and sound walls. Bridges at Katella Avenue and Douglas Road were also widened in the northbound direction. The project opened to traffic on November 19, 2014 and completed on April 21, 2015.

#### Segment: SR-57 Northbound, Orangethorpe to Yorba Linda Boulevard

#### Status: PROJECT COMPLETE

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project increased capacity and improved operations on northbound SR-57 with a new 2.5mile northbound general-purpose lane between Orangethorpe Avenue in the City of Placentia to Yorba Linda Boulevard in the City of Fullerton. In addition to the new lane, capital improvements include reconstruction of northbound on- and off-ramps, widening of seven bridges, and the addition of soundwalls. The new general purpose lane was opened to traffic on April 28, 2014. The project was completed on November 6, 2014.



**PROJECT G** 



#### Segment: SR-57 Northbound, Yorba Linda Boulevard to Lambert Road

#### Status: PROJECT COMPLETE

Contact: Rose Casey, Capital Projects • (714) 560-5729



**Summary:** Completed on May 2, 2014, this project improved capacity, operations, and traffic flow on SR-57 with the addition of a new 2.5-mile northbound general-purpose lane between Yorba Linda Boulevard in the City of Fullerton and Lambert Road in the City of Brea. Additional project benefits include on- and off-ramp improvements, the widening and seismic retrofit (as required) of six bridges in the northbound direction and the addition of soundwalls. Existing lanes and shoulders were also widened to standard widths, enhancing safety for motorists. The new general purpose lane was opened to traffic on September 23, 2013. The project was completed on May 2, 2014.

#### Segment: SR-57 Northbound, Lambert Road to Tonner Canyon Road

Status: Environmental phase expected to begin in mid-2020

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** Caltrans previously completed a Project Study Report (PSR)/Project Development Support document for the Lambert Road to Tonner Canyon Road segment, which would add a truck-climbing lane from Lambert Road to Tonner Canyon Road in the City of Brea. The mainline project includes interchange and ramp improvements at Lambert Road. Through the SB 1 Trade Corridor Enhancement Program, funds were allocated to initiate the environmental phase for interchange improvements at Lambert Road which will complement and serve as a first phase to the freeway improvement project. Phase 2, which is the mainline improvements, was approved for STIP funding in March 2018 to initiate the environmental phase to study the truck-climbing lanes in mid-2020. This project will coordinate with and take into consideration any related work by LA Metro across the county line.

#### Segment: SR-57 Northbound, Orangewood Avenue to Katella Avenue

Status: Environmental Phase Underway - 60% Complete

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project studies the addition of capacity in the northbound direction of SR-57 from Orangewood Avenue to Katella Avenue in the Cities of Anaheim and Orange. Improvements under study include adding a northbound general-purpose lane to join the northbound general purpose lane which was opened to traffic in 2014 between Katella Avenue and Lincoln Avenue. During the quarter, most of the technical reports were approved, with only two outstanding. The consultant also completed the ROW Data Sheets for all three Build Alternatives. In the next quarter, the consultant will submit the DPR and DED to OCTA and Caltrans for administrative review. The environmental phase is anticipated to be complete in early 2019. This project is marked "yellow" in the CAP, signifying a delay of one month beyond the original schedule.



## STATE ROUTE 91 (SR-91) PROJECTS -

Segment: SR-91 Westbound, I-5 to SR-57

Status: PROJECT COMPLETE

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project increased capacity in the westbound direction of SR-91 by adding an additional general purpose lane in the westbound direction between Anaheim and Fullerton, and provided operational improvements at on and off-ramps between Brookhurst Street and State College Boulevard. The general purpose lane was opened to traffic on March 7, 2016. Construction is 100 percent complete, as of June 23, 2016.

#### Segment: SR-91, SR-55 to Tustin Avenue Interchange

Status: PROJECT COMPLETE



**Summary:** This project improved traffic flow at the SR-55/SR-91 interchange by adding a westbound auxiliary lane beginning at the northbound SR-55 to westbound SR-91 connector through the Tustin Avenue interchange in the City of Anaheim. The project was intended to relieve weaving congestion in the area and included reconstruction of the westbound side of the Santa Ana River Bridge to accommodate the additional lane. The bypass lane was open to traffic on May 14, 2016. Construction completed on July 15, 2016 and Contract Acceptance was granted on October 31, 2016.

#### Segment: SR-91, SR-55 to SR-57

Status: Environmental Phase Underway - 72% Complete

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project will improve traffic flow and operations along SR-91 within the Cities of Fullerton and Anaheim. The study will look at the addition of one general purpose lane eastbound between SR-57 and SR-55, and one general purpose lane westbound from the NB SR-57 connector to State College Boulevard. Additional features of this project include improvements to various interchanges. Auxiliary lanes will be added in some segments and re-established in others within the project limits. This quarter, the consultant continued working on the environmental and engineering technical studies. Due to Caltrans requiring extra work to study interchange improvements outside of the completed PSR and the M2 promised project, the project is marked "red" in the CAP with a delay of 10 months from its original schedule. SR-91 Express Lanes excess revenue is designated to pay for the mainline freeway improvements included in M2. This project is anticipated to proceed into design shortly following the completion of this study. The environmental study is expected to be complete in mid-2019.



**PROJECT I** 

**PROJECT H** 



#### Segment: SR-91, SR-55 to SR-241

Status: PROJECT COMPLETE

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This completed Project J segment added six miles in the westbound and eastbound direction to a key stretch of SR-91 between SR-55 and SR-241 in the Cities of Anaheim and Yorba Linda. In addition to adding 12 lane miles to SR-91, the project also delivered a much needed second eastbound exit lane at the Lakeview Avenue, Imperial Highway and Yorba Linda Boulevard/Weir Canyon Road off-ramps. Beyond these capital improvements, crews completed work on safety barriers, lane striping and soundwalls. Completion of this project in March 2013 means a total of 18 lane miles have been added to SR-91 since December 2010. The lanes opened to traffic in December 2012, and construction completed on March 5, 2013.

#### Segment: SR-91, SR-241 to SR-71

Status: PROJECT COMPLETE



**Summary:** Completed in January 2011, this segment added six miles through a key stretch of SR-91 between Orange County's SR-241 and Riverside County's SR-71. The project improves mobility and operations by reducing traffic weaving from traffic exiting at SR-71 and Green River Road. An additional eastbound general purpose lane on SR-91 was added and all existing eastbound lanes and shoulders were widened. The new facilities were opened to traffic on December 2, 2010 and construction completed January 31, 2011. Because this project was shovel-ready, OCTA was able to obtain American Recovery and Reinvestment Act funding for this M2 project, saving M2 revenues for future projects.

#### Segment: SR-91, SR-241 to I-15

Status: RCTC's Design-Build - Initial Phase Complete March 20, 2017

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** The purpose of this project is to extend the 91 Express Lanes eastward from its current terminus in Anaheim to I-15 in Riverside County. This project will also add one general purpose lane in each direction of SR-91, from SR-71 to I-15, and construct various interchange and operational improvements. On March 20, 2017, the RCTC contractors completed the \$1.3 billion initial phase freeway improvement project which extended the 91 Express Lanes from Orange County to I-15 in Riverside County, added a general-purpose lane east of SR-71 to I-15, and provided tolled express connectors between SR-91 and I-15. While the portion of this project between SR-241 and the Orange County/Riverside County line is part of OCTA's M2 Project J, the matching segment between the county line and SR-71 is part of RCTC's Measure A. The ultimate project widens all SR-91 general purpose lanes to standard lane and shoulder widths from SR-241 to SR-71 (RCTC is responsible for the lane improvements between Green River and SR-71 while OCTA will be responsible for the lane improvements







PROJECT J



west of Green River to SR-241). To maintain synchronization, these general-purpose lanes improvements, which span both counties, will be scheduled to ensure coordinated delivery of both portions of the project, and will provide a continuous segment that stretches from SR-241 to SR-71. Construction of the final additional general-purpose lane between SR-241 and SR-71 will take place post-2035. This action is consistent with the 2018 SR-91 Implementation Plan.

### INTERSTATE 405 (I-405) PROJECTS -

Segment: I-405, SR-73 to I-605

Status: Design-Build Underway

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** OCTA and Caltrans are working together to widen I-405 through the Cities of Costa Mesa, Fountain Valley, Garden Grove, Huntington Beach, Los Alamitos, Seal Beach, and Westminster. These improvements will add one general purpose lane, add a second lane to be combined with the existing HOV lane to provide a dual express lanes facility, and improve the local interchanges along the corridor from SR-73 to I-605.\*

During the quarter, work continued on ROW acquisition, utility coordination, environmental permitting, final baseline schedule, and public outreach. Other work includes review of design-builder submittals including design submittals, transportation management plan and other administrative plans necessary to be completed prior to commencement of significant construction. On April 9, 2018, staff provided the Board an update on the project. The update included that construction began on March 6, 2018 and the Contractor will continue to ramp up construction activities through the end of the year. Additionally, pursuant to our Transportation Infrastructure Finance and Innovation Act (TIFIA) loan agreement, we submitted our first reimbursement request for \$165 million and received that amount on April 16, 2018. Lastly, OCTA held six open houses along the corridor in May and June of 2018 to discuss the initiation of construction with the communities adjacent to I-405. Construction is scheduled to be completed in 2023.

\* The general purpose lane portion of the project is a M2 project and will be funded by a combination of local, state and federal funds, with the express lanes portion of the project financed and primarily paid for by those who choose to pay a toll and use the 405 Express Lanes.

#### Segment: I-405, I-5 to SR-55

Status: Environmental Phase Underway - 97% Complete

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project is studying the addition of general purpose lanes on the I-405 corridor between I-5 and SR-55 in Irvine. Additional features of the project include improvements to various interchanges, auxiliary lanes

**PROJECT K** 

**PROJECT L** 



and ramps. During the quarter, the consultant continue to work on the draft final Project Report (PR) and draft final Environmental Document (ED). The final PR and ED are expected to be complete in August 2018. This project is marked "yellow" in the CAP, signifying a delay of one month beyond the original schedule.

### INTERSTATE 605 (I-605) PROJECTS -

#### Segment: I-605, Katella Interchange Improvements

Status: Environmental Phase Underway - 4% Complete

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** This project will improve freeway access and the arterial connection to I-605 at Katella Avenue in the City of Los Alamitos and the County of Orange. Improvements under this project may include enhancements at the on-ramps and off-ramps in addition to operational improvements on Katella Avenue at the I-605 Interchange. The remaining two build alternatives include modification of interchange ramps and lane configurations on Katella Avenue from Coyote Creek Channel to Civic Center Drive. During the quarter, the consultant obtained approval on the DED and the DPR. The DED was circulated in mid-April and held an open house format public hearing in late April. The final ED is anticipated to be completed in November 2018.

## FREEWAY SERVICE PATROL -

Status: Service Ongoing

Contact: Cliff Thorne • (714) 560-5975

**Summary:** M2's Freeway Service Patrol (FSP) began operation in June 2012 and provides tow truck service for motorists with disabled vehicles on the freeway system to help quickly clear freeway lanes and minimize congestion. During the quarter, the midday service provided assistance to 1186 motorists and weekend service provided assistance to 827 motorists. There was no construction service provided this quarter, but service is expected to resume next quarter. Since inception, M2 and construction-funded FSP has provided a total of 69,265 assists to motorists on the Orange County freeway system.

PROJECT M

PROJECT N



## REGIONAL CAPACITY PROGRAM -

Status: 2018 Call for Projects in Progress

Contact: Joseph Alcock, Planning • (714) 560-5372

**Summary:** This program, in combination with required local matching funds, provides funding for improvements on Orange County's Master Plan of Arterial Highways. Since 2011, 146 projects totaling more than \$295 million, including \$24 million in external funding, have been awarded through eight calls for projects by the Board. On August 6, 2018, OCTA staff will seek Board approval for the release of the 2019 Call for Projects which, if approved, will make approximately \$32 million available to fund additional road improvements throughout the County.

#### **OC Bridges Railroad Program**

This program built seven grade separations (either under or over passes) where high volume streets are impacted by freight trains along the BNSF Railroad in North County. A status for each of the seven projects is included below. As of the end of this quarter, six are complete (Kraemer, Placentia, Orangethorpe, Tustin/Rose, Lakeview, and State College), and the remaining Raymond project is scheduled to be completed in summer 2018. With all seven grade separations open to traffic in late 2017, an OC Bridges completion ceremony was held on October 24, 2017. To date, the Board has approved approximately \$664 million in committed M2 and external funds for all seven of the OC Bridges Program grade separation projects. Minor activities this quarter include completion of punch list items and close out of projects.

#### Segment: Kramer Boulevard Grade Separation

Status: PROJECT COMPLETE

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** The project located at Kraemer Boulevard railroad crossing is grade separated and open to traffic. The project separated the local street from railroad tracks in the City of Placentia by building an underpass for vehicular traffic. The grade separation was opened to traffic on June 28, 2014, and an event was held on July 8, 2014 to commemorate the opening. Project acceptance by the Cities of Anaheim and of Placentia, respectively, occurred in December 2014 and the cities assumed full maintenance responsibilities. In December 2015, the one-year warranty period expired with no issues or repairs identified.

**PROJECT O** 



#### Segment: Lakeview Avenue Grade Separation

Status: PROJECT COMPLETE

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** The project located at Lakeview Avenue railroad crossing grade separated the local street from railroad tracks in the Cities of Anaheim and Placentia by building a bridge for vehicular traffic over the railroad crossing and reconfiguring the intersection of Lakeview Avenue and Orangethorpe Avenue. Construction began on July 1, 2014.

Lakeview Avenue was reopened on June 6, 2017. Construction acceptance from the Cities of Anaheim and Placentia was obtained on June 2, 2017 and OCTA has turned over the maintenance responsibilities to the cities and completed the one-year warranty on some constructed items. The one-year warranty was extended to July 2019 for some minor repair items.

#### Segment: Orangethorpe Avenue Grade Separation

Status: PROJECT COMPLETE

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** The project located at Orangethorpe Avenue railroad crossing is grade separated and open to traffic. The project separated the local street from railroad tracks in the Cities of Placentia and Anaheim by building a bridge for vehicular traffic over the railroad tracks. On May 17, 2016, a joint-grand opening event was held to commemorate the opening to traffic for the Orangethorpe and Tustin/Rose Grade Separation projects. Construction was completed in October 2016 and construction acceptance was obtained from the Cities of Anaheim and Placentia on October 25, 2016. OCTA has turned over the maintenance responsibilities to the cities and completed the one-year warranty on the majority of constructed items. The one-year warranty was extended to June 2019 for some minor repair items.

#### Segment: Placentia Avenue Grade Separation

Status: PROJECT COMPLETE



Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** The project located at Placentia Avenue railroad crossing is grade separated and open to traffic. This project separated the local street from railroad tracks in the City of Placentia by building an underpass for vehicular traffic. An event was held on March 12, 2014, to commemorate the opening. Project acceptance by the Cities of Anaheim and Placentia occurred in December 2014 and the cities assumed full maintenance responsibilities. In December 2015, the one-year warranty period expired with no issues or repairs identified.





#### Segment: Raymond Avenue Grade Separation

Status: PROJECT COMPLETE

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** The project located at Raymond Avenue railroad crossing grade separated the local street from railroad tracks in the City of Fullerton by taking vehicular traffic under the railroad crossing. The City of Fullerton is managing construction and OCTA is providing construction oversight, public outreach, railroad coordination, and ROW support. Construction began on June 2, 2014. Activities this quarter continue to include punchlist item work and project closeout documentation. Raymond Avenue has been opened to traffic since October 2017. OCTA received conditional construction acceptance in May while the contractor completed minor work. Construction acceptance by the City is anticipated in August 2018.

#### Segment: State College Boulevard Grade Separation

Status: PROJECT COMPLETE

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** The project located at State College Boulevard railroad crossing grade separate the local street from railroad tracks in the City of Fullerton by taking vehicular traffic under the railroad crossing. The City of Fullerton managed the construction and OCTA provided construction oversight, public outreach, railroad coordination, and ROW support. Construction activities this quarter continue to include work on pump station, landscape, irrigation, pavement and striping. State College Boulevard was opened to through traffic on November 1, 2017. Construction acceptance and maintenance responsibilities from the City of Fullerton was obtained on March 7, 2018 and the one-year warranty began. Close-out activities will be ongoing through summer 2018.

Segment: Tustin Avenue/Rose Drive Grade Separation

Status: PROJECT COMPLETE

Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** The project located at Tustin Avenue/Rose Drive railroad crossing is grade separated and open to traffic. The project separated the local street from railroad tracks in the Cities of Placentia and Anaheim by building a bridge over the railroad crossing for vehicular traffic. On May 17, 2016, a joint-grand opening event was held to commemorate the opening to traffic for the Orangethorpe and Tustin/Rose Grade Separation projects. Construction was completed in October 2016 and construction acceptance was obtained from the Cities of Anaheim and Placentia on October 25, 2016. OCTA has turned over the maintenance responsibilities to the cities and completed the one-year warranty on the majority of constructed items. The one-year warranty was extended to November 2018 for some minor repair items.







### REGIONAL TRAFFIC SIGNAL SYNCHRONIZATION PROGRAM -

#### Status: 2018 Call for Projects Completed

Contact: Anup Kulkarni, Planning • (714) 560-5867

**Summary:** This program provides funding and assistance to implement multi-agency signal synchronization. The target of the program is to regularly coordinate signals for 2,000 intersections along 750 miles of roadway as the basis for synchronized operation across Orange County. The program also leverages external funding to further enhance the efficiency of the street grid and reduce travel delay.

To date, OCTA and local agencies have synchronized more than 2,000 intersections along more than 597 miles of streets (or 66 completed projects). Through a competitive process, there have been eight rounds of M2 funding awarded by the Board thus far. On June 11, 2018, the Board approved six projects for the 2018 Call for Projects Regional Traffic Signal Synchronization Program, funding \$8.9 million with M2 and leveraging \$6.6 million from SB-1. This program has provided a total of 103 projects totaling more than \$98 million, including \$18 million in external funding.

## LOCAL FAIR SHARE -

Status:OngoingContact:Vicki Austin, Finance • (714) 560-5692

**Summary:** In order to help cities and the County of Orange keep up with the rising cost of repairing the aging street system, this program provides flexible funding intended to augment, not replace, existing transportation expenditures of the cities and the County. All local agencies have been found eligible to receive Local Fair Share funds. On a bi-monthly basis, 18 percent of net revenues are allocated to local agencies by formula. Approximately \$342.4 million in Local Fair Share payments have been provided to local agencies as of the end of this quarter.


See pages 47-48 for funding allocation by local agency.

PROJECT P

**PROJECT Q** 





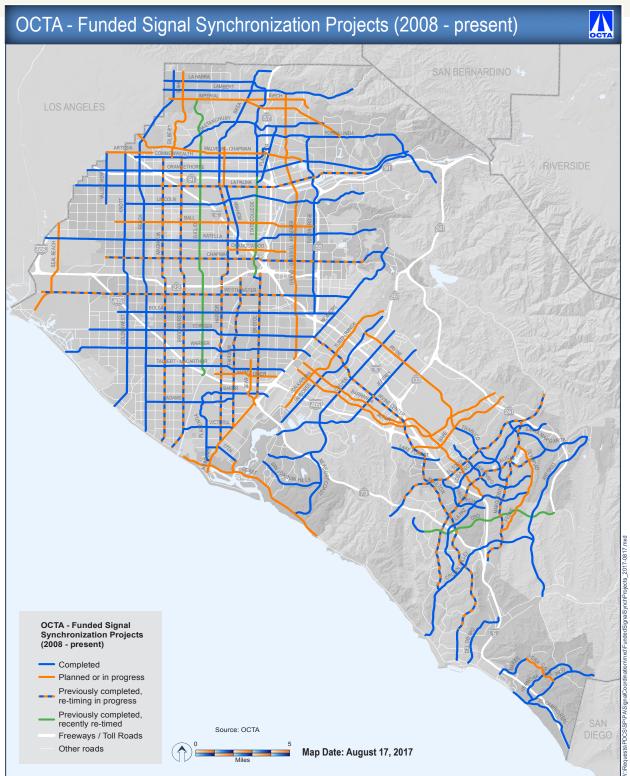



## HIGH FREQUENCY METROLINK SERVICE -

Project R will increase rail services within the County and provides additional Metrolink service north of Fullerton to Los Angeles. The program provides for track improvements, the addition of trains and parking capacity, upgraded stations, and safety enhancements to allow cities to establish quiet zones along the tracks. This program also includes funding for grade crossing improvements at high volume arterial streets, which cross Metrolink tracks.

#### Project: Metrolink Grade Crossing Improvements

Status: PROJECT COMPLETE

Contact: Jennifer Bergener, Rail • (714) 560-5462



**PROJECT R** 

**Summary:** Enhancement of the designated 52 Orange County at-grade rail-highway crossings was completed as part of the Metrolink Service Expansion Program (MSEP) in October 2012. Completion of the safety improvements provided each corridor city with the opportunity to establish a "quiet zone" at their respective crossings. Quiet zones are intended to prohibit the sounding of train horns through designated crossings, except in the case of emergencies, construction work, or safety concerns identified by the train engineer. The Cities of Anaheim, Dana Point, Irvine, Orange, Santa Ana, San Clemente, San Juan Capistrano, and Tustin have established quiet zones within their communities.

#### Project: Metrolink Service Expansion Program

Status: Service Ongoing

Contact: Jennifer Bergener, Rail • (714) 560-5462

**Summary:** Following the completion of the MSEP improvements in 2012, OCTA deployed a total of ten new Metrolink intra-county trains operating between Fullerton and Laguna Niguel/Mission Viejo, primarily during the midday and evening hours. Efforts to increase ridership through a redeployment of the trains without significantly impacting operating costs have been underway since 2014. Average daily ridership on intra-county trains has increased by 13 percent since Fiscal Year 2012-13.

In April 2015, several schedule changes were implemented to connect a 91/Perris Valley Line train to an intracounty service train, at Fullerton. This allowed a later southbound peak evening departure option from Los Angeles to Orange County. Ridership on these two trains combined has increased by 46 percent since the improvement was implemented.

Part of OCTA's re-deployment plan involves providing new trips from Orange County to Los Angeles. SCRRA continues to work on behalf of its members, the RCTC, LA Metro, and OCTA, to negotiate an agreement with the BNSF Railway for the shared used of their corridor and associated indemnification and liability. This agreement is necessary to secure 24 additional operating slots to provide more passenger rail service on railroad ROW owned



by the BNSF. Operation of additional Metrolink trains to Los Angeles is contingent on the indemnification and liability agreement, following completion of the triple track project in early 2019, on the BNSF Railway between Fullerton and Los Angeles.

#### **Rail Corridor and Station Improvements**

Additionally, under MSEP, funding is provided for rail line and station improvements to accommodate increased service. Rail station parking lot expansions, better access to platforms, among other improvements have been made or are underway. For schedule information on station improvement projects, please see the CAP pages on pages 49-53 at the back of this report.

#### Segment: Anaheim Canyon Metrolink Station Improvements

Status: Design Phase Underway

Contact: Jim Beil, Capital Programs • (714) 560-5646

**Summary:** This OCTA-led project will include construction of a second main track and platform, lengthening the existing platform, and improved pedestrian circulation. The project will also include the addition of benches, shade structures, and ticket vending machines. The design plans have been competed to 60 percent and are being reviewed by the City of Anaheim, Metrolink, and OCTA. Plans are expected to be complete and ready to bid in July 2019. Construction of the project is expected to begin in December 2019 with completion anticipated in early 2021.

#### Segment: Fullerton Transportation Center Improvements

Status: Construction Phase Underway - 50% Complete

Contact: Jim Beil, Capital Programs • (714) 560-5646

**Summary:** Completed early on, a new 5-level parking structure was constructed to provide additional transit parking at the Fullerton Transportation Center for both intercity rail service and commuter rail passengers. This City-led project was completed on June 19, 2012. After completion, an elevator upgrade project was initiated with leftover savings. The elevator project will modify the existing pedestrian bridge to add two new traction elevators, one on each side. The City of Fullerton is the lead on this project as well. Construction began in January 2016 and restroom improvements were completed. Work on the elevators was delayed due to construction contractor's elevator sub pulling off the job. Construction began again in January 2017. Shoring and excavation for the elevator pits has been completed. Due to additional scheduling issues the contractor has encountered with subs and coordination with BNSF, no work was performed in the last quarter. It is now anticipated the project will be completed in early 2019.



## Segment: Laguna Niguel/Mission Viejo Metrolink Station Americans with Disabilities Act (ADA) Ramps

Status: PROJECT COMPLETE



Contact: Jim Beil, Capital Programs • (714) 560-5646

**Summary:** The Laguna Niguel/Mission Viejo station accessibility improvements project was completed in September 2017. Improvements include new ADA-compliant access ramps on either side of the pedestrian undercrossing and a unisex ADA-compliant restroom, vending machine room, and three passenger canopies. Construction acceptance from the cities was obtained on September 20, 2017 and OCTA has turned over the maintenance responsibilities to the cities and commenced the one-year warranty. Close-out activities and final costs are underway.

#### Segment: Orange Transportation Center Metrolink Parking Structure

Status: Construction Phase Underway - 57% Complete

Contact: Jim Beil, Capital Programs • (714) 560-5646


**Summary:** This project will include a 611-space, 5-level shared use parking structure that will be located on Lemon Street between Chapman Avenue and Maple Street in Orange. Per a cooperative agreement between OCTA and the City of Orange, the City of Orange is the lead on the design phase, and OCTA is the lead on the construction phase of the project. Construction began on July 17, 2017. All surface decks on the parking structure were completed in June 2018. Interior electrical and mechanical systems are being installed as well as elevator towers. The project is expected to be completed in February 2019.

#### Segment: Placentia Metrolink Station Improvements and Parking Structure

Status: Design Complete - Ready for Advertisement subject to BNSF construction and maintenance agreement

Contact: Jim Beil, Capital Programs • (714) 560-5646

**Summary:** Plans for the proposed Placentia Metrolink Station Project were near completion when the City of Placentia requested to modify them to include a parking structure to be built where surface parking had been designed. On June 27, 2016, the Board approved a new Cooperative Agreement with the City of Placentia that revised the project's scope and budget. There will now be a parking structure as part of the project and the City of Placentia will contribute towards the cost. The station will include platforms, parking, a new bus stop, and passenger amenities. OCTA is the lead for design and construction of the project. The project will also include a third track which should assist with the on-time performance of train operations and provide operational flexibility for both freight and passenger trains. BNSF will be the lead on the rail construction. Design plans for the station are complete and will be ready to advertise for bidding once a track sharing agreement with BNSF is in place. Negotiations are underway for this agreement and deal points are anticipated to be in place by the end of the summer 2018.



#### Segment: San Clemente Pier Station Lighting

Status: PROJECT COMPLETE

Contact: Jim Beil, Capital Programs • (714) 560-5646



**Summary:** This project was completed on March 17, 2017, and is in the closeout phase. OCTA was the lead for design and installation of this project which added lighting to the existing platform and new decorative hand rails at the San Clemente Pier Station.

Additional rail corridor improvements include: completed Control Point project at Fourth Street in the City of Santa Ana, which will provide rail operational efficiencies; replacement of the San Juan Creek railroad bridge in the City of San Juan Capistrano, which will also accommodate a future bike trail on the south end along the creek (design is 90 percent complete and ROW acquisition is in progress); the Railroad ROW Slope Stabilization project, which includes eight locations within the OCTA-owned LOSSAN rail corridor that have been identified for improvements to prevent future erosion and slope instability (advertised for construction and contract award planned next quarter); and continued implementation of video surveillance systems and Positive Train Control.

#### Segment: Laguna Niguel to San Juan Capistrano Passing Siding Project

Status: Design Phase Underway - 95% Complete

Contact: Jim Beil, Capital Programs • (714) 560-5646

**Summary:** Currently in the design phase, this project will add approximately 1.8-miles of new passing siding railroad track adjacent to the existing mainline track, which will enhance operational efficiency of passenger services within the LOSSAN rail corridor. The 100 percent design plans have been reviewed by SCRRA and the City of San Juan Capistrano. Final design comments from SCRRA and the City are being resolved and incorporated. Completion of the design phase is expected in third quarter of 2018 and construction is expected to begin in early-2019. This project is marked "red" in the CAP, signifying a delay of more than three months.

#### Segment: Sand Canyon Grade Separation

Status: PROJECT COMPLETE



Contact: Rose Casey, Capital Projects • (714) 560-5729

**Summary:** The project separated the local street from railroad tracks in the City of Irvine by constructing an underpass for vehicular traffic. The westbound lanes were opened to traffic on June 12, 2014, and the eastbound lanes were opened to traffic on July 14, 2014. A road opening ceremony was held on August 11, 2014. The project is complete and construction acceptance was obtained from the City of Irvine on January 15, 2016. The project completed the one-year warranty period and no repairs were identified. The project closed out in mid-January 2017.



#### Segment: Tustin Metrolink Station Parking Structure

Status: PROJECT COMPLETE

Contact: Jim Beil, Capital Programs • (714) 560-5646

**Summary:** Also completed early on, this project provided additional parking at the Tustin Metrolink Station to meet increased requirements associated with the MSEP by constructing a new 4-story parking structure with approximately 735 spaces, plus on-site surface parking. The parking structure was opened to the public on September 22, 2011.

## TRANSIT EXTENSIONS TO METROLINK 🗸

In order to broaden the reach of Metrolink to other Orange County cities, communities, and activity centers, Project S includes a competitive program which allows cities to apply for funding to connect passengers to their final destination via transit extensions. There are currently two categories for this program: a fixed guideway program (street car) and a rubber tire transit program.

#### Project: OC Streetcar

Status: Construction Bids Opened, Contract Negotiations with Vehicle Manufacturer, Utility Relocation Work Ongoing

Contact: Kelly Hart, Rail • (714) 560-5725

**Summary:** The OC Streetcar Project will serve the Santa Ana Regional Transportation Center through downtown Santa Ana, and the Civic Center to Harbor Boulevard in the City of Garden Grove. OCTA is serving as the lead agency for the project.

In consideration of requests from the bidders for additional time to prepare construction bids, ongoing delays with the FTA's FFGA approval process, and delays in securing necessary ROW, an addendum was issued revising the construction bid submittal date to April 27, 2018. Subsequently, and for the same reasons stated above, an addendum was issued revising the bid submittal date to June 19, 2018.

On June 19, four of the five prequalified construction bidders submitted bids. Staff began conducting a bid responsiveness review of the four bids and are expected to go to the Board with the results of the bid responsiveness review and recommended contract award next quarter. Based upon construction bids, schedule delays and other project refinements, a revised project cost estimate and funding plan will be presented to the Board in July 2018 for approval.

Work continues to progress on key OC Streetcar activities, including final possession of remaining required ROW, procurement of demolition services, coordination with third parties on utility relocation, finalizing the California Public Utilities Commission safety approvals for the OC Streetcar's grade crossings certification, finalizing the



**PROJECT S** 



scope of services for the operations and maintenance request for proposals, and continued coordination with the FTA on the status of the FFGA. Staff is working toward execution and NTP for the streetcar vehicle manufacturing contract anticipated for next quarter.

#### Project: Bus and Station Van Extension Projects

Status: Service Ongoing for Anaheim Canyon Metrolink Bus Connection

Contact: Joseph Alcock, Planning • (714) 560-5372

**Summary:** Bus and Station Van Extension projects help enhance the frequency of service in the Metrolink corridor by linking communities within the central core of Orange County to commuter rail. To date, the Board has approved one round of funding for bus and van extension projects, totaling over \$730,000. One project located within the City of Anaheim and three proposals within the City of Lake Forest were approved for funding by the Board on July 23, 2012. Currently, the Anaheim Project is in service and the Lake Forest Projects have been cancelled. The Anaheim Canyon Metrolink Station Bus Connection began service in February 2013 and is anticipated to continue providing service between the station and the Anaheim Resort area through 2020.


### METROLINK GATEWAYS -

Status: PROJECT COMPLETE

Contact: Jennifer Bergener, Rail • (714) 560-5462



**Summary:** This project constructed the Anaheim Regional Transportation Intermodal Center (ARTIC) located at 2626 East Katella Avenue in the City of Anaheim. In addition to providing transit connections for OCTA bus service, Metrolink and Amtrak service, shuttle and charter bus service, taxis, bikes, and other public and private transportation services, ARTIC also accommodates future high-speed rail trains. The City of Anaheim, which led the construction effort, opened the facility to rail and bus service on December 6, 2014. A ribbon-cutting ceremony was held on December 8, 2014, with a grand opening celebration hosted on December 13, 2014. This facility replaced the former Anaheim Station that was located on the opposite side of the freeway in the Angel Stadium parking lot.



### EXPAND MOBILITY CHOICES FOR SENIORS AND PERSONS WITH DISABILITIES -

Project U expands mobility choices for seniors and persons with disabilities, and includes the SMP, the SNEMT Program, and the Fare Stabilization Program. Since inception, approximately \$58.9 million in Project U funding has been provided under M2.

**PROJECT U** 

#### Project: Senior Mobility Program

Status: Ongoing

Contact: Beth McCormick, Transit • (714) 560-5964

**Summary:** This program provides one percent of net M2 revenues to continue and expand local community transportation service for seniors under the SMP. Since inception, more than \$17.4 million and 1,955,000 boardings have been provided for seniors traveling to medical appointments, nutrition programs, shopping destinations, and senior and community center activities. This quarter, approximately \$919,400 was paid\* out to the 31 participating cities during the months of May and July.

\*Payments are made every other month (January, March, May, July, September, and November). July payments are based on June accruals, and therefore counted as June payments. The amount totaled for one fiscal year quarter either covers one or two payments, depending on the months that fall within that quarter.

#### Project: Senior Non-emergency Medical Transportation Program

Status: Ongoing

Contact: Beth McCormick, Transit • (714) 560-5964

**Summary:** This program provides one percent of net M2 revenues to supplement existing county-wide senior non-emergency medical transportation services. Since inception, more than \$19.0 million and 727,000 SNEMT boardings have been provided. This quarter, approximately \$971,000 in SNEMT funding was paid\* to the County of Orange in the months of May and July.

\*Payments are made every other month (January, March, May, July, September, and November). July payments are based on June accruals, and therefore counted as June payments. The amount totaled for one fiscal year quarter either covers one or two payments, depending on the months that fall within that quarter.



#### Project: Fare Stabilization Program

Status: Ongoing

Contact: Sean Murdock, Finance • (714) 560-5685

**Summary:** Between years 2011-2015, one percent of net M2 revenues was dedicated to stabilize fares and provide fare discounts for bus services and specialized ACCESS services for seniors and persons with disabilities. Effective January 28, 2016, an amendment to the M2 Ordinance No. 3, adjusted this amount to 1.47 percent of net M2 revenues to be dedicated to the Fare Stabilization Program.

Approximately \$1,428,000\* in revenue was allocated this quarter to support the Fare Stabilization Program. The amount of funding utilized each quarter varies based on ridership. During the quarter, based on 3,100,000 program-related boardings recorded on fixed route and ACCESS services, approximately \$881,000 was utilized. Since inception of the program, more than \$22 million and 96 million program-related boardings have been provided.

\*Payments are made every other month (January, March, May, July, September, and November). July payments are based on June accruals, and therefore counted as June payments. The amount totaled for one fiscal year quarter either covers one or two payments, depending on the months that fall within that quarter.

## COMMUNITY BASED TRANSIT/CIRCULATORS -

Status: Service Updates

Contact: Joseph Alcock, Planning • (714) 560-5372

**Summary:** This program provides funding for local jurisdictions to develop local bus transit services such as community-based circulators and shuttles that complement regional bus and rail services and meet needs in areas not adequately served by regional transit. On June 24, 2013, the Board approved the first round of funding for \$9.8 million to fund six projects. Funding was approved to implement vanpool services from local employment centers to transportation hubs, special event and seasonal services that operate during heavy traffic periods, and local community circulators that carry passengers between various shopping, medical, and transportation-related centers. On June 13, 2016 the Board approved the second round of Project V funding in the amount

approved a third round of Project V funding in the amount of \$6.8 million for 6 transit projects. OCTA receives ridership reports from local agencies on a regular basis to monitor the success of these services against performance measures adopted by the Board. Staff will continue to monitor these services to ensure that performance standards are met. The most recent Project V Ridership report was presented to the Transit Committee on July 12, 2018 and Board on July 23, 2018.

of \$26.7 million for 17 transit projects and \$323,780 for seven planning studies. On June 25, 2018 the Board

**PROJECT V** 



Out of the projects programmed by OCTA: 14 are currently active; 5 are expected to initiate new services; 3 have been cancelled (due to low ridership); and 1 is anticipated to be cancelled. Consequently, most of these services are currently meeting their required performance standards and during the last reporting period provided approximately 159,000 daily boardings. The next Project V Ridership report is scheduled for January 2019. Lessons learned from the success of implemented services are incorporated into recommendations for future funding guidelines.

## SAFE TRANSIT STOPS -

Status: City-Initiated Improvements Underway or Complete; Mobile Ticketing in Use

Contact: Joseph Alcock, Planning • (714) 560-5372

**Summary:** This program provides funding for passenger amenities at the 100 busiest transit stops across the County. Stop improvements are designed to ease transfers between bus lines and provide passenger amenities such as improved shelters and lighting.

To date, the Board has approved up to \$1,205,666 to support 51 city-initiated improvements and \$370,000 for OCTA-initiated improvements. The City of Anaheim postponed development of eight stops and will move forward in a future funding cycle. Of the remaining 43 stops, 14 stops have been completed and the remaining 29 stop improvements are currently in the project closeout process. Closeout of all projects is anticipated by September 2018.

For OCTA-initiated improvements funds were initially programmed for the Text for Next Program and were ultimately reallocated to support OCTA's mobile ticketing application (app).

In addition, a meeting with local agencies (that have stops eligible for improvements) is planned on August 17, 2018 to discuss this program and to also review current needs at eligible bus stop locations.



## CLEAN UP HIGHWAY AND STREET RUNOFF THAT POLLUTES BEACHES -

Project: Environmental Cleanup Program

Status: Ongoing

Contact: Dan Phu, Planning • (714) 560-5907

**Summary:** This program implements street and highway-related water quality improvement programs and projects that assist agencies countywide with federal Clean Water Act standards for urban runoff. It is intended to augment, not replace existing transportation-related water quality expenditures and to emphasize high-impact capital improvements over local operations and maintenance costs. The ECAC is charged with making recommendations to the Board on the allocation of funds for the ECP. These funds are allocated on a countywide, competitive basis to assist agencies in meeting the Clean Water Act standards for controlling transportation-related pollution.

Project X is composed of a two-tiered funding process focusing on early priorities (Tier 1), and a second program designed to prepare for more comprehensive capital investments (Tier 2). To date, there have been seven rounds of funding under the Tier 1 grants program. A total of 154 projects, amounting to approximately \$20.1 million, have been awarded by the Board since 2011. There have been two rounds of funding under the Tier 2 grants program. A total of \$27.89 million have been awarded by the Board since 2013. To date, 33 of the 34 Orange County cities plus the County of Orange have received funding under this program. The Board approved the release of the eighth Tier 1 Call for Projects on March 12, 2018 in the amount of approximately \$2.8 million and programming recommendations are anticipated in late-summer.

Staff estimates that over 6.2 million cubic feet of trash has been captured as a result of the installation of Tier 1 devices since the inception of the Tier 1 Program in 2011. This is equivalent to over 2,600 forty-foot shipping containers. Over time, the volume of trash captured is expected to increase. It is estimated that the funded Tier 2 projects, once fully functional, will have an annual groundwater recharge potential of approximately 157 million gallons of water from infiltration or through pumped and treated recharge facilities.

Staff continues to work with the ECAC and the County of Orange to recommend the appropriate timing for the next Tier 2 Call for Projects.

**PROJECT X** 



## FREEWAY MITIGATION -

Project: Environmental Mitigation Program

Status: Biological Permits Issued and Conservation Plan in Place

Contact: Dan Phu, Planning • (714) 560-5907

**Summary:** In June 2017, the United States Fish and Wildlife Service, and the California Department of Fish and Wildlife (Wildlife Agencies) finalized the issuance of their respective biological opinion, findings, and associated permits, as well as signed the Conservation Plan Implementing Agreement. Receipt of these permits represent the culmination of years of collaboration and support by the Board, environmental community, and Wildlife Agencies. As a result, the environmental process will be streamlined allowing OCTA to move forward with the M2 freeway projects (as described in the Conservation Plan) with little additional coordination from the Wildlife Agencies. The Conservation Plan also includes a streamlined process for coordination for streambed alteration agreements. This is needed for portions of freeway projects that cross through streams and riverbeds. The OCTA Conservation Plan is unique as it is only the second state/federal conservation plan approved in Orange County.

The program is proceeding as planned, with seven properties (Preserves) acquired (1,300 acres), and 12 restoration projects approved for funding by the Board, totaling approximately 350 acres. The restoration project plans have been approved by the wildlife agencies and are currently at various stages of implementation. The Board authorized \$42 million (inclusive of setting aside funds for long-term land management) for property acquisitions, \$10.5 million to fund habitat restoration activities, and \$2.5 million for conservation plan development and program support, for a total of approximately \$55 million.

As part of the Conservation Plan requirement, an endowment has been established to pay for the long-term management of the Preserves. It is estimated that it will take up to fifteen years to fully fund the endowment, deposits are made on a fiscal year (July 1 through June 30) basis. As anticipated, the first annual deposit of \$2.9 million for the endowment was made in early 2017. A second deposit was made in August 2017. On a go-forward basis, endowment deposits will be made near the beginning of the fiscal year during the August time-frame. Staff will continue to oversee and provide endowment updates to the Finance and Administration Committee on a regular basis.

To date, five of the seven Preserve resource management plans (RMPs) have been completed and were finalized in September 2017. These RMPs guide the management of the Preserves as outlined within the Conservation Plan. OCTA publicly released the remaining two RMPs in summer 2017 for review and comment for a 90-day period. OCTA held two public meetings in the Cities of Brea and Laguna Niguel to solicit public input and a workshop at the regularly scheduled EOC meeting on October 4, 2017. OCTA anticipates finalizing these RMPs by end of summer 2018. Staff will continue to oversee and manage the Preserves until a long-term manager(s) is established.

In consultation with the local fire authority, staff will be preparing fire management plans (Plans) for the seven Preserves. To the degree feasible The Plans will establish policies and approaches to maximize protection of biological resources during fire suppression activities. The Plans will provide guidelines for decision-making at all



## ENVIRONMENTAL

stages including fire prevention, pre-fire vegetation management, suppression activities, and post-fire responses that are compatible with conservation and stewardship responsibilities. These Plans are a requirement of the Conservation Plan and will require approval by the Wildlife Agencies. The Plans are anticipated to be complete in 2020.

In September, the Board authorized funding to advance the streamlined federal clean water permitting requirements administered by the United States Army Corps of Engineers (Corps). Concurrently, OCTA has been working with the State Water Resources Control Board (State Board) to comply with the state clean water permit requirements. In December, the Corps issued a programmatic permit to OCTA and Caltrans (as owner/operator of the state highway system). The State Board provided a letter to OCTA in January, which further secured assurances related to advanced mitigation and freeway project permit issuance. These efforts are the result of years of collaboration between OCTA, the Corps, and State Board, and constitute another groundbreaking milestone for the M2 Environmental Mitigation Program.

To date, multiple freeway projects have utilized the Conservation Plan and/or the Clean Water Act streamlined permitting process. The following projects are either in or near construction and were able to benefit from these mechanisms: Project K (Interstate 405 Improvement Project from State Route 73 to the Los Angeles County line), Project C (Interstate 5 Improvement Project from State Route 73 to El Toro Road), and Project M (Interstate 605 and Katella Interchange Project). If these mechanisms were not in place, it is anticipated that these projects would incur an additional \$700,000 to \$2.5 million in mitigation related costs and unknown schedule risks. Furthermore, a strong partnership has been fostered through collaboration with the environmental community.

OCTA provides docent led hikes and equestrian rides in the Preserves. A list of scheduled 2018 wilderness Preserve tours is available on the M2 website at <u>www.PreservingOurLegacy.org</u>.


As part of the safeguards in place for the M2 Program, a 12-member EOC makes recommendations on the allocation of environmental freeway mitigation funds and monitors the implementation of the Conservation Plan between OCTA and state and federal Wildlife Agencies. The EOC has led efforts with policy recommendations to the Board and has operated in an open and transparent manner that has garnered the trust of stakeholders, ranging from the environmental community to the recreational community to Orange County citizens.

See map of Preserves and funded restoration properties on the following page.



## ENVIRONMENTAL

C. C.

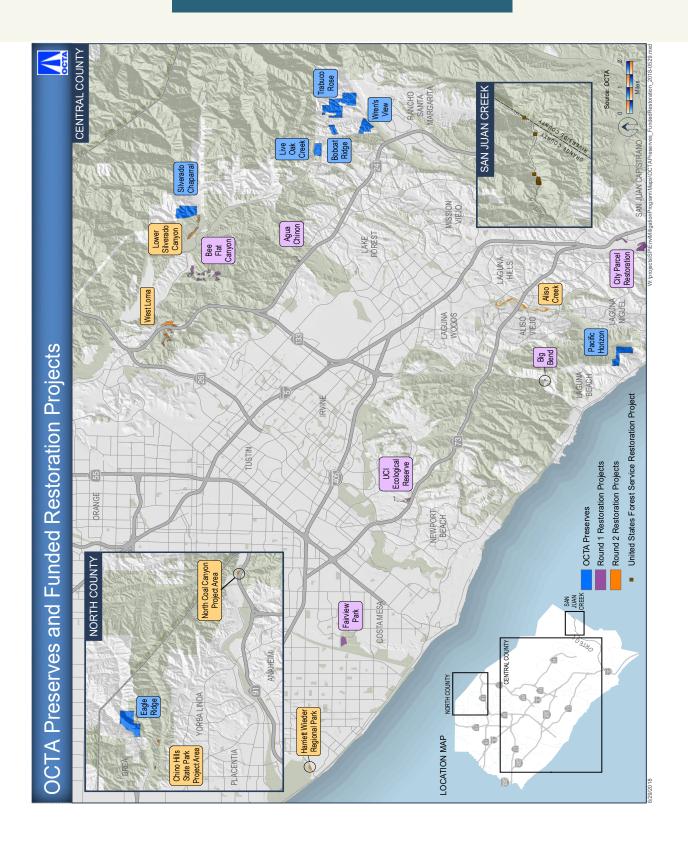



## PROGRAM MANAGEMENT OFFICE -

Contact: Tami Warren, PMO Manager • (714) 560-5590

The M2 PMO provides inter-divisional coordination for all M-related projects and programs. To ensure agencywide compliance, the PMO holds a bi-monthly committee meeting comprised of executive directors and key staff from each of the divisions, who meet to review significant issues and activities within the M2 programs. This quarter, the focus of the PMO has been on several major items, including the following.

#### **Next 10 Delivery Plan**

On November 14, 2016, the Board adopted the Next 10 Delivery Plan providing staff guidance on the delivery of M2 projects and programs between 2017 and 2026. The PMO monitors the progress on the ten deliverables identified in the Plan and reports on them in this report. See <u>pages 3-6</u> for status on deliverables. With a preliminary lower forecasted sales tax of \$13.1 billion over the lifetime of the M2 program, a 2018 update of the Next 10 Plan was presented to the Board in September 2018.

#### M2 Performance Assessment

The M2 ordinance includes a requirement for a performance assessment to be conducted at least once every three years to evaluate OCTA's efficiency and effectiveness in delivery of M2 as promised to the voters. Three prior performance assessments have been completed covering fiscal years FY 2006-07 through FY 2008-09, FY 2009-10 through FY 2011-12, and FY 2012-13 through FY 2014-15. Findings and recommendations from assessments are presented to the Board and recommendations are implemented as appropriate. A fourth assessment will begin in July 2018 and cover the period between July 1, 2015 and June 30, 2018. During this quarter, a consultant was selected, and the contract executed with work to begin in July 2018. A final report is anticipated to be brought to the Board in spring 2019.

#### **M2 Ordinance Compliance Matrix**

The PMO annually reviews and updates the M2 Ordinance Compliance Matrix to ensure that OCTA complies with all the requirements in Ordinance No. 3. The annual review for January 1, 2017 to December 31, 2017 was completed, and the M2 Ordinance Compliance Matrix was presented to the Taxpayer Oversight Committee (TOC) Audit Subcommittee on February 13, 2018. The TOC met on April 10, 2017 to conduct the Annual M2 Audit and determined Measure M is being delivered as promised to Orange County voters for the 27th consecutive year.



#### **Market Conditions Forecast and Risk Analysis**

In September 2017, the Board was presented with a Next 10 Market Conditions Forecast and Risk Analysis Report conducted by Dr. Wallace Walrod and Dr. Marlon Boarnet. The consultant's analysis identified a strong potential for OCTA to experience an increasing cost environment during the Next 10 delivery years. This, coupled with a reduction in revenue, could present the potential for significant challenges in the delivery of M2 and Next 10.

Given this analysis, the Board directed staff to continue to work with the consultant to monitor and track key early warning indicators and provide the Board with updates in a timeline consistent with updates on the M2 sales tax revenue forecast. The scope includes providing presentations on a summary of findings from the monitoring effort to the Board bi-annually and, if noteworthy, more frequent updates will be provided through these M2 quarterly progress reports. The scope was included with the FY17-18 Q2 M2 Quarterly Progress Report to the Board. During this quarter, the consultant worked on monitoring and tracking market conditions and risk analysis. A Market Trend Tracking report was presented to the Board in September 2018.

#### **M2** Administrative Safeguards

M2 includes a one percent cap on administrative expenses for salaries and benefits of OCTA administrative staff on an annual basis. In a legal opinion on M2, it was determined that in years where administrative salaries and benefits are above one percent, only one percent can be allocated with the difference borrowed from other, non-M2 fund sources. Conversely, in years where administrative salaries and benefits are below one percent, OCTA can still allocate the full one percent for administrative salaries and benefits but may use the unused portion to repay the amount borrowed from prior years in which administrative salaries and benefits were above one percent.

Based on the original M2 revenue projections, OCTA expected to receive \$24.3 billion in M2 funds, with one percent of total revenues available to fund administrative salaries and benefits over the life of the program. As M2 revenue projections declined (currently \$13.1 billion or 46 percent lower) as a result of economic conditions, the funds available to support administrative salaries and benefits have also declined from the original expectations. While revenue has declined, the administrative effort needed to deliver M2 remains the same. Additionally, the initiation of the Early Action Plan (EAP) in 2007 required administrative functions four years prior to revenue collection. While the EAP resulted in project savings and significant acceleration of the program, administrative functions were required during this time with associated administrative costs.

As a result of the aforementioned factors, OCTA has incurred higher than one percent administrative costs. OCTA currently has Board approval to use funds from the Orange County Unified Transportation Trust (OCUTT) fund to cover costs above the one percent, with the understanding that those funds will be repaid with interest in future years that OCTA administrative costs fall below the one percent cap. As of June 30, 2012, OCTA had borrowed approximately \$5.2 million from OCUTT. Over the last few years, OCTA has experienced under-runs in the one percent administration cap and has made payments to OCUTT to reduce the outstanding balance. As



of the most recent June 2018 Taxpayer Oversight Committee Report, the outstanding balance was \$1.6 million.

Staff meets quarterly to review all labor costs to ensure proper cost allocation under M2. After the quarter ended, staff met on April 27, 2018 to review labor reports for this quarter to ensure costs attributed to the one percent cap were accurately reported and there were no misplaced project related costs, as well as to ensure project costs were applied to the correct projects. Staff will meet again on July 18, 2018, to conduct this quarterly review.

#### **Taxpayer Oversight Committee**

ROTOR

The M2 Ordinance requires a TOC oversee the implementation of the M2 plan and ensure compliance with all requirements of Measure M2 Ordinance No. 3. With the exception of the elected Auditor/Controller of Orange County who is identified as the chair in the Ordinance, all other members are not elected or appointed officials. Members are recruited and screened for expertise and experience independently by the Orange County Grand Jurors Association, and are selected from the qualified pool by lottery. The TOC meets every other month. The TOC upholds the integrity of the measure by monitoring the use of M2 funds and ensuring compliance. The responsibilities of the 11-member Measure M2 TOC are to:

•Ensure all transportation revenue collected from M2 is spent on the projects approved by the voters as part of the plan

•Ratify any changes in the plan and recommend any major changes go back to the voters for approval

•Participate in ensuring that all jurisdictions in Orange County conform with the requirements of M2 before receipt of any tax monies for local projects

•Hold annual public meetings regarding the expenditure and status of funds generated by M2

•Review independent audits of issues regarding the plan and performance of the Orange County local Transportation Authority regarding the expenditure of M2 sales tax monies

•Annually certify whether M2 funds have been spent in compliance with the plan.

The TOC met on April 10, 2018 to hold its annual Measure M2 public hearing, vote on the Measure M2 Compliance Findings and Local Jurisdictions Eligibility Findings, and hear updates on the OC Streetcar, M2 Quarterly Progress Report (Second Quarter) and autonomous vehicles. The committee unanimously found that OCTA is proceeding in accordance with the M2 Transportation Ordinance and Investment Plan, and that Measure M2 is being delivered as promised to voters for the 27th consecutive year.

The TOC also met on June 12, 2018 to receive updated financial information on the M2 Quarterly Revenue & Expenditure Report (Mar. 18) and hear program/project updates on the Comprehensive Transportation Funding Programs (CTFP) and Measure M2 Quarterly Progress Report (Third Quarter). OCTA staff also provided the committee with information on SB 1.

Two subcommittees assist the TOC with their safeguard responsibilities: the Annual Eligibility Review (AER)



Subcommittee and the Audit Subcommittee. The AER Subcommittee meets a few times per year, as needed, to ensure local jurisdictions have submitted the following documents in order to be deemed eligible to receive M2 funding: Congestion Management Program, Mitigation Fee Program, Local Traffic Signal Synchronization Plan, Pavement Management Plan, and an Expenditure Report. The Audit Subcommittee meets bi-monthly and is responsible for reviewing the quarterly M2 Revenue and Expenditure Reports and the Annual M2 Audit, as well as any other items related to M2 audits.

## M2 FINANCING AND SCHEDULE OF FUNDING -

## Contact: Sean Murdock, Finance • (714) 560-5685 Revenue Forecast and Collection

OCTA contracts with three universities (Chapman University; University of California, Los Angeles; and California State University, Fullerton) to provide a long-range forecast of taxable sales to forecast M2 revenues for purposes of planning projects and program expenditures. In the past, OCTA has taken an average of the three university taxable sales projections to develop a long-range forecast of M2 taxable sales. On March 28, 2016, as part of the FY 2016-17 budget development process, the Board approved a new sales tax forecast methodology. This methodology includes a more conservative approach by utilizing a five-year forecast from MuniServices, Inc. Historically, MuniServices, Inc. has been more conservative than the three universities over the first five years of M2 revenue collection (2011-2016).

Revenue forecast information is updated quarterly based on the actual revenues received for the previous quarter. As required by law, OCTA pays the State Board of Equalization a fee to collect the sales tax. The M2 Ordinance estimated this fee to be 1.5 percent of the revenues collected over the life of the program.

## **Current Forecast**

Based on long term forecasts received in July 2018, OCTA staff forecasts total nominal sales tax collections over the life of M2 to be approximately \$13.1 billion. Original projections in 2005 estimated total nominal M2 sales tax collections at \$24.3 billion. Based on the current estimated forecast of \$13.1 billion, sales tax revenue will run approximately \$11.2 billion (46 percent) less than the original 2005 projection. The revenue forecast for the life of the M2 Program will vary as actual sales tax revenue data is incorporated.

Final sales tax receipts through May 2018 were received in July 2018 and reflected a growth in sales tax revenue of 5.15 percent over the same period of the prior fiscal year. The growth is higher than the budgeted sales tax growth rate of 3.3 percent for fiscal year 2017-18. It is important to note that, this year the California Department of Tax and Fee Administration changed the methodology of sales tax distribution to OCTA. This makes it difficult to determine the actual growth rate of sales tax for fiscal year 2017-18 until the final month's allocation is distributed in August 2018. Staff will continue to closely monitor sales tax receipts.

This Page Intentionally Left Blank



#### Schedule of Revenues, Expenditures and Changes in Fund Balance as of June 30, 2018 (Unaudited) Schedule 1

Period from Inception to Quarter Ended Year to Date (\$ in thousands) June 30, 2018 June 30, 2018 June 30, 2018 (A) (B) Revenues: Sales taxes \$ 78,442 \$ 316,533 \$ 2,075,622 Other agencies' share of Measure M2 costs: Project related 19,104 74,695 621,047 Non-project related 454 Interest: Operating: Project related Non-project related Bond proceeds 464 592 4 (207) 6.351 25,414 2,352 6,424 51,318 Debt service 80 184 307 Commercial paper 393 Right-of-way leases 5 7 914 Proceeds on sale of assets held for resale 313 5,397 12,201 Donated assets held for resale 2,071 Miscellaneous: Project related 270 --Non-project related 100 Total revenues 100,093 410,055 2,790,703 Expenditures: Supplies and services: State Board of Equalization (SBOE) fees (229)2,474 21,965 Professional services: Project related 15,679 33,569 344,927 Non-project related 2,269 5,513 22,711 Administration costs: Project related 2,228 8,914 62,371 Non-project related: Salaries and Benefits 640 2,560 22,560 Other 36,518 1,235 4.940 Other: Project related 45 92 4.941 Non-project related 64 114 4,006 Payments to local agencies: Project related 30,470 106,609 837,883 Capital outlay: Project related 80,584 225,757 856,724 Non-project related 31 Debt service: Principal payments on long-term debt 7,775 42,335 Interest on long-term debt and commercial paper 10 21,059 157,938 Total expenditures 132,995 419,376 2,414,910 Excess (deficiency) of revenues over (under) expenditures (32,902) (9,321) 375,793 Other financing sources (uses): Transfers out: Project related (2,768) (8,474) (38, 391)Transfers in: Project related 996 2,983 82,491 Non-project related (1,973)-358,593 Bond proceeds

(1,772)

(34,674)

\$

\$

(7, 464)

(16,785)

\$

402,693

778,486

Total other financing sources (uses)

Excess (deficiency) of revenues over (under) expenditures and other sources (uses)



	arter Ended				Period from		Period from		
	ne 30, 2018 (actual)		Year to Date une 30, 2018 (actual)	J	Inception through une 30, 2018 (actual)	I	July 1, 2018 through March 31, 2041 (forecast)		Total
			(C.1)		(D.1)		(E.1)		(F.1)
¢	78 112	¢	316 533	¢	2 075 622	¢	10 061 818	¢	13,037,440
φ	,	φ	,	φ		φ	, ,	φ	193,017
	· /		,				,		13,230,457
	10,200		022,001		, ,		11,120,121		
	-		-				-		454
	-		-				-		100
	78,235		322,884		2,101,590		11,129,421		13,231,011
	(229)		2,474		21,965		127,070		149,035
	2,269		5,513		18,935		83,297		102,232
	640		2,560		22,560		109,601		132,161
	1,235		4,940		36,518		179,576		216,094
	64		114		4,006		20,272		24,278
	-		-		31		-		31
	1,350		6,378		34,717		219,201		253,918
	5,329		21,979		138,732		739,017		877,749
\$	72,906	\$	300,905	\$	1,962,858	\$	10,390,404	\$	12,353,262
			(C.2)		(D.2)		(E.2)		(F.2)
¢		¢		¢	259 502	¢	1 775 000	¢	2,133,593
φ	-	φ	- 6 424	φ		φ		φ	62,169
	,		- ,		,		,		5,031
			-				4,724		393
	2,432		6,608		410,611		1,790,575		2,201,186
	-		-		3 776		6 191		9.967
	-		7,775		-, -		,		2,106,670
	10		,						956,324
	10		28,834		204,049		2,868,912		3,072,961
\$	2,422	\$	(22,226)	\$	206,562	\$	(1,078,337)	\$	(871,775)
	\$ 	(207) 78,235 - - - - - - - - - - - - - - - - - - -	$\begin{array}{c ccccccccccccccccccccccccccccccccccc$	$\begin{array}{c ccccccccccccccccccccccccccccccccccc$	$\begin{array}{c ccccccccccccccccccccccccccccccccccc$	$\begin{array}{c cccccc} & & & & & & & & & & & & & & & & $	$\begin{array}{c ccccccccccccccccccccccccccccccccccc$	$\begin{array}{c ccccccccccccccccccccccccccccccccccc$	$\begin{array}{c ccccccccccccccccccccccccccccccccccc$



#### Schedule of Revenues, Expenditures and Changes in Fund Balance as of June 30, 2018 (Unaudited) Schedule 3

#### (Unaudited)

		Net Revenues	<b>T</b> _4-1
Project	Description	through June 30, 2018	Total Net Revenues
Filipeci	(G)	(H)	(l)
	(\$) (\$ in thousands)	(11)	(1)
	Freeways (43% of Net Revenues)		
А	I-5 Santa Ana Freeway Interchange Improvements \$	77,366	\$ 486,905
В	I-5 Santa Ana/SR-55 to El Toro	49,416	310,998
С	I-5 San Diego/South of El Toro	103,210	649,552
D	I-5 Santa Ana/San Diego Interchange Upgrades	42,469	267,280
E	SR-22 Garden Grove Freeway Access Improvements	19,753	124,316
F	SR-55 Costa Mesa Freeway Improvements	60,247	379,165
G	SR-57 Orange Freeway Improvements	42,584	268,005
Н	SR-91 Improvements from I-5 to SR-57	23,045	145,036
I	SR-91 Improvements from SR-57 to SR-55	68,560	431,481
J	SR-91 Improvements from SR-55 to County Line	57,975	364,868
K	I-405 Improvements between I-605 to SR-55	176,593	1,111,387
L	I-405 Improvements between SR-55 to I-5	52,626	331,199
Μ	I-605 Freeway Access Improvements	3,292	20,719
N	All Freeway Service Patrol	24,691	155,395
	Freeway Mitigation	42,201	265,595
	Subtotal Projects	844,028	5,311,901
	Net (Bond Revenue)/Debt Service	-	
	Total Freeways\$	844,028	\$ 5,311,901

#### Street and Roads Projects (32% of Net Revenues)

O P Q	Regional Capacity Program Regional Traffic Signal Synchronization Program Local Fair Share Program	\$ 196,289 78,512 353,314	\$ 1,235,342 494,115 2,223,587
	Subtotal Projects Net (Bond Revenue)/Debt Service	 628,115 -	 3,953,044 -
	Total Street and Roads Projects %	\$ 628,115	\$ 3,953,044



Expenditures through June 30, 2018 <i>(J)</i>		imbursement through une 30, 2018 <i>(K)</i>	s	Net M2 Cost (L)
\$ 6,394 8,895 121,314 1,915 4 14,498 49,499 34,753 21,351 6,934 331,301 8,839 1,899 2,243 51,512	\$	2,322 5,706 45,329 527 - 1,437 11,812 824 5,202 5,294 28,063 6,496 16 - 2,477	\$	4,072 3,189 75,985 1,388 4 13,061 37,687 33,929 16,149 1,640 303,238 2,343 1,883 2,243 49,035
 661,351 40,154		115,505		545,846 40,154
\$ 701,505	\$	115,505	\$	586,000 39.0%
\$ 707,430 48,246 343,873 1,099,549 44,599	\$	435,583 5,017 77 440,677 -	\$	271,847 43,229 343,796 658,872 44,599
\$ 1,144,148	\$	440,677	\$	703,471 46.9%



Project	t Description (G) (\$ in thousands) Transit Projects (25% of Net Reve		Net Revenues through June 30, 2018		Total Net Revenues		
			(H) )		(1)		
R S	High Frequency Metrolink Service Transit Extensions to Metrolink	\$	183,177 173,275	\$	1,232,055 1,090,507		
T U	Metrolink Gateways Expand Mobility Choices for Seniors and Persons with Disabilities		28,388 62,296		63,140 428,351		
V W	Community Based Transit/Circulators Safe Transit Stops		39,247 4,332		247,000 27,263		
	Subtotal Projects Net (Bond Revenue)/Debt Service		490,715 -		3,088,316 -		
	Total Transit Projects %	\$	490,715	\$	3,088,316		
	Measure M2 Program	\$	1,962,858	\$	12,353,261		
	Environmental Cleanup (2% of Rev	venue	s)				
x	Clean Up Highway and Street Runoff that Pollutes Beaches	\$	42,021	\$	264,609		
	Net (Bond Revenue)/Debt Service		-		-		
	Total Environmental Cleanup %	\$	42,021	\$	264,609		
	Taxpayer Safeguards and Aud	lits					
	Collect Sales Taxes (1.5% of Sales Taxes) %	\$	31,134	\$	195,562		
	Oversight and Annual Audits (1% of Revenues) %	\$	21,010	\$	132,305		



	Expenditures through	Net			
	June 30, 2018		through June 30, 2018		M2 Cost
	(J)		(K)		(L)
\$	167,772	\$	99,455	\$	68,317
,	17,542		2,133	•	15,409
	98,213		60,956		37,257
	00,210		00,000		01,201
	60,008		88		59,920
	5,806		455		5,351
	275		26		249
	349,616 24,943		163,113 -		186,503 24,943
	,				,
\$	374,559	\$	163,113	\$	211,446
_	· · · · ·	-			14.1%
\$	2,220,212	\$	719,295	\$	1,500,917
\$	34,717	\$	- 292	\$	34,425
\$	34,717	\$	292	\$	34,425
					1.6%
*	04.005	ć			04.005
\$	21,965	\$	-	\$	21,965
					1.1%
\$	22,560	\$	1,550	\$	21,010
·	,	÷	,	<u> </u>	1.0%



M2 Funds							
ENTITY	4th Quarter	FUNDS TO DATE					
	FY 2017-18						
ALISO VIEJO	\$223,973	\$4,266,149					
ANAHEIM	\$1,909,549	\$37,124,176					
BREA	\$315,963	\$6,175,390					
BUENA PARK	\$464,596	\$9,740,325					
COSTA MESA	\$816,704	\$15,624,242					
CYPRESS	\$271,284	\$5,731,553					
DANA POINT	\$187,117	\$3,546,188					
FOUNTAIN VALLEY	\$328,089	\$6,712,558					
FULLERTON	\$703,069	\$14,017,382					
GARDEN GROVE	\$798,215	\$16,054,068					
HUNTINGTON BEACH	\$1,054,925	\$20,909,103					
IRVINE	\$1,517,031	\$28,712,778					
LAGUNA BEACH	\$139,749	\$2,749,674					
LAGUNA HILLS	\$185,795	\$3,675,695					
LAGUNA NIGUEL	\$353,435	\$7,213,071					
LAGUNA WOODS	\$67,856	\$1,379,361					
LA HABRA	\$277,293	\$5,685,714					
LAKE FOREST	\$441,887	\$8,490,939					

# LOCAL FAIR SHARE

M2 Funds							
ENTITY	4th Quarter	FUNDS TO DATE					
LA PALMA	<b>FY 2017-18</b> \$85,701	\$1,816,602					
LOS ALAMITOS	\$70,494	\$1,397,788					
MISSION VIEJO	\$513,203	\$10,108,562					
NEWPORT BEACH	\$605,966	\$11,836,238					
ORANGE	\$906,822	\$17,741,743					
PLACENTIA	\$260,220	\$5,123,747					
RANCHO SANTA MARGARITA	\$229,040	\$4,570,026					
SAN CLEMENTE	\$316,489	\$6,031,962					
SAN JUAN CAPISTRANO	\$199,729	\$4,085,956					
SANTA ANA	\$1,530,578	\$29,981,931					
SEAL BEACH	\$131,696	\$2,726,186					
STANTON	\$161,627	\$3,242,006					
TUSTIN	\$489,059	\$9,607,158					
VILLA PARK	\$28,518	\$563,062					
WESTMINSTER	\$470,677	\$9,226,639					
YORBA LINDA	\$324,035	\$6,463,727					
COUNTY UNINCORPORATED	\$1,101,329	\$20,023,276					
TOTAL M2 FUNDS	\$17,481,713	\$342,354,972					



CAPITAL ACTION PLAN

Grey = Milestone achieved Green = Forecast milestone meets or exceeds plan Yellow = Forecast milestone is one to three months later than plan Red = Forecast milestone is over three months later than plan Non-bolded = Planned/Baseline Bold = Forecasted/Actual

Capital Projects	<b>Cost</b> Baseline/	Schedule Plan/Forecast					
	Forecast (millions)	Begin Environmental	Begin Design	Begin Construction	Complete Construction		
Freeway Projects:							
I-5, SR-55 to SR-57	\$38.1	Jul-11	Jun-15	Dec-17	Feb-20		
Project A	\$41.7	Jun-11	Jun-15	Nov-18	Jan-21		
I-5, I-405 to SR-55	TBD	May-14	TBD	TBD	TBD		
Project B	TBD	May-14	TBD	TBD	TBD		
I-5, Pico to Vista Hermosa	\$113.0	Jun-09	Jun-11	Dec-14	Aug-18		
Project C	\$85.9	Jun-09	Jun-11	Dec-14	Jul-18		
I-5, Vista Hermosa to Pacific Coast Highway	\$75.6	Jun-09	Jun-11	Dec-13	Mar-17		
Project C	\$71.4	Jun-09	Jun-11	Jun-14	Jul-17		
I-5, Pacific Coast Highway to San Juan Creek Road	\$70.7	Jun-09	Jun-11	Oct-13	Sep-16		
Project C	\$71.2	Jun-09	Jun-11	Dec-13	Jul-18		
I-5, SR-73 to Oso Parkway	\$151.9	Sep-11	Mar-15	Dec-18	Jan-24		
Project C & D Cost/Schedule Risk	\$188.1	Oct-11	Mar-15	Nov-19	Dec-24		
I-5, Oso Parkway to Alicia Parkway	\$196.2	Sep-11	Nov-14	Jun-18	Feb-23		
Project C & D Cost/Schedule Risk	\$188.6	Oct-11	Nov-14	Jan-19	Oct-23		
I-5, Alicia Parkway to El Toro Road	\$133.6	Sep-11	Mar-15	May-19	Jun-23		
Project C Cost/Schedule Risk	\$164.2	Oct-11	Mar-15	Jun-20	Jun-24		
I-5, SR-73 to El Toro Road (Landscape)	TBD	N/A	TBD	TBD	TBD		
Project C Cost/Schedule Risk	\$12.4	N/A	Jan-22	Jun-24	Dec-25		
I-5, I-5/Ortega Interchange	\$90.9	Sep-05	Jan-09	Aug-12	Sep-15		
Project D	\$75.2	Sep-05	Jan-09	Aug-12	Jan-16		

# CAPITAL ACTION PLAN

Grey = Milestone achieved Green = Forecast milestone meets or exceeds plan Yellow = Forecast milestone is one to three months later than plan Red = Forecast milestone is over three months later than plan Non-bolded = Planned/Baseline **Bold = Forecasted/Actual** 

Capital Projects	<b>Cost</b> Baseline/	Schedule Plan/Forecast					
	Forecast (millions)	Begin Environmental	Begin Design	Begin Construction	Complete Construction		
I-5, I-5/Ortega Interchange (Landscape)	N/A	N/A	N/A	N/A	N/A		
Project D	N/A	N/A	Jan-14	Sep-15	Sep-16		
I-5, I-5/El Toro Road Interchange	TBD	Apr-17	TBD	TBD	TBD		
Project D	TBD	Apr-17	TBD	TBD	TBD		
SR-55, I-405 to I-5 Cost/Schedule Risk	\$410.9	Feb-11	Sep-17	Jul-21	Aug-25		
Project F Cost/Schedule Risk	\$410.9	May-11	Sep-17	Jul-21	Aug-25		
SR-55, I-5 to SR-91	TBD	Dec-16	TBD	TBD	TBD		
Project F	TBD	Dec-16	TBD	TBD	TBD		
SR-57 Northbound (NB), Orangewood Avenue to Katella Avenue	TBD	Apr-16	TBD	TBD	TBD		
Project G	TBD	Apr-16	TBD	TBD	TBD		
SR-57 (NB), Katella Avenue to Lincoln Avenue	\$78.7	Apr-08	Jul-08	Aug-11	Sep-14		
Project G	\$38.0	Apr-08	Aug-08	Oct-11	Apr-15		
SR-57 (NB), Katella Avenue to Lincoln Avenue (Landscape)	N/A	N/A	N/A	N/A	N/A		
Project G	N/A	N/A	May-09	Sep-17	Jun-18		
SR-57 (NB), Orangethorpe Avenue to Yorba Linda Boulevard	\$80.2	Aug-05	Feb-08	Oct-10	May-14		
Project G	\$52.3	Aug-05	Feb-08	Oct-10	Nov-14		
SR-57 (NB), Yorba Linda Boulevard to Lambert Road	\$79.3	Aug-05	Feb-08	Oct-10	Sep-14		
Project G	\$54.1	Aug-05	Feb-08	Oct-10	May-14		
SR-57 (NB), Orangethorpe Avenue to Lambert Road (Landscape)	N/A	N/A	N/A	N/A	N/A		
Project G	N/A	N/A	Oct-14	Feb-18	Apr-19		

110

# CAPITAL ACTION PLAN

Grey = Milestone achieved Green = Forecast milestone meets or exceeds plan Yellow = Forecast milestone is one to three months later than plan Red = Forecast milestone is over three months later than plan Non-bolded = Planned/Baseline Bold = Forecasted/Actual

Capital Projects	<b>Cost</b> Baseline/	<b>Schedule</b> Plan/Forecast					
	Forecast (millions)	Begin Environmental	Begin Design	Begin Construction	Complete Construction		
SR-57 (NB), Lambert Road to Tonner Canyon	TBD	TBD	TBD	TBD	TBD		
Project G	TBD	Jul-20	TBD	TBD	TBD		
SR-91 Westbound (WB), I-5 to SR-57	\$78.1	Jul-07	Oct-09	Nov-12	Apr-16		
Project H	\$59.0	Jul-07	Mar-10	Jan-13	Jun-16		
SR-91 Westbound (WB), I-5 to SR-57 (Landscape)	N/A	N/A	N/A	N/A	N/A		
Project H	N/A	N/A	Nov-14	Mar-17	Nov-17		
SR-91, SR-57 to SR-55	TBD	Jan-15	TBD	TBD	TBD		
Project I Cost/Schedule Risk	TBD	Jan-15	TBD	TBD	TBD		
SR-91 (WB), Tustin Interchange to SR-55	\$49.9	Jul-08	Jul-11	Oct-13	Jul-16		
Project I	\$42.6	Jul-08	Jun-11	Oct-13	Jul-16		
SR-91, SR-55 to SR-241	\$128.4	Jul-07	Jun-09	Sep-11	Dec-12		
Project J	\$79.7	Jul-07	Apr-09	May-11	Mar-13		
SR-91, SR-55 to SR-241 (Landscape)	N/A	N/A	N/A	N/A	N/A		
Project J	N/A	N/A	May-12	Oct-13	Feb-15		
SR-91 Eastbound, SR-241 to SR-71	\$104.5	Mar-05	Jul-07	Jul-09	Nov-10		
Project J	\$57.8	Mar-05	Jul-07	Aug-09	Jan-11		
I-405, I-5 to SR-55	TBD	Dec-14	TBD	TBD	TBD		
Project L	TBD	Dec-14	TBD	TBD	TBD		
I-405, SR-55 to I-605 (Design-Build)	\$1,900.0	Mar-09	Mar-14	Nov-16	May-23		
Project K	\$1,900.0	Mar-09	Mar-14	Nov-16	May-23		

51



Grey = Milestone achieved Green = Forecast milestone meets or exceeds plan Yellow = Forecast milestone is one to three months later than plan Red = Forecast milestone is over three months later than plan Non-bolded = Planned/Baseline Bold = Forecasted/Actual

Capital Projects	<b>Cost</b> Baseline/	<b>Schedule</b> Plan/Forecast					
	Forecast (millions)	Begin Environmental	Begin Design	Begin Construction	Complete Construction		
I-605, I-605/Katella Interchange	TBD	Aug-16	TBD	TBD	TBD		
Project M	TBD	Aug-16	TBD	TBD	TBD		
Grade Separation Projects:							
Raymond Avenue Railroad Grade Separation	\$77.2	Feb-09	Mar-10	May-13	Aug-18		
Project O	\$128.4	Feb-09	Mar-10	Feb-14	May-18		
State College Boulevard Railroad Grade Separation (Fullerton)	\$73.6	Dec-08	Jul-06	May-13	May-18		
Project O	\$97.0	Dec-08	Jul-06	Feb-14	Jan-18		
Placentia Avenue Railroad Grade Separation	\$78.2	Jan-01	Jan-09	Jun-11	Nov-14		
Project O	\$64.5	Jan-01	Jan-09	Jul-11	Dec-14		
Kraemer Boulevard Railroad Grade Separation	\$70.4	Jan-01	Jan-09	Aug-11	Oct-14		
Project O	\$63.8	Jan-01	Feb-09	Sep-11	Dec-14		
Orangethorpe Avenue Railroad Grade Separation	\$117.4	Jan-01	Feb-09	May-12	Sep-16		
Project O	\$108.6	Jan-01	Feb-09	Jan-13	Oct-16		
Tustin Avenue/Rose Drive Railroad Grade Separation	\$103.0	Jan-01	Feb-09	Aug-12	May-16		
Project O	\$98.3	Jan-01	Feb-09	Feb-13	Oct-16		
Lakeview Avenue Railroad Grade Separation	\$70.2	Jan-01	Feb-09	May-13	Mar-17		
Project O	\$110.6	Jan-01	Feb-09	Nov-13	Jun-17		
Sand Canyon Avenue Railroad Grade Separation	\$55.6	N/A	Jan-04	Feb-11	May-14		
Project R	\$61.9	N/A	Jan-04	Feb-11	Jan-16		
17th Street Railroad Grade Separation	TBD	Oct-14	TBD	TBD	TBD		
Project R	TBD	Oct-14	TBD	TBD	TBD		

\*Status through June 2018. For detailed project information, please refer to the individual project section within this report.




Grey = Milestone achieved Green = Forecast milestone meets or exceeds plan Yellow = Forecast milestone is one to three months later than plan Red = Forecast milestone is over three months later than plan Non-bolded = Planned/Baseline Bold = Forecasted/Actual

Capital Projects		<b>Cost</b> Baseline/	Schedule Plan/Forecast			
		Forecast (millions)	Begin Environmental	Begin Design	Begin Construction	Complete Construction
Rail and Station Projects	5:					
Rail-Highway Grade Crossing Safety Enhancement		\$94.4	Jan-08	Jan-08	Aug-09	Dec-11
Project R		\$90.4	Jan-08	Jan-08	Aug-09	Dec-11
San Clemente Beach Trail Safety Enhancements		\$6.0	Sep-10	Feb-12	Oct-12	Jan-14
Project R		\$5.0	Sep-10	Feb-12	May-13	Mar-14
San Juan Capistrano Passing Siding		\$25.3	Aug-11	Mar-15	Dec-16	Jan-19
		\$30.8	Aug-11	Mar-15	Jan-19	Feb-21
Placentia Metrolink Station ar	nd Parking Structure	\$34.8	Jan-03	Oct-08	TBD	TBD
Project R	Cost/Schedule Risk	\$34.8	Jan-03	Oct-08	May-19	Jan-21
Anaheim Canyon Station		\$27.9	Jan-16	Mar-19	Nov-19	Mar-21
		\$27.9	Jan-16	Mar-18	Nov-19	Mar-21
Orange Station Parking Expansion		\$33.2	Dec-09	Nov-10	Nov-16	Feb-19
		\$32.3	Dec-09	Nov-10	Jun-17	Feb-19
Fullerton Transportation Center - Elevator Upgrades Cost/Schedule Risk		\$3.5	N/A	Jan-12	Sep-14	Mar-17
		\$4.6	N/A	Jan-12	Apr-15	Dec-18
Laguna Niguel/Mission Viejo Station ADA Ramps		\$3.5	Jul-13	Jul-13	Jan-15	Apr-17
		\$5.2	Jul-13	Jul-13	Oct-15	Sep-17
Anaheim Regional Transportation Intermodal Center		\$227.4	Apr-09	Jun-09	Jul-12	Nov-14
Project R & T	Cost/Schedule Risk	\$232.2	Apr-09	Jun-09	Sep-12	Dec-14
OC Streetcar		\$310.4	Aug-09	Feb-16	Aug-18	Aug-21
Project S	Cost/Schedule Risk	\$418.9	Aug-09	Feb-16	Aug-18	Aug-21

\*Status through June 2018. For detailed project information, please refer to the individual project section within this report.

53

This Page Intentionally Left Blank

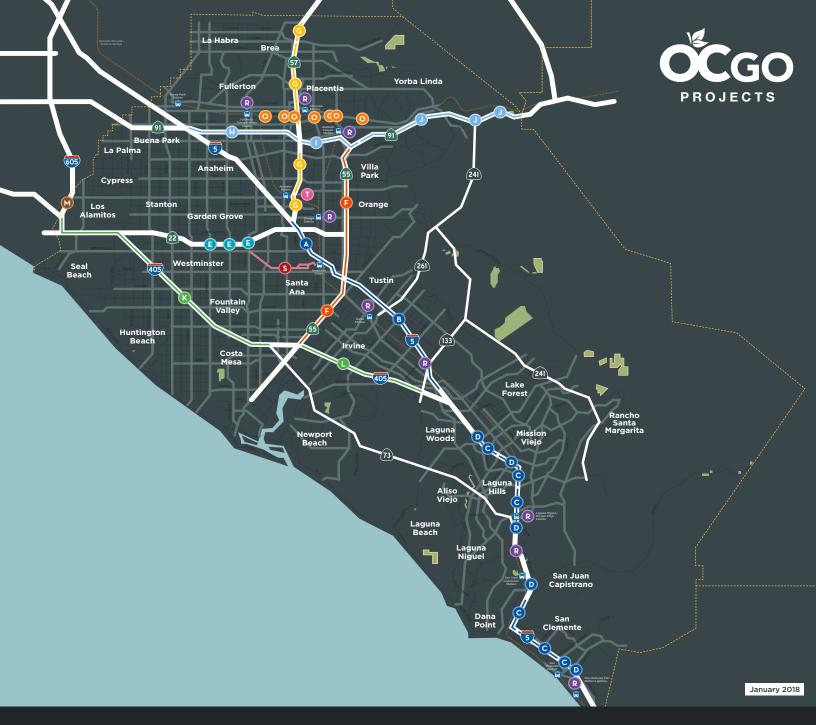

#### FREEWAY IMPROVEMENT PROGRAM

#### Interstate 5 (I-5) Projects

- (A) I-5, SR-55 to SR-57
- B I-5, El Toro "Y" Area to SR-55
- C I-5, SR-73 to El Toro Road
- C I-5, Avenida Pico to San Juan Creek Road
- D I-5 Highway Interchanges

#### State Route 22 (SR-22) Projects

**E** SR-22 Access Improvements

#### State Route 55 (SR-55) Projects

**SR-55**, I-405 to I-5 **SR-55**, I-5 to SR-91

#### State Route 57 (SR-57) Projects

- G SR-57 NB, Orangewood Avenue to Katella Avenue
- 🜀 SR-57 NB, Katella Avenue to Lincoln Avenue
- SR-57 NB, Orangethorpe Avenue to Lambert Road
- G SR-57 NB, Lambert Road to Tonner Canyon Road

- State Route 91 (SR-91) Projects
- 🕕 SR-91 WB, I-5 to SR-57
- **SR-91**, SR-57 to SR-55
- SR-91, SR-55 to Riverside County Line

Interstate 405 (I-405) Projects

L I-405, SR-55 to El Toro "Y" Area

#### Interstate 605 (I-605) Projects

- I-605 Katella Interchange Improvements
- Freeway Mitigation Restoration Projects Part of Projects A-M
- Freeway Mitigation Acquisition Projects Part of Projects A-M

## **STREETS & ROADS**

Grade Separation Program (shown)
 Signal Synchronization Project Corridors

#### TRANSIT PROJECTS

- **R** Grade Separation and Station Improvement Projects
- S Transit Extensions to Metrolink
- Metrolink Station Conversion to accept Future High-Speed Rail Systems

#### OC GO PROJECTS NOT SHOWN

Project N: Freeway Service Patrol Project O: Streets & Roads -Regional Capacity Program Project Q: Local Fair Share Program

Project R: Grade crossing and Trail Safety Enhancements Project U: Senior Mobility Program (SMP), Senior Non-emergency Medical Transportation Program (SNEMT), and Fare Stabilization Programs Project V: Community Based Transit/Circulators Project W: Safe Transit Stops Project X: Environmental Cleanup Program
