



# **MEASURE M2 QUARTERLY** PROGRESS REPORT

First Quarter of Fiscal Year 2025–26 July 1, 2025 through September 30, 2025

### First Quarter Highlights:

- Freeway Projects
- Streets and Roads
- Environmental Cleanup & Water Quality
  Freeway Mitigation Program
  Finance Matters

- Program Management OfficeSummary






#### **SUMMARY**

On November 7, 2006, Orange County voters, by a margin of nearly 70 percent, approved the Renewed Measure M (M2) Transportation Investment Plan (Plan), a one-half cent sales tax for transportation improvements. Voters originally endorsed Measure M (M1) in 1990 with a sunset in 2011. The renewal of Measure M continues the investment of local tax dollars in Orange County's transportation infrastructure for another 30 years to 2041.

As required by M2 Ordinance No. 3 (M2 Ordinance), a quarterly report covering activities from July 1, 2025, through September 30, 2025, is provided to update progress in implementing the Plan. To be cost-effective and to facilitate accessibility and transparency of information to stakeholders and the public, M2 progress reports are available on the OCTA website.



The cover photo shows the Laguna Beach Trolley in the City of Laguna Beach. This project is funded through the Community-Based Transit Circulators Program (Project V). On August 25, 2025, the Board received a biannual ridership report update, which highlighted that all active services met the ridership and service performance standards.



# MEASURE M2 PROGRESS REPORT

#### TABLE OF CONTENTS Section **Project Page Project Schedules M2** Delivery Risk Update 1 **Next 10 Delivery Plan Update** 4 Freeway Program (Projects A-N) 9 9 Interstate 5 (I-5) Projects [A-D] State Route 22 (SR-22) Projects 13 [E] State Route 55 (SR-55) Projects [F] 13 State Route 57 (SR-57) Projects [G] 14 State Route 91 (SR-91) Projects [H-J] 16 Interstate 405 (I-405) Projects [K-L] 19 20 Interstate 605 (I-605) Projects [M] Freeway Service Patrol 21 [N] Streets and Roads Programs (Projects O, P and Q) 22 Regional Capacity Program and OC Bridges Railroad Program [0] 22 Regional Traffic Signal Synchronization Program [P] 24 Local Fair Share Program [Q] 25 **Transit Programs (Projects R, S, T, U, V and W)** 27 High Frequency Metrolink Service 27 [R] Transit Extensions to Metrolink 32 [S] Metrolink Gateways 33 [T]Expand Mobility Choices for Seniors and Persons with Disabilities <u>34</u> [U] Community Based Transit/Circulators [V] 35 Safe Transit Stops [W] 36 **Environmental Programs (Project X and Freeway Mitigation Program)** 37 **Environmental Cleanup** [X] 37 Freeway Mitigation Program (part of Projects A - M) 38 **Program Management Office** <u>41</u> M2 Financing and Schedule of Funding 47 **Local Fair Share - M2 Funding by Agency** 51 **Capital Action Plan - Capital Project Status** 53 **Common Abbreviations** <u>59</u>















Conceptual


Environmental

Design, Advertise, & Award

Design-Build

Construction


Complete

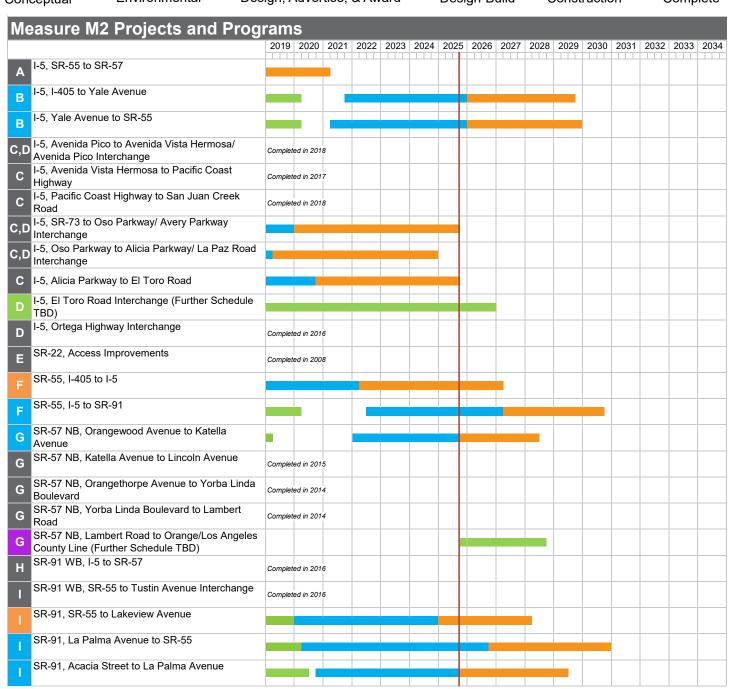

Project schedules are based on phase start dates. Shown schedules are subject to change.

For full project schedules, see <a href="https://octa.net/programs-projects/programs/oc-go-measure-m/">https://octa.net/programs-projects/programs/oc-go-measure-m/</a>
<a href="https://octa.net/programs-projects/programs/oc-go-measure-m/">https://octa.net/programs-projects/programs/oc-go-measure-m/</a>
<a href="https://octa.net/programs-projects/programs/oc-go-measure-m/">https://octa.net/programs-projects/programs/oc-go-measure-m/</a>
<a href="https://octa.net/programs-projects/programs/oc-go-measure-m/">https://octa.net/programs-projects/programs/oc-go-measure-m/</a>
<a href="https://octa.net/programs-projects/programs/oc-go-measure-m/">https://octa.net/programs-projects/programs/oc-go-measure-m/</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/projects/#/schedule</a>
<a href="https://octa.net/projects/#/schedule</a>
<a href="https://octa.net/projects/#/schedule</a>
<a href="https://octa.net/projects/#/schedule</a>
<a href="https://octa.net/projects/#/schedul

<sup>&</sup>lt;sup>1</sup> Projects managed by local agencies

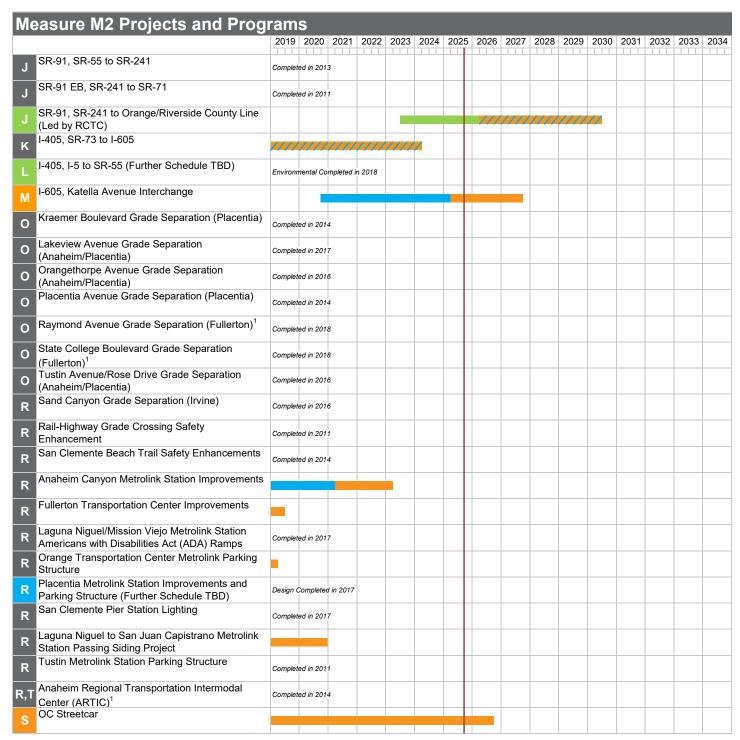

Project schedules are based on phase start dates. Shown schedules are subject to change.

For full project schedules, see <a href="https://octa.net/programs-projects/programs/oc-go-measure-m/">https://octa.net/programs-projects/programs/oc-go-measure-m/</a>
<a href="https://octa.net/programs-projects/programs/oc-go-measure-m/">https://octa.net/programs-projects/programs/oc-go-measure-m/</a>
<a href="https://octa.net/programs-projects/programs/oc-go-measure-m/">https://octa.net/programs-projects/programs/oc-go-measure-m/</a>
<a href="https://octa.net/programs-projects/programs/oc-go-measure-m/">https://octa.net/programs-projects/programs/oc-go-measure-m/</a>
<a href="https://octa.net/programs-projects/programs/oc-go-measure-m/">https://octa.net/programs-projects/programs/oc-go-measure-m/</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/programs-projects/#/schedule">https://octa.net/programs-projects/#/schedule</a>
<a href="https://octa.net/projects/#/schedule</a>
<a href="https://octa.ne

<sup>&</sup>lt;sup>1</sup> Projects managed by local agencies



### M2 DELIVERY RISK UPDATE ▼

This section discusses the risks and challenges related to Measure M2 and the updated Next 10 Delivery Plan (Next 10 Plan) that the M2 Program Management Office (PMO) is monitoring with associated explanations and proposed actions.

Deli	very Risk	Explanation	Proposed Action
Fina	ancial		
1	by economic conditions. The 2024 M2 revenue forecast is \$14 billion, which is a \$800 million (-5.4 percent)	revenue forecast is lower, in most areas of the M2 Plan, programs can be scaled to available	The 2025 M2 sales tax revenue forecast is anticipated to be presented to the Board in October 2025. Staff will continue to monitor sales tax revenue receipts to ensure that M2 is delivered as promised to voters.
2	Reduced external funding opportunities for the M2 freeway program.	State and federal priorities continue to shift and favor projects that reduce automobile travel, which could affect access to currently programmed as well as future external funding opportunities for the M2 freeway projects.	Current external funding commitments are assumed in the M2 cash flow for the 2024 Next 10 Plan, but prospects of future revenues for highway projects are low.
3	Potential for an environment of increasing cost for M2 capital projects.	the Next 10 Plan Market Conditions Forecast and Risk Analysis anticipates moderate inflationary pressures in 2025, 2026, and 2027. This is due to declining building permits, rising	project costs. The next update is anticipated in October 2025 and will be incorporated into the 2025 update of the Next 10 Plan.



Delivery Risk		Explanation	Proposed Action
4	Schedule and scope changes on capital projects that impact delivery and project costs.	Changes as a result of updated highway standards, new regulatory requirements, or issues identified in the field may impact scope, schedule, and costs substantially.	OCTA will work closely with project partners and project contractors to limit changes in scope and schedules.
5	Increase Southern California Regional Rail Authority (Metrolink) train service as an alternative to driving within the limits of available revenue.	The coronavirus (COVID-19) altered travel behavior, which has affected ridership and farebox revenues. The cost of Metrolink service continues to grow as contracted rates increase, the system ages, track-sharing arrangements with BNSF Railway Company (BNSF) are revised, and new air quality requirements are implemented.	0 (
Res	ource		
6	Substantial work underway in the region has resulted in significant demand for professional and skilled labor which may impact delivery given the volume of the M2 capital program.	The spring 2025 update of the Next 10 Plan Market Conditions Forecast and Risk Analysis reflects an increase in unemployment rates. This may ease labor market pressures and reduce delivery risk. However, wildfires devastated communities in Los Angeles, and as a result, the availability of professional and skilled labor may be redirected toward rebuilding efforts in the area.	OCTA will monitor resources for professional and skilled labor needed for project delivery. Expert and timely coordination between OCTA and project partners is imperative to manage this risk.



D	elivery Risk	Explanation	Proposed Action
7	New operational responsibilities with the OC Streetcar.	With the implementation of the OC Streetcar service, OCTA will be increasing its overall role in operations.	To ensure the success of the OC Streetcar, OCTA hired a streetcar operations manager with proven start-up experience to oversee start-up and daily operations. A contractor with extensive experience in operations of rail systems was selected to handle the startup and revenue operation phases.
C	imate		
8	Climate-related hazards could affect M2 investments.	OCTA has experienced hazards affecting M2 investments. Wildfires present a continual risk to the M2 Environmental Mitigation Program (EMP) Preserves and resoration projects that have not been completed and approved by the United States Fish and Wildlife Service (USFWS) and the California Department of Fish and Wildlife (CDFW) (collectively, Wildlife Agencies). In addition, tidal events, ocean currents and waves, storm surges, and slope movement affect OCTA's railroad track in the south Orange County.	Plans (FMP) for the seven properties purchased as part of the M2 Freeway EMP. Additionally, OCTA has initiated a planning study to identify immediate as well as short- and medium-
R	egulatory		
g	Changing federal and state directives could affect M2 freeway project approvals.	approval policies place great	could impact delivery.



### **NEXT 10 DELIVERY PLAN**

Contact: Francesca Ching, M2 PMO Manager • (714) 560-5625

The Next 10 Plan sets priorities and funding commitments over a ten-year period, providing guidance to staff on the delivery of M2 projects and programs. Annually, staff reviews the Board-adopted commitments in the Next 10 Plan to ensure it remains deliverable with updated revenues and project costs.

On November 12, 2024, the Board adopted the 2024 Next 10 Plan, which spans fiscal year (FY) 2024-25 through FY 2033-34. The update incorporated the \$14 billion sales tax revenue forecast, revised project estimates and schedules, as well as the fall market conditions forecast and risk analysis. As a result of OCTA's strategic planning to date, the 2024 Next 10 Plan continues to demonstrate that the Plan remains deliverable.

#### **Next 10 Plan Deliverables**

Significant progress continues with projects in and advancing towards construction, as well as regular funding allocations to local jurisdictions through local programs.

#### 1. Deliver 13 freeway improvement projects through construction (Projects A-M).

The M2 Freeway Program is currently made up of 30 projects/project segments. This deliverable includes 13 projects to be delivered through construction by FY 2029-30. Of the 13 projects to be delivered, three have been completed, three are in construction, six are in final design, and a joint project with the Riverside County Transportation Commission (RCTC), is in environmental revalidation. The joint project will improve SR-91 between SR-241 and SR-71. Completion of these projects will bring the total number of completed projects to 27 by 2030, which equates to approximately 90 percent of the M2 Freeway Program. For more details, see pages i-ii (Project Schedules) and the project updates contained in their respective sections.

#### Upcoming activities:

- SR-57 Northbound, Orangewood Avenue to Katella Avenue Begin Construction
- SR-91, Acacia Street to La Palma Avenue Award Construction Contract
- I-5, I-405 to Yale Avenue Award Construction Contract
- I-5, Yale Avenue to SR-55 Award Construction Contract
- SR-91, La Palma Avenue to SR-55 Advertise for Construction
- SR-91 Eastbound Corridor Operations Project Advertise for Progressive Design-Build Construction



#### 2. Prepare remaining freeway improvement projects for delivery (Projects A-M).

The three remaining projects (of the 30 total) are environmentally cleared or on track to be environmentally cleared by 2034, making them shelf-ready for further advancement. The remaining projects include Project D (I-5, El Toro Road Interchange), Project G (SR-57 northbound from Lambert Road to Orange/Los Angeles County Line), and Project L (I-405 between I-5 and SR-55). These projects will continue to be reevaluated for earlier delivery as part of the annual Next 10 Plan review. For more details, see pages i-ii (Project Schedules) and the project updates contained in their respective sections.

3. Provide annual competitive funding opportunities for local jurisdictions to address bottlenecks and gaps in the street system (Project O), synchronize signals (Project P), and continue flexible funding to local jurisdictions to support pavement rehabilitation or other transportation needs as appropriate (Project Q).

As of September 2025, OCTA has awarded approximately \$594.4 million in competitive funding through the Regional Capacity Program (RCP) (Project O) and Regional Traffic Signal Synchronization Program (RTSSP) (Project P) annual calls. Additionally, approximately \$823.0 million<sup>1,2</sup> in Local Fair Share (LFS) (Project Q) funds have been distributed to local jurisdictions.

On September 8, 2025, the Board authorized the 16th call for projects (call) to support local streets and roads improvement projects throughout Orange County. Applications are due on November 20, 2025. Based on the project selection criteria in the Comprehensive Transportation Funding Program (CTFP) guidelines, projects will be prioritized for Board consideration in spring 2026. For more details, see the project updates on page 22 and page 24.

#### **Upcoming activities:**

Project O and P – 16th call open

#### 4. Maintain Metrolink service (Project R).

Project R provides funding for Metrolink operations and aims to increase rail services within the County and provide additional Metrolink service north of the City of Fullerton to the Los Angeles County Line. The program also provides for track improvements, the addition of trains and parking capacity, upgraded stations, and safety enhancements to allow cities to establish quiet zones along the tracks.

<sup>&</sup>lt;sup>1</sup> Only includes disbursed funds. On May 28, 2024, the Board determined the City of Buena Park ineligible to receive net M2 revenues for five years pursuant to Section 10.4 of the M2 Ordinance. Disbursements of net M2 revenues have been suspended until the City of Buena Park reestablishes eligibility.

<sup>&</sup>lt;sup>2</sup> On May 12, 2025, the Board determined the City of Huntington Beach ineligible to receive net M2 revenues for five years pursuant to Section 10.4 of the M2 Ordinance. Disbursements of net M2 revenues have been suspended until the City of Huntington Beach reestablishes eligibility.



Close monitoring of Metrolink operations is necessary to ensure sustainability through 2041. Metrolink ridership recovery continues to struggle, which impacts farebox revenues and cost recovery. To exacerbate this shortfall, operating costs have also increased. On October 21, 2024, Metrolink implemented a service optimization schedule aimed at addressing service gaps and making the most efficient use of equipment and crews as Metrolink adjusts the focus from commuter rail to regional rail. As such, the three lines serving Orange County (Orange County, Inland Empire-Orange County, and the 91/Perris Valley lines) now operate 58 trains, a 29 percent increase from the 45 weekday trains previously serving Orange County. Without this funding or changes in service levels, ridership growth, or operations and rehabilitation costs, current projections with the addition of Transit and Intercity Rail Program (TIRCP) formula funds will only sustain Metrolink operations through FY 2035-36. OCTA will continue to actively engage with Metrolink and the other member agencies to monitor ridership levels and the financial impacts to M2. For more details, see project updates on page 27.

Railroad track stabilization efforts in south Orange County have become a major focus area given its importance to continued operation of Metrolink in Orange County. While the rail line is currently open as a result of ongoing emergency work, longer-term solutions must be developed to ensure the ability to provide reliable rail service in this portion of the County. In partnership with key stakeholders, a planning study is currently underway to identify and evaluate immediate as well as short- and medium-term solutions with the goal of protecting the rail line in place for approximatively the next 30 years. A separate long-term study will assess potential long-term solutions, which may include relocation of the rail line. The California State Transportation Agency has committed to lead the long-term study to plan for future investments necessary to ensure a resilient Los Angeles—San Diego—San Luis Obispo (LOSSAN) corridor. As these studies progress, future updates to the Next 10 Plan will incorporate more current information. For more details, see the project updates on page 29.

5. Complete construction, secure vehicles, begin operating the OC Streetcar, and work with local jurisdictions to consider recommendations from planning studies to guide development of future high-quality transit connections (Project S).

The 4.15-mile OC Streetcar will serve the Santa Ana Regional Transportation Center (SARTC) through Downtown Santa Ana and the Civic Center to Harbor Boulevard in the City of Garden Grove. Construction reached 95 percent completion. To date, the contractor has completed major infrastructure work including bridges, tracks, Overhead Contact System (OCS) pole installation, and station platform systems. During the quarter, the remaining four of the eight vehicles were delivered to the Maintenance and Storage Facility (MSF). Work continued on overhead contact system (OCS) wire installation, electrical systems, and interior and exterior work at the MSF. System testing, operations planning, and staff training preparation are underway. more details, see the project updates on page 32.



#### 6. Support expanded mobility choices for seniors and persons with disabilities (Project U).

Project U is comprised of three programs: the Senior Mobility Program (SMP), the Senior Non-Emergency Medical Transportation (SNEMT) Program, and the Fare Stabilization Program. Since inception, nearly \$151.7 million<sup>3,4</sup> has been provided to these three programs. The SMP provides funding to participating cities to design and implement transit service that best fits the needs of seniors (60 and above) in their communities. The SNEMT Program provides funding to the County of Orange Office on Aging for senior transportation to and from medical appointments, dentists, therapies, exercise programs, testing, and other health-related trips at a low cost to the rider than would otherwise be available. The Fare Stabilization Program provides stable discounted fares for seniors and persons with disabilities by lowering the cost of riding transit. For more details, see the program updates on page 34.

# 7. Work with local agencies to maintain successful community circulator projects and potentially provide grant opportunities for expanded or new local transit services (Project V).

Since inception, OCTA has approved 49 projects and ten planning studies totaling over \$96.8 million through five calls. OCTA receives ridership reports from local agencies on a regular basis to monitor the success of awarded services against performance measures adopted by the Board. Staff continues to work with local jurisdictions through letters of interest requests, workshops, CTFP guidelines revisions, calls, and cooperative agreement amendments to fine-tune this program and facilitate successful project implementation. For more details, see the program updates on page 35.

# 8. Continue to improve the top 100 busiest transit stops to enhance the customer experience (Project W).

Through three calls, the Board has approved \$3.1 million to improve 122 city-initiated improvement projects at the busiest OCTA transit stops. The program is designed to ease transfers between bus lines and provide improvements such as the installation of bus benches or seating, shelters, improved lighting, and other passenger-related amenities. For more details, see the program updates on page 36.

<sup>&</sup>lt;sup>3</sup> Only includes disbursed funds. On May 28, 2024, the Board determined the City of Buena Park ineligible to receive net M2 revenues for five years pursuant to Section 10.4 of the M2 Ordinance. Disbursements of net M2 revenues have been suspended until the City of Buena Park reestablishes eligibility.

<sup>&</sup>lt;sup>4</sup> On May 12, 2025, the Board determined the City of Huntington Beach ineligible to receive net M2 revenues for five years pursuant to Section 10.4 of the M2 Ordinance. Disbursements of net M2 revenues have been suspended until the City of Huntington Beach reestablishes eligibility.



9. Ensure the ongoing preservation of purchased open space, which provides comprehensive mitigation of the environmental impacts of freeway improvements and higher-value environmental benefits in exchange for streamlined project approvals (Projects A-M).

The M2 freeway EMP includes seven conservation properties (Preserves) totaling more than 1,300 acres and 13 restoration projects covering nearly 350 acres. In 2017, OCTA received biological resource permits after completing a state and federal Natural Community Conservation Plan/Habitat Conservation Plan (Conservation Plan) for the EMP, allowing streamlined project approvals for the M2 freeway improvement projects. The Conservation Plan also includes a streamlined process for coordination of streambed alteration agreements. In 2018, OCTA secured programmatic permits and assurances for federal and state clean water permitting requirements. Receipt of these permits represents the culmination of years of collaboration and support by the Board, environmental community, and regulatory agencies.

To protect the Preserves in perpetuity, a non-wasting endowment was established. To date, OCTA has made ten annual deposits of approximately \$2.9 million. As of September 30, 2025, the balance of the endowment was \$38,595,652. While the performance of the endowment fund will affect the timeframe for full funding, current projections indicate that OCTA is still on track to meet the target of \$46.2 million in FY 2027-28. For more details, see the program updates on page 38.

10. Work with the Environmental Cleanup Allocation Committee (ECAC) to develop the next tiers of water quality programs to prevent the flow of trash, pollutants, and debris into waterways from transportation facilities. In addition, focus on improving water quality on a regional scale that encourages partnerships among the local agencies as part of the Environmental Cleanup Program (ECP {Project X}).

In May 2010, the Board approved a two-tier approach to funding Project X. Tier 1 consists of funding equipment purchases and upgrades to existing catch basins and related best management practices, such as screens and other low-flow diversion devices. Tier 2 consists of funding regional, potentially multi-jurisdictional, and capital-intensive projects. Since 2011, the Board has awarded more than \$40.2 million in funding for 233 Tier 1 projects through 14 calls and approximately \$34.9 million for 26 Tier 2 projects through three calls. The 15th Tier 1 call was released on March 10, 2025. Applications were received on May 8, 2025. Based upon the project selection criteria in the CTFP guidelines, projects will be prioritized for Board consideration in October 2025. For more details, see the program updates on page 37.

#### Upcoming activities:

• Project X Tier 1 – Programming recommendations for the 15th call



PROJECT A

## INTERSTATE 5 (I-5) PROJECTS

Segment: I-5, SR-55 to SR-57
Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925



**Summary:** This project added a second high-occupancy vehicle (HOV) lane (approximately three miles) in both directions along I-5 between SR-55 and SR-57 in the City of Santa Ana. The final Environmental Document (ED) and Project Report (PR) were approved on April 27, 2015. Construction began on December 27, 2019, and the improvements opened to traffic on August 24, 2020. The total cost is measured against an amended baseline cost established in the first quarter of FY 2017-18; the final schedule is measured against an amended baseline schedule established in the second quarter of FY 2018-19. The project was officially completed three months ahead of schedule on January 6, 2021, and plant establishment was completed on May 24, 2021.

**PROJECT B** 

I-5, I-405 to SR-55 is one project broken into two segments. The final ED and PR were approved on January 7, 2020.

Segment: I-5, I-405 to Yale Avenue


Status: Design Phase Underway – 99 Percent Complete
Contact: Jeff Mills, Capital Projects • (714) 560-5925

Summary: This project will add an additional general purpose lane (approximately 4.5 miles) in both directions of I-5 between I-405 and Yale Avenue, improve interchanges, and replace and add new auxiliary lanes in the City of Irvine. The forecasted schedule is measured against an amended baseline schedule established in the first quarter of FY 2022-23; the forecasted cost is measured against an amended baseline cost established in the second quarter of FY 2024-25. This quarter, the project was advertised for construction on August 18, 2025. Bids are anticipated to be opened in November 2025 to begin construction in early 2026.

Segment: I-5, Yale Avenue to SR-55

Status: Design Phase Underway – 99 Percent Complete
Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project will add an additional general purpose lane (approximately 4.5 miles) in both directions of I-5 between Yale Avenue and SR-55, improve interchanges, and replace and add new auxiliary lanes in the cities of Irvine and Tustin. The forecasted schedule is measured against an amended baseline schedule established in the third quarter of FY 2022-23; the forecasted cost is measured against



an amended baseline cost established in the second quarter of FY 2024-25. This quarter, the project was advertised for construction on August 11, 2025. Bids are anticipated to be opened in October 2025 to begin construction in early 2026.

PROJECT C AND PART OF PROJECT D

I-5, Avenida Pico to San Juan Creek Road is one project broken into three segments. The final ED and PR were approved on October 26, 2011. All three segments were completed, and the improvements opened to traffic on March 13, 2019.

Segment: I-5, Avenida Pico to Avenida Vista Hermosa/Avenida Pico Interchange

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

A. C.

**Summary:** This project added a carpool lane (approximately 0.7 miles) in both directions of I-5 between Avenida Pico and Avenida Vista Hermosa in the City of San Clemente, included major improvements through reconstruction of the Avenida Pico Interchange (part of Project D), and added bicycle lanes in both directions on Avenida Pico. Construction began on December 22, 2014, and was officially completed on August 23, 2018. Plant establishment was completed in May 2019. The total cost is measured against an amended baseline cost established in the second quarter of FY 2011-12; the final schedule is measured against an amended baseline schedule established in the second quarter of FY 2014-15.

Segment: I-5, Avenida Vista Hermosa to Pacific Coast Highway

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

All a

Summary: This project added a carpool lane (approximately 2.5 miles) in both directions of I-5 between Avenida Vista Hermosa and Pacific Coast Highway (PCH) in the City of San Clemente and reconstructed on- and off-ramps at Avenida Vista Hermosa and Camino de Estrella. Construction began on July 3, 2014, and was officially completed on July 31, 2017. Plant establishment was completed in May 2018. The total cost is measured against an amended baseline cost established in the second quarter of FY 2011-12; the final schedule is measured against an amended baseline schedule established in the second quarter of FY 2013-14.

Segment: I-5, Pacific Coast Highway to San Juan Creek Road

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project added a carpool lane (approximately 2.5 miles) in both directions of I-5 between PCH and San Juan Creek Road in the cities of Dana Point, San Clemente, and San Juan Capistrano and reconstructed the on- and off-ramps at PCH/Camino Las Ramblas. Construction began on December 20, 2013, and was officially completed on July 3, 2018. Plant establishment was



completed in March 2019. The total cost is measured against an amended baseline cost established in the second quarter of FY 2011-12; the final schedule is measured against an amended baseline schedule established in the second quarter of FY 2013-14.

I-5, SR-73 to El Toro Road is one project broken into three segments. The final ED and PR for all three segments were approved on May 6, 2014. Improvements for the three segments opened to traffic in March 2025. A separate landscape contractor began plant establishment efforts for all three segments on June 10, 2025, with completion anticipated by December 2026.

Segment: I-5, SR-73 to Oso Parkway/Avery Parkway Interchange

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project added a general purpose lane (approximately 2.2 miles) in both directions of I-5 between Avery Parkway and Oso Parkway and reconstructed the Avery Parkway Interchange (part of Project D) in the cities of Laguna Hills, Laguna Niguel, and Mission Viejo. Construction began on January 15, 2020, and was completed on July 30, 2025. The total cost is measured against an amended baseline cost established in the third quarter of FY 2014-15; the final schedule is measured against an amended baseline schedule established in the third quarter of FY 2019-20.

Segment: I-5, Oso Parkway to Alicia Parkway/La Paz Road Interchange

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project added a general purpose lane (approximately 2.6 miles) in both directions along I-5 between Oso Parkway and Alicia Parkway and reconstructed the La Paz Road Interchange (part of Project D) in the cities of Laguna Hills and Mission Viejo. Construction began on April 4, 2019, and was completed on December 19, 2024. The total cost is measured against an amended baseline cost established in FY 2014-15; the final schedule is measured against an amended baseline schedule established in the fourth quarter of FY 2018-19.

Segment: I-5, Alicia Parkway to El Toro Road

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project added a general purpose lane in the southbound direction (approximately 1.7 miles) and extended the second HOV lane (approximately one mile) in both directions along I-5 between Alicia Parkway to El Toro Road in the cities of Laguna Hills, Laguna Woods, Lake Forest, and Mission Viejo. Construction began on October 13, 2020, and was completed on July 9, 2025. The total cost is measured against an amended baseline cost established in the third quarter of FY 2014-15; the final schedule is measured against an amended baseline schedule established in the first quarter of FY 2020-21. This quarter, the contractor continued slope erosion control and staff continued project closeout activities.



**PROJECT D** 

This project will update and improve key I-5 interchanges at Avenida Pico, Ortega Highway, Avery Parkway, La Paz, and El Toro Road. Three interchange improvements at La Paz, Avery Parkway, and Avenida Pico are included and discussed as part of the respective segments in Project C.

Segment: I-5, Ortega Highway Interchange

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project widened and reconstructed the SR-74 Ortega Highway bridge over I-5 and improved local traffic flow along SR-74 and Del Obispo Street in the City of San Juan Capistrano. The final ED and PR were approved on June 1, 2009. Construction began on September 18, 2012, and all lanes on the new bridge opened to traffic on September 4, 2015. The final schedule is measured against an amended baseline scheduled established in the fourth quarter of FY 2011-12. The project was officially completed on January 15, 2016.

**Segment:** I-5, El Toro Road Interchange

Status: Environmental Phase Two Underway – 65 Percent Complete

Contact: Jeff Mills, Capital Projects • (714) 560-5925

Caltrans is the lead for the environmental phase of this project. The project area includes the cities of Laguna Hills, Laguna Woods, and Lake Forest, which are direct stakeholders of the project improvements. The study began in April 2017 and the draft Initial Study/Environmental Assessment was completed in March 2019. The three stakeholder cities were not in consensus on a preferred alternative, and costs identified for the remaining alternatives were significantly higher than the assumed cost in the Next 10 Plan, which created additional challenges. The environmental phase was anticipated to be completed in late 2019; however, without the cities' consensus, OCTA does not support the finalization of the document. OCTA requested Caltrans put completion of the ED on hold until a consultant, retained by OCTA, provides a further assessment of the alternatives to help facilitate reaching an agreement. The three cities reached a consensus to add two new alternatives from the assessment into the environmental process. The environmental phase was reinitiated in January 2023 to incorporate feedback from the cities on the proposed alternatives. The forecasted cost and schedule are measured against an amended baseline cost and schedule established in the fourth quarter of FY 2022-23. This guarter, OCTA and Caltrans continued coordination with the cities of Laguna Hills, Laguna Woods, and Lake Forest on the proposed alternatives, preliminary design, and environmental phase studies. In addition, Caltrans completed updates to the final Traffic Operations Analysis Report.


**PROJECT E** 

# STATE ROUTE 22 (SR-22) PROJECTS

**Segment:** SR-22 Access Improvements

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925



PROJECT F

### STATE ROUTE 55 (SR-55) PROJECTS

**Segment:** SR-55, I-405 to I-5

Status: Construction Underway – 57 Percent Complete
Contact: Jeff Mills, Capital Projects • (714) 560-5925

Summary: This project will add a general purpose lane (approximately four miles) and a second HOV lane (approximately four miles) in both directions between I-405 and I-5 in the cities of Irvine, Santa Ana, and Tustin. Auxiliary lanes will be added and extended in some segments within the project limits. The final ED and PR were approved on August 31, 2017. The forecasted cost is measured against an amended baseline cost established in the fourth quarter of FY 2017-18; the forecasted schedule is measured against an amended baseline schedule established in the fourth quarter of FY 2021-22. Construction began on August 10, 2022. This quarter, work continued with roadway, retaining wall, bridge widening, electrical, and drainage construction activities.

**Segment:** SR-55, I-5 to SR-91

Status: Design Phase Underway – 87 Percent Complete
Contact: Jeff Mills, Capital Projects • (714) 4560-5925

Summary: This project includes the addition of a general purpose lane (approximately two miles) in both directions between I-5 and SR-22 and operational improvements between SR-22 and SR-91 in the cities of Anaheim, Orange, Santa Ana, and Tustin. The project limits span approximately 7.5 miles. The final ED and PR were approved on March 30, 2020. The forecasted cost is measured against an amended baseline cost established in the fourth quarter of FY 2020-21; the forecasted schedule is measured against an amended baseline schedule established in the third quarter of FY 2022-23. The design of this project was initiated on August 8, 2022. This quarter, the design team continued to address comments on the 100 percent design package submittal. ROW activities are underway.



**PROJECT G** 

# STATE ROUTE 57 (SR-57) PROJECTS

Segment: SR-57 Northbound, Orangewood Avenue to Katella Avenue

Status: Design Phase Completed

Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project will add a new northbound general purpose lane (approximately one mile) on SR-57 from Orangewood Avenue to Katella Avenue in the cities of Anaheim and Orange. The new northbound general purpose lane will join the completed Project G segments between Katella Avenue and Lambert Road, which opened to traffic in 2014. The final ED and PR were approved on March 29, 2019. The forecasted cost is measured against an amended baseline cost established in the third quarter of FY 2020-21; the forecasted schedule is measured against an amended baseline schedule established in the fourth quarter of FY 2022-23. The project was advertised for construction on July 7, 2025, bids were opened on September 4, 2025, and the contract was awarded on September 26, 2025. Construction is anticipated to begin in December 2025.

Segment: SR-57 Northbound, Katella Avenue to Lincoln Avenue

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project increased capacity by adding a new general purpose lane (approximately 2.8 miles) and improved on- and off-ramps and soundwalls on northbound SR-57 between Katella Avenue and Lincoln Avenue in the City of Anaheim. Bridges at Katella Avenue and Douglas Road were also widened in the northbound direction. The final ED was approved on September 30, 2009, and the final PR was approved on November 25, 2009. Construction began on November 17, 2011, and the improvements opened to traffic on November 19, 2014. The final schedule is measured against an amended baseline schedule established in the second quarter of FY 2011-12. The project was officially completed on April 21, 2015.

Segment: SR-57 Northbound, Orangethorpe Avenue to Yorba Linda Boulevard

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project increased capacity by adding a northbound general purpose lane (approximately 2.4 miles) between Orangethorpe Avenue in the City of Placentia to Yorba Linda Boulevard in the City of Fullerton and improved operations with the reconstruction of northbound on- and off-ramps, widening of seven bridges, and the addition of soundwalls. The final ED and PR were approved on November 30, 2007. Construction began on October 26, 2010, and the improvements opened to traffic on April 28, 2014. The final schedule is measured against an amended baseline schedule established in the fourth quarter of FY 2013-14. The project was officially completed on November 6, 2014.



Segment: SR-57 Northbound, Yorba Linda Boulevard to Lambert Road

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925



Summary: This project improved capacity, operations, and traffic flow on SR-57 with the addition of a new northbound general purpose lane (approximately 2.5 miles) between Yorba Linda Boulevard in the City of Fullerton and Lambert Road in the City of Brea. Additional project benefits included on- and off-ramp improvements, the widening and seismic retrofit (as required) of six bridges in the northbound direction, and the addition of soundwalls. Existing lanes and shoulders were also widened to standard widths, enhancing safety for motorists. The final ED and PR were approved on November 30, 2007. Construction began on November 2, 2010, and the improvements opened to traffic on September 23, 2013. The total cost is measured against an amended baseline cost established in the second quarter of FY 2010-11; the final schedule is measured against an amended baseline schedule established in the fourth quarter of FY 2013-14. The project was officially completed on May 2, 2014.

Segment: SR-57 Northbound, Lambert Road to Orange/Los Angeles County Line

Status: Project Study Report-Project Development Support (PSR-PDS) Document Preparation

Underway – 99 Percent Complete

Contact: Jeff Mills, Capital Projects • (714) 560-5925

Kristin Tso, Planning • (714) 560-5496

Summary: Caltrans previously completed a PSR in 2001 to add a northbound truck-climbing lane (approximately 2.5 miles) from Lambert Road in the City of Brea to approximately 0.62 miles north of the Orange County/Los Angeles County line. Following discussions with Caltrans in late 2021, it was decided that a new PSR-PDS should be prepared due to the changing conditions on SR-57 since the previous study was completed. The proposed project included mainline and interchange improvements at Lambert Road. Through the SB 1 (Chapter 5, Statutes of 2017) Trade Corridor Enhancement Program, funds were allocated to construct the interchange improvements at Lambert Road, which complemented and served as the first phase to the improvement project. Construction began in mid-2019, the project opened to traffic in December 2023, and construction was fully completed in early 2024. Preparation of the new PSR-PDS for the second phase began in August 2023, utilizing State Transportation Investment Program funding, to study potential northbound mainline improvements from Lambert Road to Orange/Los Angeles County Line (up to two miles). This quarter, the consultant continued addressing comments from the circulation of the draft final PSR-PDS, which is anticipated to receive final approval in October 2025. The environmental phase of the project is anticipated to begin in November 2025.



PROJECT H

## STATE ROUTE 91 (SR-91) PROJECTS

Segment: SR-91 Westbound, I-5 to SR-57

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project increased capacity by adding a general purpose lane (approximately 4.5 miles) in the westbound direction between the cities of Anaheim and Fullerton and provided operational improvements at on- and off-ramps between Brookhurst Street and State College Boulevard. The final ED was approved on May 20, 2010, and the final PR was approved on June 16, 2010. Construction began on February 6, 2013, and the improvements opened to traffic on March 7, 2016. The final schedule is measured against an amended baseline schedule established in the third quarter of FY 2012-13. The project was officially completed on June 23, 2016.

**PROJECT I** 

Segment: SR-91, SR-55 to Tustin Avenue Interchange

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

Summary: This project improved traffic flow at the SR-55/SR-91 interchange by adding a westbound auxiliary lane (approximately two miles) beginning at northbound SR-55 to the westbound SR-91 connector through the Tustin Avenue interchange in the City of Anaheim. The project reduced weaving congestion in the area and included reconstruction of the westbound side of the Santa Ana River Bridge to accommodate the additional lane. The final ED was approved on May 11, 2011, and the final PR was approved on May 19, 2011. Construction began on November 1, 2013, and the improvements opened to traffic on May 14, 2016. The total cost is measured against an amended baseline cost established in the fourth quarter of FY 2010-11; the final schedule is measured against an amended baseline schedule established in the fourth quarter of FY 2012-13. The project was officially completed on July 15, 2016.

SR-91, between SR-57 and SR-55 is one project broken into three segments. To augment the decrease in projected M2 revenues, on September 12, 2016, the Board approved to use 91 Express Lanes excess revenue to fund this project. The final ED and PR were approved on June 22, 2020.

Segment: SR-91, SR-55 to Lakeview Avenue

Status: Construction Underway - Ten Percent Complete
Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project will provide westbound operational improvements (approximately 2.2 miles), which includes the realignment of the existing westbound SR-91 on- and off-ramps, the addition of a new on-ramp from the Lakeview Avenue overcrossing bridge to connect directly to southbound SR-55, and







construction of a barrier to separate westbound SR-91 from SR-55. With the proposed improvements, the existing Lakeview Avenue overcrossing bridge is anticipated to be replaced with a new bridge. The forecasted schedule is measured against an amended baseline schedule established in the third quarter of FY 2024-25; the forecasted cost is measured against an amended baseline cost established in the fourth quarter of FY 2023-24. This project was combined with the Caltrans multi-asset project during the design phase. Construction activities began on April 8, 2025. During the quarter, the contractor began installation of retaining walls, drainage systems, and prepared the site for the Lakeview Avenue bridge reconstruction.

Segment: SR-91, La Palma Avenue to SR-55

Status: Design Phase Underway - 95 Percent Complete
Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project will provide an additional eastbound general purpose lane (approximately 2.7 miles), replace the eastbound shoulder, and restore auxiliary lanes as needed throughout the project limits. With the proposed improvements, the existing Kraemer Boulevard and Tustin Avenue overcrossing bridges are anticipated to be replaced with new bridges and the Santa Ana River bridge will be widened. The forecasted cost is measured against an amended baseline cost established in the fourth quarter of FY 2019-20; the forecasted scheduled is measured against an amended baseline schedule established in the first quarter of FY 2020-21. The design of this project was initiated on June 17, 2020. This quarter, the design team continued to address and resolve outstanding comments on the final design package submittal. In addition, ROW activities continued and several utility relocation permits were obtained.

Segment: SR-91, Acacia Street to La Palma Avenue
Status: Design Phase Underway - 96 Percent Complete
Contact: Jeff Mills, Capital Projects • (714) 560-5925

Summary: This project will provide westbound operational improvements (approximately 1.8 miles) by adding a fourth general purpose lane along westbound SR-91 from the northbound SR-57 to the westbound SR-91 connector, extending the southbound SR-57 to westbound SR-91 connector auxiliary lane through the State College Boulevard interchange, tying into the existing westbound SR-91 auxiliary lane west of State College Boulevard, and reconfiguring the westbound SR-91 to SR-57 connector to provide dedicated exits to SR-57. With the proposed improvements, the existing La Palma Avenue overcrossing bridge will be replaced with a new bridge. The forecasted schedule is measured against an amended baseline schedule established in the fourth quarter of FY 2020-21; the forecasted cost is measured against an amended baseline cost established in the fourth quarter of FY 2023-24. This project was combined with the Caltrans multi-asset project during the design phase. The project was advertised for construction on May 12, 2025, and bids were opened on August 12, 2025. The contract is anticipated to be awarded in October 2025, with construction anticipated to begin in December 2026.

**PROJECT J** 

Segment: SR-91, SR-55 to SR-241 Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project added a general purpose lane (approximately six miles) in both directions of SR-91 between SR-55 and SR-241 in the cities of Anaheim and Yorba Linda. In addition to adding 12 lane miles to SR-91, the project also delivered a second eastbound exit lane at Lakeview Avenue, Imperial Highway, and Yorba Linda Boulevard/Weir Canyon Road off-ramps. Beyond these capital improvements, crews completed work on safety barriers, lane striping, and soundwalls. The final ED and PR were approved on April 24, 2009. Construction began on May 27, 2011, and opened to traffic in December 2012. The final schedule is measured against an amended baseline schedule established in the fourth quarter of FY 2010-11. The project was officially completed on March 5, 2013.

Segment: SR-91 Eastbound, SR-241 to SR-71

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

Summary: This project improved mobility and operations by adding an eastbound lane (approximately six miles) through a key stretch of SR-91 between Orange County's SR-241 and Riverside County's SR-71, widened existing eastbound lanes and shoulders, and reduced traffic weaving as a result of traffic exiting at SR-71 and Green River Road. The final ED and PR were approved on December 28, 2007. Construction began on September 16, 2009, and the improvements opened to traffic on December 2, 2010. The final schedule is measured against an amended baseline schedule established in the second quarter of FY 2010-11. The project was officially completed on January 31, 2011. Because this project was shovel-ready, OCTA was able to obtain American Recovery and Reinvestment Act funding for this M2 project, saving M2 revenues for future projects.

Segment: SR-91, SR-241 to Orange/Riverside County Line

Status: RCTC's Westbound Corridor Operation Project – Completed in January 2022; Eastbound

Corridor Operation Project Environmental Phase Underway - 75 Percent Complete

Contact: Jeff Mills, Capital Projects • (714) 560-5925

Summary: Since the SR-91 corridor is one of the busiest in the region, implementation of this project requires coordinating and constructing the improvements in multiple segments and capitalizing on available funding. Freeway improvements that cross county lines require close coordination to maintain seamless travel. This project plans to add a general purpose lane on SR-91 between SR-241 and SR-71. While the portion of this project between SR-241 and the Orange/Riverside County Line is part of OCTA's M2 Project J, the matching segment between the county line and SR-71 is part of RCTC's Measure A. The sixth lane addition requires joint implementation to ensure smooth delivery of the project. With significant SR-91 freeway improvements taking place as a result of both counties' sales tax measures, the construction timing of the additional general purpose lane between SR-241 and SR-71 was anticipated to take place



post-2035. However, RCTC requested OCTA's support to accelerate a portion of the ultimate project in the westbound direction (in Orange County) to address a bottleneck issue affecting the City of Corona. With OCTA's support, RCTC developed the 91 Westbound Corridor Operation Project, which began construction in late 2020 and was completed in January 2022.

In addition, OCTA and RCTC conducted a feasibility study to determine how best to implement the sixth general purpose lane while minimizing environmental and construction impacts in the eastbound direction between SR-241 and SR-71. The final alternatives analysis report was completed in April 2022. RCTC is leading the effort to proceed with the environmental phase of the project, to be referred to as the 91 Eastbound Corridor Operation Project. This effort began in June 2023 and is anticipated to be completed in early 2026. This quarter, the project team continued working on preliminary engineering for the build alternatives, developing cost estimates, and updating environmental technical studies and a Supplemental Project Report. RCTC plans to utilize progressive design-build as the project delivery approach that will include preliminary design (Phase I) followed by final design and construction (Phase II). Phase I is anticipated to begin mid-2026.

PROJECT K

## INTERSTATE 405 (I-405) PROJECTS

Segment: I-405, SR-73 to I-605 Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925



Summary: This project added a general purpose lane (approximately 16 miles) between Euclid Street and I-605 in both directions and a second HOV lane (approximately 14 miles) combined with the existing HOV lane to provide dual express lanes in both directions of I-405 from SR-73 to I-605, otherwise known as the 405 Express Lanes.<sup>5</sup> Additional improvements included reconstruction of local interchanges and enhancements to freeway entrances and exits along the corridor from SR-73 to I-605 through the cities of Costa Mesa, Fountain Valley, Garden Grove, Huntington Beach, Los Alamitos, Seal Beach, and Westminster. The final ED and PR were approved on June 15, 2015. Construction activities began on January 31, 2017, and the project fully opened to traffic on December 1, 2023. The final schedule is measured against an amended baseline schedule established in the second quarter of FY 2020-21; the total cost is measured against an amended baseline cost established in the fourth quarter of FY 2022-23. Final acceptance and relief of maintenance is expected in late 2025. During the quarter, work continued on remaining miscellaneous construction activities including landscaping and punch-list items.

<sup>&</sup>lt;sup>5</sup> The general purpose lane portion of the project is an M2 project and was funded by a combination of local, state, and federal funds. The express lanes portion of the project was financed and will be paid for by those who choose to pay a toll and use the 405 Express Lanes.



**PROJECT L** 

**Segment:** I-405, I-5 to SR-55

**Status:** Environmental Phase Complete

Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project studied potential improvements along approximately 8.5 miles of I-405 between I-5 and SR-55 in the City of Irvine. The project development team reviewed the alternatives and public comments received during public circulation, and as a result of the effort, recommended adding one general purpose lane in both directions. The forecasted schedule is measured against an amended baseline schedule established in the third quarter of FY 2015-16. The final ED and PR were approved on August 31, 2018. The design phase is anticipated to begin in 2030 and will be constructed beyond the Next 10 Plan timeframe.

**PROJECT M** 

### INTERSTATE 605 (I-605) PROJECTS

Segment: I-605, Katella Avenue Interchange Improvements
Status: Construction Underway - 15 Percent Complete
Contact: Jeff Mills, Capital Projects • (714) 560-5925

Summary: This project will make enhancements to the on- and off-ramps and operational improvements on Katella Avenue at the I-605 Interchange in the City of Los Alamitos. In addition, pedestrian and bicycle improvements will incorporate complete streets components, including enhanced safety for all modes of travel. The final ED and PR were approved on October 3, 2018. The forecasted cost is measured against an amended baseline cost established in the third quarter of FY 2019-20; the forecasted schedule is measured against an amended baseline schedule established in the fourth quarter of FY 2024-25. The project was awarded and construction activities began on April 3, 2025. During the quarter, the contractor completed median reconstruction along Katella Avenue, and began improvements along Katella Avenue. The construction management team continued to coordinate with the design team and utility companies on timing of final utility relocations.



**PROJECT N** 

# FREEWAY SERVICE PATROL

Status: Service Ongoing

Contact: Patrick Sampson, Motorist Services • (714) 560-5435

**Summary:** The Freeway Service Patrol (FSP) assists motorists whose vehicles become disabled along Orange County freeways and removes congestion-causing debris from traffic lanes to reduce freeway congestion and collisions. In June 2012, M2 began supporting FSP with local funds to maintain existing service levels and expand services through 2041. During the quarter, FSP provided 15,463 services.<sup>6</sup> Since June 2012, FSP has provided 874,343 services<sup>6</sup> on the Orange County freeway system.

<sup>&</sup>lt;sup>6</sup> Service calculations are based on all services provided as FSP is funded by M2 and external sources.



**PROJECT O** 

### REGIONAL CAPACITY PROGRAM

Status: 16th Call Open

Contact: Charvalen Alacar, Planning • (714) 560-5401

Summary: This program, in combination with required local matching funds, provides funding for improvements on Orange County's Master Plan of Arterial Highways. Since 2011, through 15 calls, the Board has awarded 195 projects (237 project phases) totaling more than \$432 million, including \$23.4 million in external funding. To date, 155 project phases have been completed, 55 are in various stages of implementation, and 27 have been cancelled by the awarded local jurisdictions. On September 8, 2025, the Board approved the release of the 16th call. Applications for the call are due on November 20, 2025, and programming recommendations are anticipated to be presented to the Board in spring 2026.

#### **OC Bridges Railroad Program**

This program built seven grade separations (either under or overpasses) where high-volume streets are impacted by freight trains along the BNSF railroad in north Orange County. On September 13, 2021, the Board approved program closeout and budget adjustment to approximately \$666.55 million for all the OC Bridges grade separation projects, of which \$152.6 million was committed M2 and \$513.9 million in leveraged external funding. Funding reimbursement and closeout for all seven grade separation projects have been completed.

**Segment:** Kraemer Boulevard Grade Separation

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

**Summary:** This project grade separated the local street from railroad tracks by building an underpass for vehicular traffic under the railroad crossing in the cities of Anaheim and Placentia. Construction began on November 9, 2012, and the improvements opened to traffic on June 28, 2014. The final schedule is measured against an amended baseline schedule established in the second quarter of FY 2011-12. Construction acceptance was obtained in December 2014. OCTA turned over maintenance responsibilities to the cities and completed the one-year warranty in December 2015 with no issues or claims identified. Funding reimbursement and closeout have been completed.

Segment: Lakeview Avenue Grade Separation

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

Summary: This project grade separated the local street from railroad tracks by building a bridge for vehicular traffic over the railroad crossing and reconfiguring the intersection of Lakeview Avenue and





Orangethorpe Avenue in the cities of Anaheim and Placentia. Construction began on March 3, 2014, and the improvements opened to traffic on June 6, 2017. The final schedule is measured against an amended baseline schedule established in the first quarter of FY 2013-14. Construction acceptance was obtained in June 2018. OCTA turned over maintenance responsibilities to the cities and extended the one-year warranty to July 2019 for some minor repair items. The Board approved a final claim resolution in July 2019. Funding reimbursement and closeout have been completed.

Segment: **Orangethorpe Avenue Grade Separation** 

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

This project grade separated the local street from railroad tracks by building a bridge for Summarv: vehicular traffic over the railroad crossing in the cities of Anaheim and Placentia. Construction began on April 25, 2013, and the improvements opened to traffic on June 23, 2016. The final schedule is measured against an amended baseline schedule established in the third quarter of FY 2012-13. Construction acceptance was obtained in October 2016. OCTA turned over maintenance responsibilities to the cities and extended the one-year warranty to June 2019 for some minor repair items. No additional issues or repairs were identified. Funding reimbursement and closeout have been completed.

Segment: Placentia Avenue Grade Separation

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

Summary: This project grade separated the local street from railroad tracks by building an underpass for vehicular traffic under the railroad crossing in the City of Placentia. Construction began on October 5, 2011, and the improvements opened to traffic on March 12, 2014. The total cost is measured against an amended baseline cost established in the fourth quarter of FY 2009-10; the final schedule is measured against an amended baseline schedule established in the second quarter of FY 2011-12. Construction acceptance was obtained in December 2014. OCTA turned over maintenance responsibilities to the cities and completed the one-year warranty in December 2015 with no issues or repairs identified. Funding reimbursement and closeout have been completed.

Segment: Raymond Avenue Grade Separation

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

This project grade separated the local street from railroad tracks by building an underpass Summary: for vehicular traffic under the railroad crossing in the City of Fullerton. The City of Fullerton managed construction while OCTA provided construction oversight, public outreach, railroad coordination, and ROW support. Construction began on March 27, 2014, and the improvements opened to traffic on October 2, 2017. The total cost is measured against an amended baseline cost established in the first quarter of FY 2010-11; the final schedule is measured against an amended baseline schedule established in the third quarter of FY 2013-14. Construction acceptance was obtained in May 2018. OCTA turned over maintenance responsibilities to the City of Fullerton and completed the one-year warranty on constructed 23 items. Funding reimbursement and closeout have been completed.





Segment: State College Boulevard Grade Separation

**Status:** PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

Summary: This project grade separated the local street from railroad tracks by building an underpass for vehicular traffic under the railroad crossing in the City of Fullerton. The City of Fullerton managed construction while OCTA provided construction oversight, public outreach, railroad coordination, and ROW support. Construction began on March 27, 2014, and the improvements opened to traffic on November 1, 2017. The total cost is measured against an amended baseline cost established in the second quarter of FY 2010-11; the final schedule is measured against an amended baseline schedule established in the third quarter of FY 2013-14. Construction acceptance was obtained in March 2018. OCTA turned over maintenance responsibilities to the City of Fullerton and completed the one-year warranty on constructed items. Funding reimbursement and closeout have been completed.

Segment: Tustin Avenue/Rose Drive Grade Separation

Status: PROJECT COMPLETE

Contact: Jeff Mills, Capital Projects • (714) 560-5925

Summary: This project grade separated the local street from railroad tracks by building a bridge over the railroad crossing for vehicular traffic in the cities of Anaheim and Placentia. Construction began on April 22, 2013, and the improvements opened to traffic on December 7, 2015. The total cost is measured against an amended baseline cost established in the first quarter of FY 2010-11; the final schedule is measured against an amended baseline schedule established in the third quarter of FY 2012-13. Construction acceptance was obtained in October 2016. OCTA turned over maintenance responsibilities to the cities and extended the one-year warranty to November 2018 for some minor repair items. No additional issues or repairs were identified. Funding reimbursement and closeout have been completed.

**PROJECT P** 

### REGIONAL TRAFFIC SIGNAL SYNCHRONIZATION PROGRAM

Status: 16th Call Open

Contact: Anup Kulkarni, Planning • (714) 560-5867

**Summary:** This program provides funding and assistance to implement multi-agency signal synchronization. The target of the program is to regularly coordinate a network of over 2,000 signalized intersections along 750 miles of roadway within Orange County. OCTA also leverages external funding to further enhance the efficiency of the street grid and reduce travel delays.



To date, OCTA and local agencies have synchronized 3,789 intersections over 979 miles of streets (109 completed projects). Through 15 calls, 123 projects<sup>7</sup> totaling approximately \$162.3 million have been awarded. Overall, OCTA has funded 143 projects<sup>7</sup> totaling nearly \$196.8 million, including \$40.1 million in leveraged external funding. On September 8, 2025, the Board approved the release of the 16th call. Applications for the call are due on November 20, 2025, and programming recommendations are anticipated to be presented to the Board in spring 2026.

In parallel with the annual call, OCTA is leading the Countywide Signal Synchronization Baseline Project. The project aims to develop and implement a countywide signal synchronization network for Orange County and will consist of approximately 2,500 retimed signals along regionally significant corridors to ensure seamless travel across the County. This effort began in June 2024 with data collection ongoing. While this innovative project is entirely externally funded, the results will benefit and shape the future of the M2 Regional Traffic Signal Synchronization Program.

**PROJECT Q** 

# LOCAL FAIR SHARE

Status: Ongoing

Contact: Sean Murdock, Finance • (714) 560-5685


**Summary:** To help cities and the County of Orange keep up with the rising cost of repairing the aging street system, this program provides flexible funding intended to augment, not replace, existing transportation expenditures by the cities and the County. On a bimonthly basis, 18 percent of net revenues are allocated by formula. Since 2011, nearly \$823.0 million<sup>8,9</sup> in LFS payments have been provided to local jurisdictions, of which more than \$12.6 million<sup>8,9</sup> was provided this guarter.

For more details, see funding allocation by local agency on pages 51-52.

<sup>&</sup>lt;sup>7</sup> To date, three projects totaling approximately \$1.6 million have been cancelled by the awarded local jurisdictions.

<sup>&</sup>lt;sup>8</sup> Only includes disbursed funds. On May 28, 2024, the Board determined the City of Buena Park ineligible to receive net M2 revenues for five years pursuant to Section 10.4 of the M2 Ordinance. Disbursements of net M2 revenues have been suspended until the City of Buena Park reestablishes eligibility.

<sup>&</sup>lt;sup>9</sup> On May 12, 2025, the Board determined the City of Huntington Beach ineligible to receive net M2 revenues for five years pursuant to Section 10.4 of the M2 Ordinance. Disbursements of net M2 revenues have been suspended until the City of Huntington Beach reestablishes eligibility.

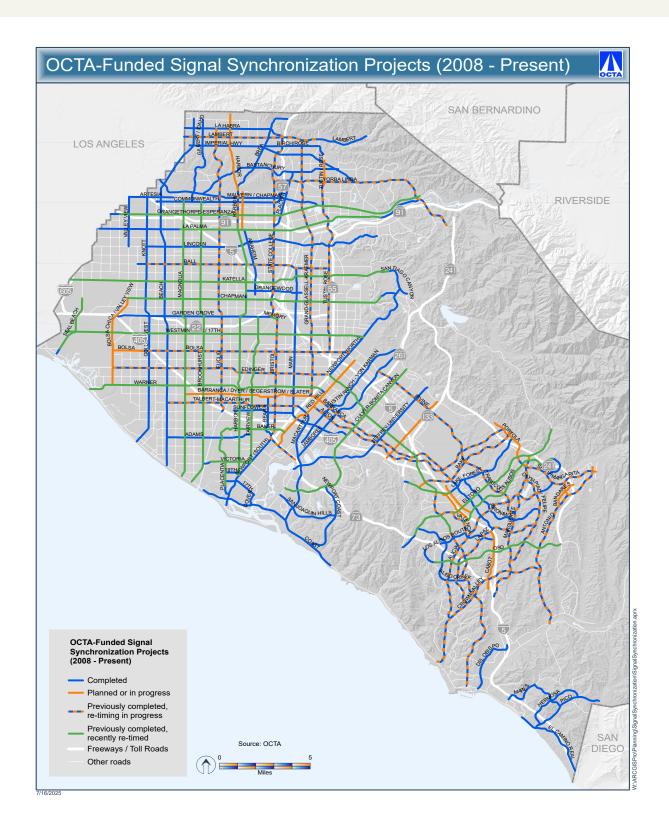



**PROJECT R** 

## HIGH FREQUENCY METROLINK SERVICE

Project R provides funding for Metrolink operations and aims to increase rail services within the County and provide additional Metrolink service north of the City of Fullerton to the Los Angeles County Line. The program provides for track improvements, the addition of trains and parking capacity, upgraded stations, and safety enhancements to allow cities to establish quiet zones along the tracks. This program also includes funding for grade crossing improvements at high-volume arterial streets, which cross Metrolink tracks.

**Project:** Metrolink Grade Crossing Improvements

Status: PROJECT COMPLETE

Contact: Megan Taylor, Operations • (714) 560-5601

**Summary:** Enhancements at 50 of the designated 52 Orange County at-grade rail-highway crossings were completed in support of the Metrolink Service Expansion Program (MSEP) in October 2012. The total cost is measured against an amended baseline cost established in the fourth quarter of FY 2010-11. As a result of one private crossing, which did not allow OCTA to make enhancements, and one street closure, which eliminated the need for enhancements, the final count of enhanced rail-highway crossings was 50. Completion of the safety improvements provided each corridor city with the opportunity to establish a "quiet zone" at their respective crossings. Quiet zones are intended to prohibit the sounding of train horns through designated crossings, except in the case of emergencies, construction work, or safety concerns identified by the train engineer. The cities of Anaheim, Dana Point, Irvine, Orange, San Clemente, San Juan Capistrano, Santa Ana, and Tustin have established quiet zones within their communities.

**Project:** Metrolink Service Expansion Program

Status: PROJECT COMPLETE

Contact: Megan Taylor, Operations • (714) 560-5601

**Summary:** Following the completion of the MSEP improvements in 2012, OCTA deployed a total of ten new Metrolink intracounty trains operating between the cities of Fullerton and Laguna Niguel/Mission Viejo, primarily during the midday and evening hours.

In October 2019, several intracounty trains were extended to Los Angeles County to increase ridership through a redeployment of the trains without significantly impacting operating costs. This change resulted in 54 weekday trains operating between the three lines within Orange County. However, following the onset of the COVID-19 pandemic, service was reduced to 41 trains. In October 2021, partial service was restored which increased service to 45 trains. On October 21, 2024, Metrolink implemented an optimized service schedule aimed at addressing service gaps, increasing efficiency of assets, and serving a wider variety of travel patterns as Metrolink adjusts the focus from commuter rail to regional rail. As such, the three lines serving Orange County now operate 58 trains, surpassing the number of trains operating pre-COVID-19. Total boardings for the quarter are 45 percent lower compared to the same quarter of FY 2019-20 (used as a pre-pandemic data set). They are nearly two percent higher than in the same guarter in FY 2024-25.





Metrolink ridership continues to struggle to recover pre-pandemic ridership, affecting farebox recovery. To exacerbate this shortfall, operating costs have also increased. Current projections with the addition of TIRCP formula funds will only sustain current Metrolink service levels through FY 2035-36. OCTA will continue to actively engage with Metrolink and the other member agencies to monitor ridership levels and the corresponding financial impacts to M2.

#### Rail Corridor and Station Improvements

Additionally, under MSEP, funding is provided for rail line and station improvements to accommodate increased service. Rail station parking lot expansions and better access to platforms, among other improvements have been made or are underway. For schedule information on station improvement projects, please see the Capital Action Plan on pages 53-57.

**Project: Anaheim Canyon Metrolink Station Improvements** 

Status: PROJECT COMPLETE

Jim Beil, Capital Programs • (714) 560-5646 Contact:

This project added a second main track and passenger platform, extended the existing passenger platform, added improvements to at-grade crossings for pedestrian circulation, and installed new station amenities including benches, shade structures, and ticket vending machines. The improvements were completed on January 30, 2023. The total cost is measured against an amended baseline cost established in the third quarter of FY 2016-17; the final schedule is measured against an amended baseline schedule established in the fourth quarter of FY 2020-21.

**Project: Fullerton Transportation Center Improvements** 

Status: PROJECT COMPLETE

Contact: Jim Beil, Capital Programs • (714) 560-5646

Completed early on, this project constructed a new five-level parking structure to provide additional transit parking at the Fullerton Transportation Center for both intercity rail service and commuter rail passengers. Construction on this city-led project began on October 18, 2010, and the improvements were completed on June 19, 2012. After completion, an elevator upgrade project was initiated with leftover savings. The elevator project modified the existing pedestrian bridge to add two new traction elevators, one on each side. The City of Fullerton was the lead on this project, which was completed on May 1, 2019.

**Project:** Laguna Niguel/Mission Viejo Metrolink Station Americans with

Disabilities Act (ADA) Ramps


PROJECT COMPLETE Status:

Contact: Jim Beil, Capital Programs • (714) 560-5646

This project added new ADA-compliant access ramps on either side of the pedestrian **Summary:** undercrossing and a unisex ADA-compliant restroom, vending machine room, and three passenger canopies. Construction began on February 23, 2016, and the improvements were completed on September 20, 2017. The final schedule is measured against an amended baseline schedule established in the third quarter of FY 2018-19.







**Project:** Orange Transportation Center Metrolink Parking Structure

Status: PROJECT COMPLETE

Contact: Jim Beil, Capital Programs • (714) 560-5646

**Summary:** This project constructed a 608-space, five-level, shared-use parking structure that is located on Lemon Street between Chapman Avenue and Maple Street in the City of Orange. Per a cooperative agreement between OCTA and the City of Orange, the City of Orange led the design phase, and OCTA led the construction phase of the project. Construction began on July 17, 2017, and the improvements were completed on February 15, 2019. The total cost is measured against an amended baseline cost established in the fourth quarter of FY 2015-16; the final schedule is measured against an amended baseline schedule established in the second guarter of FY 2017-18.

**Project:** New Placentia Metrolink Station and Parking Structure

Status: Design Complete; Ready for Advertisement subject to BNSF construction and

maintenance (C&M) agreement

Contact: Jim Beil, Capital Programs • (714) 560-5646

Summary: This project will construct a new Metrolink station to include platforms, parking, a new bus stop, and passenger amenities in the City of Placentia. Plans for the proposed Placentia Metrolink Station Project were near completion when the City of Placentia requested to modify them to include a parking structure to be built where surface parking had been designed. On June 27, 2016, the Board approved a cooperative agreement with the City of Placentia that revised the project's scope and budget, and with the changes, the City of Placentia will contribute towards the cost. The project will also include a third track which should assist with the on-time performance of train operations and provide operational flexibility for both freight and passenger trains. OCTA is the lead agency for the design and construction and BNSF will be the lead on rail construction. The final design was completed on July 22, 2017. The forecasted cost and schedule is measured against an amended baseline cost and schedule established in the first quarter of FY 2016-17. The project will be ready to advertise once a C&M agreement with BNSF is in place.

**Project:** San Clemente Pier Station Lighting

Status: PROJECT COMPLETE

Contact: Jim Beil, Capital Programs • (714) 560-5646

**Summary:** This OCTA-led project added lighting to the existing platform and new decorative handrails at the San Clemente Pier Station in the City of San Clemente. The improvements were completed on March 17, 2017, and project closeout was completed in the same month.

#### **Additional Rail Corridor Improvements**

In September 2021, a failing slope severely degraded the railroad track structure in the City of San Clemente in the Cyprus Shore area south of the San Clemente Pier [Mile Post (MP) 206.8]. Emergency repair efforts were taken between late 2021 and early 2022. However, higher tidal events coupled with the movement of an ancient slide impacted the stability of the track, leading to a temporary suspension of rail service. Funded by the commuter rail fund and some State emergency funds, emergency





work to stabilize the railroad track was sufficiently completed to allow full passenger rail service resumption on April 2023. The track stabilization efforts were substantially completed in August 2023.

During this time, a hillside owned by the City of San Clemente at the Casa Romantica Cultural Center and Gardens (MP 204.6) failed and continued to move incrementally. Landslide debris continued to crumble down the slope and foul the tracks owned by OCTA, which led to the suspension of all passenger rail services in the City of San Clemente and south Orange County in April 2023. A temporary barrier wall at the bottom of the slope was constructed and service resumed in July 2023, to protect the railroad track while the City of San Clemente continued construction of the long-term slope stabilization repairs. OCTA continues to work with partners to seek additional funding as needed.

In January 2024, landslide movement caused debris from the hillside slope along the Mariposa Trail Bridge (Mariposa Point [MP 204.2]) in the City of San Clemente to fall onto the ROW and railroad tracks, including dislodging two spans of the city-owned pedestrian bridge, which temporary suspended rail service in the area. As the hillside continued experience movement, a catchment wall was designed and constructed and resumed passenger rail service in March 2024.

A comprehensive plan to integrate engineering and sand nourishment solutions is underway to protect the coastal segment of the rail corridor in south Orange County in the immediate timeframe. In December 2024, OCTA received \$305 million in state and federal funding to implement the necessary immediate protective solutions for inland slope stability and coastal erosion, identified as Areas 1 through 4 for the rail corridor within the City of San Clemente. While the rail line is currently open as a result of ongoing emergency work, longer-term solutions must be developed to ensure the ability to provide reliable rail service in this portion of the County. In partnership with key stakeholders, a planning study is currently underway to identify and evaluate immediate short- and medium-term solutions with the goal of protecting the rail line in place for approximately the next 30 years. A separate long-term study will assess potential long-term solutions, which may include relocation of the rail line. OCTA is leading the effort on the near-term resiliency measures. The State will lead the long-term study, but the lead state agency has not been identified; OCTA will remain an active participant in the study. Future implications to M2 with respect to service levels or project costs are unknown at this time.

#### Completed:

- Installation of the Control Point project at Fourth Street in the City of Santa Ana, which provided greater efficiency and reliability for passenger rail service
- Implementation of Positive Train Control system, which improves rail safety by monitoring and controlling train movement
- Implementation of video surveillance systems at the Fullerton, Irvine, Laguna Niguel, Mission Viejo, Orange, Santa Ana, and Tustin stations
- Railroad ROW Slope Stabilization project at eight locations within the rail corridor to prevent future erosion and slope instability
- Replacement of detectable tiles and painted guidelines at six stations
- Replacement of stairs at the Fullerton Transportation Center



- ROW acquisition to replace the San Juan Creek railroad bridge in the City of San Juan Capistrano, which will not preclude a future bicycle trail on the south end along the creek
- Emergency track stabilization in the City of San Clemente at Cyprus Shore, Casa Romantica, and Mariposa Point
- Repair riprap in Areas 1 and 2 and remove the pedestrian bridge in Area 3 in the City of San Clemente as identified in the Coastal Rail Resiliency Study
- Approximately 2,500 cubic yards of sand were placed at North Beach in the City of San Clemente

#### Underway:

- Award contract for slope stabilization and drainage improvements in the cities of Lake Forest, Mission Viejo and Laguna Niguel
- Construction of the San Juan Creek railroad bridge replacement in the City of San Juan Capistrano, led by Metrolink
- Construction of Area 3 catchment wall and restoration of the coastal trail in the City of San Clemente
- Rehabilitation of pedestrian audible warning system in the City of San Clemente
- Alternative analyses to evaluate solutions for coastal protective measures for Area 4 in the City of San Clemente as identified in the Coastal Rail Resiliency Study; associated environmental studies, conceptual designs, and permit preparation for Area 4
- Continue to seek inland and offshore sand sources to be environmentally cleared and permitted for placement on the beach for Areas 1, 2, and 4

**Project:** Sand Canyon Grade Separation

Status: PROJECT COMPLETE

Contact: Jim Beil, Capital Programs • (714) 560-5646

Summary: This project separated the local street from railroad tracks in the City of Irvine by constructing an underpass for vehicular traffic. Construction began on May 3, 2011, and the improvements opened to traffic on July 14, 2014. The project was completed, and construction acceptance was obtained from the City of Irvine on January 15, 2016. The final schedule is measured against an amended baseline scheduled established in the second quarter of FY 2010-11. The project completed the one-year warranty period, and no repairs were identified. The project closed out in January 2017.

**Project:** Tustin Metrolink Station Parking Structure

Status: PROJECT COMPLETE

Contact: Jim Beil, Capital Programs • (714) 560-5646

**Summary:** This early completion project provided additional parking at the Tustin Metrolink Station to meet requirements associated with MSEP by constructing a new four-story parking structure with approximately 735 spaces and on-site surface parking. Construction on the parking structure began on October 27, 2010, and opened to the public on September 22, 2011.






Project: Laguna Niguel to San Juan Capistrano Passing Siding Project

Status: PROJECT COMPLETE

Contact: Jim Beil, Capital Programs • (714) 560-5646



**PROJECT S** 

## TRANSIT EXTENSIONS TO METROLINK

To broaden the reach of Metrolink to other Orange County cities, communities, and activity centers, Project S includes a competitive program that allows cities to apply for funding to connect passengers to their final destination via transit extensions. There are currently two categories for this program: a fixed-guideway program (streetcar) and a rubber tire transit program.

**Project:** OC Streetcar

Status: Full Funding Grant Agreement Executed November 30, 2018; Construction Work Ongoing,

All Eight Vehicles Completed and Delivered, Preparations Underway for Start-Up

**Contact:** Jeff Mills, Rail • (714) 560-5925

Cleve Cleveland, Rail • (714) 560-5535

**Summary:** The OC Streetcar will serve the SARTC through Downtown Santa Ana, and the Civic Center to Harbor Boulevard in the City of Garden Grove. At the request of the two cities, OCTA is serving as the lead agency for the project. Construction on the project began on November 19, 2018.

### Construction

Construction is 95 percent complete. During the quarter, the OCS foundations and pole installations were completed along the alignment, while installation of the OCS contact wires continued. In addition, work continued along the Pacific Electric ROW, at the MSF, and on utility installations at various stations.

### **Vehicles**

All eight cars have been delivered to the MSF, with the final vehicle delivered on September 10, 2025. OCTA continued negotiations with the vehicle manufacturer regarding long-term storage and maintenance for the vehicles.



## **Operations**

Monthly coordination meetings continue to support system integration testing and ensure the streetcar is ready for safe and reliable operations. Bi-weekly meetings with OCTA and the operations and maintenance contractor continue to refine testing procedures and validate systems ahead of revenue service. In addition, the Operations and Maintenance contractor completed various documents, procedures, and forms in preparation of assuming operating responsibilities from the construction contractor. Training continued for operations staff, including vehicle operators and maintenance technicians.

### **Cost and Schedule**

The baseline cost and schedule is measured against an amended baseline cost and schedule established during the third quarter of FY 2024-25. In February 2025, the Board approved a revised project budget of \$649 million. The project is anticipated to begin revenue service in summer 2026.

**Project:** Bus and Station Van Extension Projects

Status: Last Service Completed on June 30, 2020; No Future Calls Anticipated

Contact: Charvalen Alacar, Planning • (714) 560-5401

**Summary:** Bus and station van extension projects help enhance the frequency of service in the Metrolink corridor by linking communities within the central core of Orange County to commuter rail. To date, the Board has approved one round of funding for bus and van extension projects, totaling over \$732,000. On July 23, 2012, the Board approved funding for one project in the City of Anaheim and three projects in the City of Lake Forest. The City of Lake Forest has cancelled all three projects. The Anaheim Canyon Metrolink Station Bus Connection project provided service between the Anaheim Canyon Metrolink station and the Anaheim Resort area; this project was completed on June 30, 2020, under Project S. The service continues under a Project V grant and is subject to meeting minimum performance requirements as part of the Project V program.

**PROJECT T** 

# METROLINK GATEWAYS

**Project:** Anaheim Regional Transportation Intermodal Center

Status: PROJECT COMPLETE

Contact: George Olivo, Capital Programs • (714) 560-5872

All a

Summary: This project constructed the ARTIC located at 2626 East Katella Avenue in the City of Anaheim. ARTIC is a major multimodal transportation hub serving commuters and residents in the City of Anaheim. In addition to OCTA buses and Metrolink trains, ARTIC provides transit connections to Pacific Surfliner Amtrak, Anaheim Resort Transit, shuttle and charter bus service, taxis, bicycles, other private transportation services available, and accommodates future high-speed rail trains. The City of Anaheim, which led the construction effort, began construction on September 24, 2012, and opened the facility to rail and bus service on December 6, 2014. This facility replaced the former Anaheim Metrolink Station that was located on the opposite side of the freeway in the Los Angeles Angels of Anaheim Stadium parking lot.



PROJECT U

## EXPAND MOBILITY CHOICES FOR SENIORS AND PERSONS WITH DISABILITIES

Project U expands mobility choices for seniors and persons with disabilities, and includes the SMP, the SNEMT Program, and the Fare Stabilization Program. Since inception, approximately \$151.7 million<sup>10,11,12</sup> in Project U funding has been provided under M2.

<sup>10</sup> Payments are made every other month (January, March, May, July, September, and November). July payments are based on June accruals, and therefore counted as June payments. The amount totaled for one FY quarter either covers one or two payments, depending on the months that fall within that quarter.

<sup>11</sup> Only includes disbursed funds. On May 28, 2024, the Board determined the City of Buena Park ineligible to receive net M2 revenues for five years pursuant to Section 10.4 of the M2 Ordinance. Disbursements of M2 revenues have been suspended until the City of Buena Park reestablishes eligibility.

<sup>12</sup>On May 12, 2025, the Board determined the City of Huntington Beach ineligible to receive net M2 revenues for five years pursuant to Section 10.4 of the M2 Ordinance. Disbursements of net M2 revenues have been suspended until the City of Huntington Beach reestablishes eligibility.

**Project:** Senior Mobility Program

Status: Ongoing

Contact: Jack Garate, Transit • (714) 560-5387

Summary: The SMP provides one percent of net M2 revenues to eligible local jurisdictions to provide transit services that best meet the needs of seniors living in their community. According to the SMP Funding and Policy Guidelines, M2 revenue is allocated to local jurisdictions proportionally, relative to the total county's senior population, by the residents aged 60 and above multiplied by available revenues. The remaining unallocated funds are distributed to the M2 Project U Fare Stabilization Program.

Since inception, more than \$43.1 million<sup>10,11,12</sup> has been provided to support more than 3.3 million boardings for seniors traveling to medical appointments, nutrition programs, shopping destinations, and senior and community center activities. This quarter, approximately \$656,000 <sup>10,11,12</sup> was paid out to 30 of the 32 participating cities that are currently active.

Project: Senior Non-Emergency Medical Transportation Program

Status: Ongoing

Contact: Jack Garate, Transit • (714) 560-5387

**Summary:** This program provides one percent of net M2 revenues to supplement existing countywide SNEMT services. Since inception, approximately \$46.2 million has been allocated to support more than 1.7 million SNEMT boardings<sup>13</sup>. This quarter, nearly \$770,000<sup>10</sup> in SNEMT funding was paid to the County of Orange.

<sup>&</sup>lt;sup>13</sup> The SNEMT program is operated by the County of Orange Office on Aging. Total boardings are calculated based on all services funded by M2 and the County of Orange.



**Project:** Fare Stabilization Program

Status: Ongoing

Contact: Sean Murdock, Finance • (714) 560-5685

**Summary:** From 2011 to 2015, one percent of net M2 revenues was dedicated to stabilizing fares and providing fare discounts for bus services and specialized ACCESS services for seniors and persons with disabilities. Effective January 28, 2016, an amendment to the M2 Ordinance adjusted this amount to 1.47 percent of net M2 revenues to be dedicated to the Fare Stabilization Program.

Approximately \$1.1 million in revenue was allocated this quarter to support the Fare Stabilization Program. The amount of funding utilized each quarter varies based on ridership. During the quarter, based on 2.6 million program-related boardings recorded on fixed-route and ACCESS services, approximately \$735,000 was utilized. The senior and disabled boardings recorded are based on pass sales and ACCESS boardings figures. Since inception, more than \$62.4 million has been allocated to support approximately 166 million program-related boardings.

**PROJECT V** 

# COMMUNITY-BASED TRANSIT/CIRCULATORS

Status: Service Updates

Contact: Charvalen Alacar, Planning • (714) 560-5401

**Summary:** This program provides funding for local jurisdictions to develop local bus transit services, such as community-based circulators and shuttles, which complement regional bus and rail services to meet needs in areas not adequately served by regional transit. To date, through five calls, the Board has awarded 49 projects and ten planning studies totaling approximately \$96.8 million<sup>14</sup>. Of the 49 transit circulator projects<sup>15</sup>, 21 are currently active, four are planned, 13 have been cancelled (primarily due to low ridership), and 11 have been completed.

On January 25, 2021, the Board approved changes to the Project V program guidelines to better support these key community services in a post-COVID-19 environment. Key revisions included modifying minimum performance standards and allowing for escalation in the subsidy per boarding and annual FY funding caps. Staff continued to work with local jurisdictions to update existing cooperative agreements to incorporate these programmatic changes.

<sup>&</sup>lt;sup>14</sup> Includes \$700,000 programming increase to the 2024 call Balboa Peninsula Trolley Service Continuation project, as approved by the Board on September 23, 2024, and confirmed on August 25, 2025.

<sup>&</sup>lt;sup>15</sup> Includes reinstatement of the \$1.65 million award from the 2018 Project V call to the City of San Clemente for the existing San Clemente Rides ride-hailing service. The 2018 Project V award was cancelled by the Board on December 10, 2018, and reinstated on August 14, 2023, to correct for issues in the service model that were encountered during the pandemic.



OCTA receives ridership reports from local agencies on a regular basis to monitor the success of these services against performance measures adopted by the Board. The most recent Project V ridership report was presented to the Board on August 25, 2025. The report identified that all of the active services met the ridership and service performance standards. The next ridership report is anticipated to be presented to the Board in February 2026. Lessons learned from the success of implemented services are incorporated into recommendations for future funding guidelines and programming recommendations.

**PROJECT W** 

## SAFE TRANSIT STOPS

Status: City-Initiated Improvements Underway or Completed

Contact: Charvalen Alacar, Planning • (714) 560-5401

**Summary:** This program provides funding for passenger amenities at the busiest transit stops across Orange County. Stop improvements are designed to ease transfers between bus lines and provide passenger amenities such as the installation of bus benches or seating, shelters, and lighting.

To date, through a competitive process, OCTA has issued three calls (July 2014, June 2019, and September 2020), which have awarded just over \$3.1 million to support improvements at 122 locations. Of the 122 projects, 94 have been completed, 18 are in various stages of implementation, and ten have been cancelled. Staff is reviewing M2 revenues and assessing the appropriate timing for the next call.



PROJECT X

## CLEAN UP HIGHWAY AND STREET RUNOFF THAT POLLUTES BEACHES

**Project:** Environmental Cleanup Program

Status: 15th Tier 1 Call Applications Under Review Contact: Dan Phu, Planning • (714) 560-5907

**Summary:** This program implements street and highway-related water quality improvement programs and projects that assist agencies countywide with federal Clean Water Act standards for urban runoff. It is intended to augment, not replace, existing transportation-related water quality expenditures and to emphasize high-impact capital improvements over local operations and maintenance costs. The ECAC is charged with making recommendations to the Board on the allocation of funds. These funds are allocated on a countywide, competitive basis to assist agencies in meeting the Clean Water Act standards for controlling transportation-related pollution.

The ECP is composed of a two-tiered funding process focusing on early priorities (Tier 1), and a second program designed to prepare for more comprehensive capital investments (Tier 2). All Orange County cities plus the County of Orange have received funding under this program. To date, there have been 14 rounds of funding under the Tier 1 grants program.

To date, 233 Tier 1 projects, totaling approximately \$40 million, have been awarded by the Board since 2011. Of the 233 projects, construction on 203 projects have been completed, 13 are in various stages of implementation, and 17 have been cancelled by the awarded agency. The 15th Tier 1 call was released on March 10, 2025. Applications were received on May 8, 2025. Based upon the project selection criteria in the CTFP guidelines, projects will be prioritized for Board consideration in October 2025.

It is estimated that 81.5 million gallons of trash have been captured since the inception of the program, which equates to over 14,400 trash truck loads of garbage that could have been deposited in Orange County streams and waters. Over time, the volume of trash captured is expected to increase.

To date, 26 Tier 2 projects totaling approximately \$35 million have been awarded by the Board since 2013. Of the 26 projects, construction on 18 projects have been completed, four projects are in progress, and four projects have been cancelled by the awarded agency. It is estimated that Tier 2-funded projects, once fully functional, will have an annual groundwater recharge and water savings potential of approximately 352 million gallons of water from infiltration, recharge facilities, and diversion to recycled water supply. The appropriate timing of the next Tier 2 call will be assessed and determined by funding availability as well as the number of viable projects from eligible agencies.



## FREEWAY MITIGATION

**Segment:** Environmental Mitigation Program

Status: Biological Permits Issued and Conservation Plan in Place

Contact: Adriann Cardoso, Planning • (714) 560-5915

Summary: Working in collaboration with the Wildlife Agencies, this program allocates funds to acquire land and fund habitat restoration projects to offset the environmental impacts of M2 freeway projects. In June 2017, OCTA received biological resource permits after completing a state and federal Conservation Plan. This Conservation Plan commits to protecting the natural habitat and wildlife on OCTA's Preserves, funding multiple habitat restoration projects, and minimizing impacts to resources during construction of M2 freeway projects, allowing streamlined project approvals for the M2 freeway projects with little additional coordination from the Wildlife Agencies. This program represents the culmination of years of collaboration and support by the Board, environmental community, and Wildlife Agencies. The OCTA Conservation Plan is unique, as it is only the second state/federal conservation plan approved in Orange County.

The Conservation Plan includes a streamlined process for coordination for streambed alteration agreements for portions of freeway projects that cross through streams and riverbeds. In 2017, the United States Army Corps of Engineers issued a programmatic permit to OCTA and Caltrans (as owner/operator of the state highway system). The State Board provided a letter to OCTA in 2018, which further secured assurances related to advanced mitigation and freeway project permit issuance. These efforts are the result of years of collaboration and constitute another groundbreaking milestone for the M2 EMP.

The Board has approved the acquisition of seven properties (Preserves) totaling 1,300 acres and 13<sup>16</sup> restoration projects totaling 350 acres. To date, nine restoration projects (one of these projects had two distinct areas) have been completed and have been approved by the Wildlife Agencies. The Board authorized \$42 million (inclusive of setting aside funds for long-term land management) for property acquisitions, \$10.5 million to fund habitat restoration activities, and \$2.5 million for conservation plan development and program support, for a total of approximately \$55 million.

The Conservation Plan requires the establishment of an endowment to fund the long-term management of the Preserves. The most recent Board-adopted 2024 Next 10 Plan confirms that OCTA will be able to continue endowment deposits of \$2.9 million annually. To date, OCTA has made ten endowment deposits. As of September 30, 2025, the endowment balance was \$38,595,652, which is above the target of \$35,788,429 for the first quarter of FY 2024-25. Based on the performance to date, current projections indicate that OCTA still remains on track to meet the endowment target of \$46.2 million in FY 2027-28; however, the performance of the endowment fund may affect the timeframe. The next report summarizing the status of the endowment is anticipated to be presented to the Board in December 2025. Staff will continue to oversee and provide endowment updates to the Board, Finance and Administration (F&A) Committee and the Environmental Oversight Committee (EOC) on a regular basis.

<sup>&</sup>lt;sup>16</sup> The project count was updated from 12 to 13 to reflect that one project covers two distinct areas with different criteria.



Resource management plans (RMP) for the Preserves were completed in 2018. These RMPs guide the management of the Preserves as outlined within the Conservation Plan. The RMPs will be reviewed and updated as necessary, approximately every five years. Updates to the documents are currently underway and are anticipated to include new figures depicting more recent plant and animal species information, documentation of completed management tasks, potential new tasks identified, and the incorporation of the recently completed FMPs. All revisions will be coordinated with the Wildlife Agencies, shared with the EOC, and posted on OCTA's website. Staff will continue to oversee and manage the Preserves until a long-term manager(s) is established.

Conservation Plan reports are completed annually. These reports include the tracking of impacts associated with covered freeway improvement projects, other management and monitoring activities on Preserves, status and activities, the progress of the restoration projects, plan administration, and public outreach activities. These reports take time to develop as they fold in multiple reports from various consultants and contractors working on the OCTA Preserves and the funded restoration projects through the end of every calendar year. Annual reports to date document that OCTA's activities are in compliance and on target with the Conservation Plan commitments. The annual report documenting the 2024 calendar year activities has been completed and reviewed by the Wildlife Agencies and will be shared with the EOC and Board in late-2025.

The EMP accomplishments have largely met the intent of the program. These efforts are the result of years of positive collaboration between OCTA and the aforementioned agencies, stakeholders, and the public. The success of this program has been recognized at the regional and national level. Through these efforts, pre-negotiated permit terms have helped streamline project implementation and reduce the required mitigation needs. Without the EMP's established process, additional mitigation-related requirements could have been incurred, resulting in increased project costs and schedule risks. The established permits and partnerships have also enabled swift response to other OCTA project needs.

Docent-led hikes and equestrian ride tours are offered throughout the year at various OCTA Preserves. The 2025 hike and ride schedule is available at <a href="https://www.PreservingOurLegacy.org">www.PreservingOurLegacy.org</a>.

As part of the safeguards in place for the M2 Program, a 12-member EOC makes recommendations on the allocation of environmental freeway mitigation funds and monitors the implementation of the Conservation Plan between OCTA and state and federal Wildlife Agencies. The EOC has led efforts with policy recommendations to the Board and has operated in an open and transparent manner which has garnered the trust of stakeholders, ranging from the environmental community to the recreational community to Orange County citizens. See the map of Preserves and funded restoration properties on the following page.





# PROGRAM MANAGEMENT OFFICE

Contact: Francesca Ching, M2 PMO Manager • (714) 560-5625

The M2 PMO provides inter-divisional coordination for all Measure M-related projects and programs. To ensure agency-wide compliance, the PMO holds a bimonthly committee meeting comprised of executive directors and key staff from each of the divisions, who meet to review significant issues and activities within the M2 programs. This quarter, the focus of the PMO has been on several major items, including the following:

### **Market Conditions Forecast and Risk Analysis**

On September 11, 2017, the Board was presented with a Next 10 Plan Market Conditions Forecast and Risk Analysis Report conducted by Dr. Wallace Walrod and Dr. Marlon Boarnet through a contract with the Orange County Business Council. The consultant team's analysis identified strong potential for OCTA to experience an increasing cost environment during the Next 10 Plan delivery years. This, coupled with a reduction in revenue, could present the potential for significant challenges in the delivery of M2 and the Next 10 Plan.

The Board directed staff to continue to work with the consultant team to monitor and track key early warning indicators and provide the Board with updates in a timeline consistent with updates on the M2 sales tax revenue forecast. The consultant team continues to analyze trends in material costs, labor costs, and general economic conditions to determine a range of potential cost impacts providing insight on OCTA's capital program twice a year.

During the quarter, the consultant team completed the update to the forecasting model and shared with staff the results. The analysis identified that OCTA may experience an uptick in inflationary pressures in 2026, 2027, and 2028. This outlook reflects a rise in residential building permits, unemployment rates in California, and construction labor and materials costs. While the Federal Reserve has made strides in getting inflation under control, tariffs have begun to have a measurable impact on short-term costs and continued uncertainty surrounding the impacts of economic, trade, and immigration policies which has resulted in slowed hiring trends as businesses struggle to forecast future needs. Adding to shifting government policies, the accelerating adoption of artificial intelligence technologies has also started to potentially slow overall job growth. In addition, wildfires have devastated communities in Los Angeles County, which may further impact construction cost pressures. The updated market conditions forecast is anticipated to be presented to the Board in October 2025, and information from this analysis will be incorporated into the M2 cash flow for the 2025 update of the Next 10 Plan.

### **Next 10 Delivery Plan**

On November 14, 2016, the Board adopted the Next 10 Plan, which provides guidance on the delivery of M2 projects and programs between FY 2016-17 and FY 2025-26. In December 2020, the Board approved to shift the timeframe to FY 2020-21 through FY 2029-30. The intent is for the Next 10 Plan to be a living document with delivery timeframes shifted to ensure revenue and project information stay current. The PMO monitors progress on the ten deliverables identified in the Next 10 Plan and provides status updates.



Annually, OCTA reviews the Next 10 Plan and M2 program assumptions based on changes to the revenue forecast and updated project cost and schedules. On November 12, 2024, the Board approved the 2024 Next 10 Plan, which spans FY 2024-25 to FY 2033-34. The 2024 update of the Next 10 Plan incorporated an updated sales tax revenue forecast of \$14 billion (supplemented with external revenue — Federal, State, and local dollars), insight from the updated construction market forecast, current programmed external revenues, revised bonding assumptions, and refined project information. Through this process, staff confirms that the M2 Program remains deliverable; however, this update continues to emphasize that Metrolink operations requires close monitoring. The next review of the Next 10 Plan is underway and anticipated to be presented to the Board in December 2025.

### **M2 Performance Assessment**

The M2 Ordinance includes a requirement for a performance assessment to be conducted at least once every three years to evaluate OCTA's efficiency and effectiveness in the delivery of M2 as committed to the voters. Five performance assessments have been completed covering FY 2006-07 through FY 2008-09, FY 2009-10 through FY 2011-12, FY 2012-13 through FY 2014-15, FY 2015-16 through FY 2017-18, and FY 2018-19 through FY 2020-21. Findings and recommendations are implemented as appropriate. The sixth assessment began in July 2024 and covers the period between July 1, 2021, and June 30, 2024. The consultant team presented the final report to the Board on March 10, 2025. The consultant's report reflected a positive assessment of OCTA's efficiency and effectiveness in the delivery of M2 projects and programs. While there were no significant findings, four recommendations for enhancements were made: improving transparency in project reporting, strengthening E-procurement evaluation processes, clarifying internal procedures related to contract approvals, and addressing the timeliness of grant payments.

To date, several actions have been completed to address these recommendations. To improve transparency in project reporting, staff incorporated details on how capital project costs and schedules are measured into the M2 Quarterly Report. The new e-procurement system was launched in September 2025, which included enhanced evaluation processes. Internal procedures related to contract approvals were updated in January 2025, and steps recommended by the payment process consultant have been initiated to improve the timeliness of grant payments. Actions to complete the remaining recommendations are underway and are anticipated to be completed by the end of FY 2025-26.

### M2 Ten-Year Review

The M2 Ordinance includes a provision to conduct a ten-year comprehensive review of M2 programs and projects. The ten-year review is intended to evaluate the performance of the overall program and may result in revisions to further improve performance. Due to the early initiation of project development activities prior to the start-up of revenue collection in 2011, the first review was completed in 2015. The second effort is underway. During the quarter, a ten-year review update was presented to the Executive Committee on August 28, 2025, highlighting five objectives to ensure the required elements in the M2 Ordinance are analyzed. Outreach continued this quarter with a second roundtable discussion with elected officials, two stakeholder briefings, and continued participation in various community events. Feedback from these activities will help guide the development of key findings and recommendations. The next update on the ten-year review efforts is anticipated to be presented to the Board in December 2025.



### **M2 Ordinance Tracking Matrix**

The M2 Ordinance includes numerous requirements that staff must follow to keep the commitment to Orange County voters through the passage of M2. The PMO annually updates the M2 Ordinance Tracking Matrix to verify that OCTA complies with all requirements detailed in the M2 Ordinance. The tracking matrix was finalized and shared with the TOC on June 10, 2025. This document is for PMO tracking purposes, but is also helpful to Taxpayer Oversight Committee (TOC) members during their annual compliance finding.

### **PMO M2 Tracking Tools**

The PMO has developed several tracking tools to assist in reporting consistency and increased transparency of the M2 program. See the following for a brief explanation of PMO M2 tracking tools and their current status:

### **Local Jurisdiction Fact Sheets**

Fact sheets have been created for the County of Orange and each of Orange County's 34 cities. The city fact sheets provide data on transportation and transit projects (funded through M2, state, and federal grants) in a format that emphasizes key points concisely on a single printed page. The city fact sheets are utilized when speaking with the jurisdictions to provide a summary overview of how OCTA has provided the local agency with funding (M2 and other) and transportation improvements. This quarter, the update of the city fact sheets through June 2025 was completed and uploaded to the OCTA website. The update incorporated the 2024 ECP Tier 1 and Tier 2 projects approved by the Board on October 14, 2024, the 2025 RCP and RTSSP projects approved by the Board on April 14, 2025, the September 2024 semi-annual review of CTFP projects approved by the Board on December 9, 2024, and programming updates.

### Engineer's Estimate versus Bids Tracking

The estimate versus bid tracking process allows the PMO to monitor the bidding environment for capital projects in the M2 Program. Capital projects that were planned for and began construction early in the M2 Program have shown cost savings due to a favorable bidding environment during the recession. For these earlier M2 projects, savings can be primarily traced back to construction costs.

Highway project constructions bids in the region continues to reflect escalating labor, material, and equipment costs. Workforce availability may exacerbate the construction and manufacturing labor markets, and there is uncertainty around the impacts of tariffs, additional future tariffs, and their potential duration. Recent market conditions analyses have indicated that OCTA may experience a tempering of cost pressures related to decreased demand for construction services, however, a lack of labor resources, and high construction material and labor costs still remain. It should be noted that the engineer's estimate is based on several factors – such as bidding history and historical and current market rates (materials, labor, equipment, etc.) – and adjusted accordingly for the project's conditions. Because the estimate uses prior information, there may be a lag between an uptick or a downtick in the market.

Project G (SR-57 northbound from Orangewood Avenue to Katella Avenue) was advertised for construction on July 8, 2025, bids opened on September 4, 2025, and the project was awarded on



September 26, 2025. The lowest, responsive, and responsible bidder was approximately seven percent below the engineer's estimate. In addition, the easterly segment of Project I (SR-91, Acacia Street to La Palma Avenue) was advertised for construction on May 12, 2025, and bids opened on August 12, 2025. The apparent lowest, responsive, and responsible bidder was approximately 4.7 percent below the engineer's estimate. Furthermore, Project B segment 1 (I-5, I-405 to Yale Avenue) was advertised for construction on August 18, 2025, and segment 2 (I-5, Yale Avenue to SR-55) was advertised for construction on August 11, 2025. Bids for both projects are anticipated to be opened next quarter. Staff will continue to monitor the construction market and update the spreadsheet as appropriate.

## **M2 Administrative Safeguards**

M2 includes a one percent cap on administrative expenses for salaries and benefits of OCTA administrative staff on an annual basis. In a legal opinion on M2, it was determined that in years where administrative salaries and benefits are above one percent, only one percent can be allocated with the difference borrowed from other non-M2 fund sources. Conversely, in years where administrative salaries and benefits are below one percent, OCTA can still allocate the full one percent for administrative salaries and benefits but may use the unused portion to repay the amount borrowed from prior years in which administrative salaries and benefits were above one percent.

Based on the original M2 revenue projections, OCTA expected to receive \$24.3 billion in M2 funds, with one percent of total revenues available to fund administrative salaries and benefits over the life of the program. As M2 revenue projections declined (\$14 billion or 42 percent lower as of June 30, 2025) because of economic conditions, the funds available to support administrative salaries and benefits have also declined from the original expectations. While revenue has declined, the administrative effort needed to deliver M2 remains the same. Additionally, the initiation of the Early Action Plan (EAP) in 2007 required administrative functions four years prior to revenue collection. While the EAP resulted in project savings and significant acceleration of the program, administrative functions were required during this time with associated administrative costs.

As a result of the aforementioned factors, OCTA has incurred higher than one percent administrative costs. OCTA has Board approval to use funds from the Orange County Unified Transportation Trust (OCUTT) fund to cover costs above the one percent, and to repay those funds with interest in future years when OCTA administrative costs fall below the one percent cap. OCTA has borrowed approximately \$5.3 million from OCUTT to date. As of September 30, 2025, the total borrowings to date from OCUTT along with accrued interest are paid off.

Staff meets quarterly to review all labor costs to ensure costs attributed to the one percent cap are accurately reported and that there are no misplaced project-related costs.

### **Taxpayer Oversight Committee**

The M2 Ordinance requires a TOC to oversee compliance with the M2 Ordinance. With the exception of the elected Auditor Controller of Orange County, who is identified as the chair in the M2 Ordinance, all other



members cannot be elected or appointed officials. Members are recruited and screened for expertise and experience independently by the Grand Jurors Association of Orange County and are selected from the qualified pool by lottery. The TOC used to meet every other month, but the TOC voted on April 11, 2023, to meet quarterly beginning in FY 2023-24. The responsibilities of the 11-member M2 TOC are to:

- Approve, by a vote of no less than two-thirds of all committee members, any amendments to the Plan proposed by OCTA which changes funding categories, programs, or projects identified on page 31 of the Plan
- Receive and review the following documents submitted by each eligible jurisdiction:
  - o Congestion Management Program
  - Mitigation Fee Program
  - Expenditure Report
  - o Local Traffic Signal Synchronization Plan
  - Pavement Management Plan
- Review yearly audits and hold an annual public hearing to determine whether OCTA is proceeding in accordance with the Plan
- Receive and review the triennial performance assessments of the Orange County Local Transportation Authority to assess the performance of OCTA in carrying out the purposes of the Ordinance
- The TOC Chair shall annually certify whether M2 funds have been spent in compliance with the Plan

On September 9, 2025, the TOC received presentations on the M2 Quarterly Report for the fourth quarter of FY 2024-25, Measure M2 Ten-Year Review, an overview of the CTFP, and a TOC roles and purview update.

Two subcommittees assist the TOC with their safeguard responsibilities: the AER Subcommittee and the Audit Subcommittee. The AER Subcommittee meets a few times per year, as needed, to receive and review the following documents submitted by local jurisdictions to be deemed eligible to receive M2 funding: Congestion Management Program, Mitigation Fee Program, Local Signal Synchronization Plan, Pavement Management Plan, and Expenditure Reports. The Audit Subcommittee meets as needed and is responsible for reviewing the quarterly M2 Revenue and Expenditure Reports and the annual M2 Audit, as well as any other items related to M2 audits.

# M2 FINANCING AND SCHEDULE OF FUNDING

Contact: Sam Kaur, Revenue and Grants • (714) 560-5889

### **Revenue Forecast and Collection**

OCTA contracts with three universities (Chapman University; California State University, Fullerton; and University of California, Los Angeles) to provide a long-range forecast of taxable sales to forecast M2 revenues for purposes of planning projects and program expenditures.



In the past, OCTA averaged the three university taxable sales projections to develop a long-range forecast of M2 taxable sales. On March 28, 2016, the Board approved a revised sales tax forecast methodology as part of the FY 2016-17 budget development process. This methodology includes a more conservative approach by utilizing the MuniServices, LLC forecast for the first five years, and the three-university average for the remaining years.

OCTA continuously monitors actual sales tax receipts, and revenue forecast information is provided by MuniServices, LLC quarterly. As required by law, OCTA pays the California Department of Tax and Fee Administration a fee to collect the sales tax. The M2 Ordinance estimated this fee to be 1.5 percent of the revenues collected over the life of the program.

### **Current Forecast**

Originally, the 2005 projections for M2 sales tax collections were anticipated at \$24.3 billion. As of September 2025, the current revised total nominal sales tax collections over the life of M2 is estimated to be \$14 billion, which represents a year-over-year decrease of \$800 million in forecasted sales tax when compared to last year's forecast.

MuniServices, LLC provided their sales tax forecasts to the F&A Committee on May 14, 2025, followed by the sales tax forecast from Chapman University on June 11, 2025, and from University of California, Los Angeles on June 25, 2025. During the quarter, California State University, Fullerton provided their sales tax forecast presentation to the F&A Committee on July 23, 2025.

OCTA remains in a strong financial position, supported by healthy reserve levels and the program's built-in consideration of economic uncertainties, which together provide a solid cushion against potential revenue shortfalls or increases in costs. The agency is actively monitoring various factors, including inflation, interest rates, and demographic changes in Orange County to assess their potential impact on sales tax revenues. In light of the observed revenue decline and economic uncertainties, OCTA prioritizes fiscal stewardship and proactive financial planning to ensure our commitment to the public; promises made, promises kept.

The next updated forecast is anticipated to be presented to the Board in October 2025. As a reference, there is no projected growth for FY 2025-26.

46



(\$ in thousands)		Quarter Ended Jul 1, 2025 - Sept 30, 2025	Year to Date Jul 1, 2025 - Sept 30, 2025	Period from Inception to Sept 30, 2025
			(A)	(B)
Revenues:				
Sales taxes	\$	114,841	\$ 114,841	\$ 4,919,154
Other agencies' share of Measure M2 costs: Project related		5,050	5,050	901,118
Non-project related		-	-	454
Interest:				
Operating:		1 000	4.000	44.040
Project related Non-project related		1,290 10,096	1,290 10,096	11,349 163,102
Bond proceeds		-	-	104,570
Debt service		178	178	4,344
Commercial paper		-	-	393
Right-of-way leases		83	83	2,177
Project related Non-project related		- 83	- 83	2,177
Proceeds on sale of assets held for resale		-	-	17,597
Donated assets held for resale				•
Project related		-	-	2,071
Miscellaneous: Project related				331
Non-project related		- -		125
Total revenues		131,538	131,538	6,126,802
		131,000	131,336	0,120,002
Expenditures: Supplies and services:				
Sales tax administration fees		915	915	46,219
Professional services:		0.0	0.0	.0,2.0
Project related		1,795	1,795	624,503
Non-project related		107	107	42,260
Administration costs: Project related		3,204	3,204	146,640
Non-project related:		3,204	3,204	140,040
Salaries and Benefits		1,250	1,250	50,823
Other		2,302	2,302	87,747
Other:		40	10	7.055
Project related Non-project related		40 43	40 43	7,955 6,426
Payments to local agencies:		40	40	0,420
Project related		16,953	16,953	1,564,666
Capital outlay:		.,	.,	,
Project related		3,955	3,955	2,535,301
Non-project related		-	-	31
Debt service: Principal payments on long-term debt		_	_	138,355
Interest on long-term debt and		<u>-</u>	_	130,333
commercial paper		11,775	11,775	398,211
Total expenditures		42,339	42,339	5,649,137
Excess (deficiency) of revenues				
over (under) expenditures		89,199	89,199	477,665
Other financing sources (uses):				
Transfers out:				
Project related		(4,282)	(4,282)	(837,391)
Transfers in:		540	540	505 004
Project related Bond proceeds		543	543	595,061 1,068,603
Payment to refunded bond escrow agent				(312,829)
Total other financing sources (uses)		(3,739)	(3,739)	513,444
Excess (deficiency) of revenues				
over (under) expenditures and other sources (uses)	\$	85,460	\$ 85,460	\$ 991,109
(4500)	<u>-</u>	23,100	. 55,100	. 33.,100



(\$ in thousands)		uarter Ended 25 - Sept 30, 2025 (actual)		Year to Date 025 - Sept 30, 2025 (actual)	Period from Inception through Sept 30, 2025 (actual)	Octol tl Marc	riod from per 1, 2025 nrough h 31, 2041 precast)		Total
Revenues:				(C.1)	(D.1)		(E.1)		(F.1)
Sales taxes	\$	114,841	\$	114,841	\$ 4,919,154	\$	8,300,106	\$	13,219,260
Operating interest Subtotal		10,096 124.937		10,096 124.937	 163,102 5.082,256		441,054 8,741,160		604,156 13,823,416
Subtotal		124,937		124,931	 5,062,250	-	0,741,100	-	13,623,410
Other agencies share of M2 costs		-		-	454		-		454
Right-of-way leases		-		-	17		-		17
Miscellaneous Total revenues		124,937		124,937	 5,082,852	-	8,741,160		125 13,824,012
rotal revenues		124,937		124,937	5,062,652		0,741,100		13,024,012
Administrative expenditures:									
Sales tax administration fees		915		915	46,219		62,315		108,534
Professional services		107		107	38,485		66,303		104,788
Administration costs: Salaries and Benefits		1,250		1.250	50,823		85,644		136,467
Other		2,302		2,302	87,747		147,618		235,365
Other		43		43	2,590		4,400		6,990
Payments to local agencies:					_,,,,,		.,		-,
Capital outlay		-		-	31		-		31
Environmental cleanup		567		567	 56,076		165,976		222,052
Total expenditures		5,184		5,184	 281,971		532,256	_	814,227
Net revenues	\$	119,753	\$	119,753	\$ 4,800,881	\$	8,208,904	\$	13,009,785
				(C.2)	(D.2)		(E.2)		(F.2)
Financing expenditures:									
Debt interest expense		11,775		11,775	398,211 3,775		241,199		639,410
Professional services Other		-		-	3,775 3,836		-		3,775 3,836
Total financing expenditures		11,775		11,775	 405,822	-	241,199	_	647,021
• •									
Interest revenue:									
Interest revenue from bond proceeds		-		- 470	104,570		-		104,570
Interest revenue from debt service funds Interest revenue from commercial paper		178		178	4,344 393		11,779		16,123 393
Total bond revenues		178	-	178	 109,307		11,779	_	121,086
rotal bond revenues	-				 ·	-		_	
Net financing expenditures:	\$	11,597	\$	11,597	\$ 296,515	\$	229,420	\$	525,935



Project	Description (G) (\$\\$ in thousands)  Freeways (43% of Net Revenue)	Total Net Revenues Inception to March 31, 2041 (actual) + (forecast) (H)		Net Revenues Inception to Sept 30, 2025 (actual)		Expenditures Inception to Sept 30, 2025 (actual)		Reimbursements Inception to Sept 30, 2025 (actual)  (K)		(J) - (K) = (L) Net M2 Cost Inception to Sept 30, 2025 (actual) (L)
Α	I-5 Santa Ana Freeway Interchange Improvements \$	5 512.782	\$	189.227	\$	10.908	\$	8.786	\$	2.122
В	I-5 Santa Ana/SR-55 to El Toro	327,526	Ψ	120.864	Ψ	64.741	Ψ	24,059	Ψ	40.682
C	I-5 San Diego/South of El Toro	684,073		252,437		461,858		53,044		408,814
D	I-5 Santa Ana/San Diego Interchange Upgrades	281,485		103,874		3.268		527		2.741
E	SR-22 Garden Grove Freeway Access Improvements	130,923		48.313		5		-		5
F	SR-55 Costa Mesa Freeway Improvements	399.316		147.356		183.636		80.113		103.523
G	SR-57 Orange Freeway Improvements	282.248		104,156		61.105		15,078		46,027
Н	SR-91 Improvements from I-5 to SR-57	152,744		56,366		34,961		824		34,137
1	SR-91 Improvements from SR-57 to SR-55	454,412		167,688		80,623		77,951		2,672
J	SR-91 Improvements from SR-55 to County Line	384,259		141,800		18,675		17,185		1,490
K	I-405 Improvements between I-605 to SR-55	1,170,453		431,920		1,711,805		380,194		1,331,611
L	I-405 Improvements between SR-55 to I-5	348,801		128,715		9,249		6,954		2,295
М	I-605 Freeway Access Improvements	21,821		8,052		10,209		16		10,193
N	All Freeway Service Patrol	163,654		60,392		17,023		-		17,023
	Freeway Mitigation	279,710		103,219		64,187		12,197		51,990
	Subtotal Projects	5,594,207		2,064,379		2,732,253		676,928		2,055,325
	Net Finance Expenditures	-				203,530		<u> </u>		203,530
	Total Freeways <u>s</u>	5,594,207	\$	2,064,379	\$	2,935,783	\$	676,928	\$	2,258,855 51.0%
	Street and Roads Projects (32% of Net	Revenues)								
0	Regional Capacity Program	1.300.995	\$	480.094	\$	842.816	\$	507,884	\$	334,932
Р	Regional Traffic Signal Synchronization Program	520,375		192,029		141,117	•	29,393		111,724
Q	Local Fair Share Program	2,341,761		864,159		833,078		77		833,001
	Subtotal Projects Net Finance Expenditures	4,163,131		1,536,282		1,817,011 59.634		537,354		1,279,657 59,634
	Tion I mano Exponditures					00,004				00,004
	Total Street and Roads Projects	4,163,131	\$	1,536,282	\$	1,876,645	\$	537,354	\$	1,339,291 30.2%



Project	Description (G) (\$ in thousands)  Transit Projects (25% of Net Re	M (ac	tal Net Revenues Inception to March 31, 2041 ttual) + (forecast) (H)		Net Revenues Inception to Sept 30, 2025 (actual)		Expenditures Inception to Sept 30, 2025 (actual)		Reimbursements Inception to Sept 30, 2025 (actual) (K)		(J) - (K) = (L)  Net M2 Cost Inception to Sept 30, 2025 (actual)  (L)
Б	• •	\$		•	466,228	œ.	524,388	e	100.000	¢.	424 240
R S	High Frequency Metrolink Service Transit Extensions to Metrolink	Ъ	1,297,533 1,148,463	\$	400,228	\$	306,960	\$	100,069 151,974	\$	424,319 154,986
T	Metrolink Gateways		66,496		42,894		98,220		60,956		37,264
Ü	Expand Mobility Choices for Seniors and Persons		00,430		42,094		30,220		00,900		37,204
J	with Disabilities		451,116		160,704		154,812		88		154,724
V	Community Based Transit/Circulators		260,127		95,992		24,606		1,998		22,608
W	Safe Transit Stops		28,712		10,595		2,130		26		2,104
	'		-,		-,		,				
	Subtotal Projects		3,252,447		1,200,220		1,111,116		315,111		796,005
	Net Finance Expenditures		-		-		33,351		-		33,351
	Total Transit Projects	\$	3,252,447	\$	1,200,220	\$	1,144,467	\$	315,111	\$	829,356
	%										18.7%
	Measure M2 Program	\$	13,009,785	\$	4,800,881	\$	5,956,895	\$	1,529,393	\$	4,427,502
Project	Description	N	Total Revenues Inception to March 31, 2041 Stual) + (forecast)		Revenues Inception to Sept 30, 2025 (actual)		Expenditures Inception to Sept 30, 2025		Reimbursements Inception to Sept 30, 2025 (actual)		Net M2 Cost Inception to Sept 30, 2025 (actual)
Project	(G)	(au	luar) + (lurecast)								(actual)
			, , ,				(actual)		, ,		(1)
	* /		(H.1)		(1.1)		(J)		(K)		(L)
	(\$) (\$ in thousands) Environmental Cleanup (2% of R	Revenues	(H.1)				. ,		, ,		(L)
X	(\$ in thousands) Environmental Cleanup (2% of R	Revenues	(H.1)				. ,		, ,		(L)
х	(\$ in thousands)	Revenues \$	(H.1)	\$		\$	. ,	\$	, ,	\$	(L) 55,765
X	(\$ in thousands)  Environmental Cleanup (2% of R  Clean Up Highway and Street Runoff		(H.1)	\$	(1.1)	\$	(J)	\$	(K)	\$	
x	(\$ in thousands)  Environmental Cleanup (2% of R  Clean Up Highway and Street Runoff		(H.1)	\$	(1.1)	\$	(J)	\$	(K)	\$	
Х	(\$ in thousands)  Environmental Cleanup (2% of R  Clean Up Highway and Street Runoff that Pollutes Beaches		(H.1) (S) 276,468	\$	(1.1)	\$	(J) 56,076	\$	(K) 311	\$	55,765
X	(\$ in thousands)  Environmental Cleanup (2% of R  Clean Up Highway and Street Runoff that Pollutes Beaches  Net Finance Expenditures  Total Environmental Cleanup		(H.1) (S) 276,468	\$	(1.1)	\$	(J) 56,076	\$	(K) 311	\$	55,765 - 55,765
X	(\$ in thousands)  Environmental Cleanup (2% of R  Clean Up Highway and Street Runoff that Pollutes Beaches  Net Finance Expenditures	\$	(H.1)  276,468		101,645		56,076 -	_	(K) 311_		55,765
х	(\$ in thousands)  Environmental Cleanup (2% of R  Clean Up Highway and Street Runoff that Pollutes Beaches  Net Finance Expenditures  Total Environmental Cleanup	\$	(H.1)  276,468		101,645		56,076 -	_	(K) 311_		55,765 - 55,765
Х	(\$ in thousands)  Environmental Cleanup (2% of R  Clean Up Highway and Street Runoff that Pollutes Beaches  Net Finance Expenditures  Total Environmental Cleanup	\$	(H.1)  276,468		101,645		56,076 -	_	(K) 311_		55,765 - 55,765
X	Environmental Cleanup (2% of R Clean Up Highway and Street Runoff that Pollutes Beaches  Net Finance Expenditures  Total Environmental Cleanup %  Taxpayer Safeguards and A	\$ \$ uudits	(H.1) 276,468 - 276,468	\$	101,645	\$	56,076 - 56,076	\$	(K) 311_	\$	55,765 - 55,765 1.1%
X	Environmental Cleanup (2% of R Clean Up Highway and Street Runoff that Pollutes Beaches  Net Finance Expenditures  Total Environmental Cleanup %  Taxpayer Safeguards and A Collect Sales Taxes (1.5% of Sales Taxes)	\$	(H.1)  276,468		101,645		56,076 -	_	(K) 311_		55,765 - 55,765 1.1% 46,219
X	Environmental Cleanup (2% of R Clean Up Highway and Street Runoff that Pollutes Beaches  Net Finance Expenditures  Total Environmental Cleanup %  Taxpayer Safeguards and A	\$ \$ uudits	(H.1) 276,468 - 276,468	\$	101,645	\$	56,076 - 56,076	\$	(K) 311_	\$	55,765 - 55,765 1.1%
X	Environmental Cleanup (2% of R Clean Up Highway and Street Runoff that Pollutes Beaches  Net Finance Expenditures  Total Environmental Cleanup %  Taxpayer Safeguards and A Collect Sales Taxes (1.5% of Sales Taxes)	\$ \$ uudits	(H.1) 276,468 - 276,468	\$	101,645	\$	56,076 - 56,076	\$	(K) 311_	\$	55,765 - 55,765 1.1% 46,219
X	Environmental Cleanup (2% of R Clean Up Highway and Street Runoff that Pollutes Beaches  Net Finance Expenditures  Total Environmental Cleanup %  Taxpayer Safeguards and A Collect Sales Taxes (1.5% of Sales Taxes)	\$ \$ uudits	(H.1) 276,468 - 276,468	\$	101,645	\$	56,076 - 56,076	\$	(K) 311_	\$	55,765 - 55,765 1.1% 46,219



M	2 Funds	
ENTITY	1ST QUARTER FY 2025-26	FUNDS TO DATE*
ALISO VIEJO	\$177,489	\$10,272,835
ANAHEIM	\$1,480,208	\$86,574,986
BREA	\$239,812	\$14,775,078
BUENA PARK	\$0**	\$20,145,666**
COSTA MESA	\$616,316	\$37,766,850
CYPRESS	\$214,120	\$13,442,657
DANA POINT	\$143,369	\$8,680,779
FOUNTAIN VALLEY	\$262,925	\$16,021,090
FULLERTON	\$557,908	\$33,807,649
GARDEN GROVE	\$627,660	\$38,469,602
HUNTINGTON BEACH	\$0***	\$47,954,002***
IRVINE	\$1,346,140	\$73,594,746
LAGUNA BEACH	\$106,248	\$6,516,947
LAGUNA HILLS	\$137,453	\$8,703,624
LAGUNA NIGUEL	\$277,130	\$17,132,734
LAGUNA WOODS	\$55,424	\$3,318,261
LA HABRA	\$221,071	\$13,699,494
LAKE FOREST	\$342,869	\$20,765,502
LA PALMA	\$59,451	\$3,955,878
LOS ALAMITOS	\$54,044	\$3,343,830
MISSION VIEJO	\$379,043	\$23,711,526
NEWPORT BEACH	\$450,092	\$28,201,310
ORANGE	\$699,704	\$42,834,121
PLACENTIA	\$205,644	\$12,051,095
RANCHO SANTA MARGARITA	\$173,597	\$10,876,871



M	2 Funds	
ENTITY	1ST QUARTER FY 2025-26	FUNDS TO DATE*
SAN CLEMENTE	\$240,051	\$14,677,448
SAN JUAN CAPISTRANO	\$164,442	\$9,856,232
SANTA ANA	\$1,126,751	\$70,793,561
SEAL BEACH	\$99,716	\$6,305,008
STANTON	\$129,904	\$7,745,758
TUSTIN	\$395,814	\$23,461,639
VILLA PARK	\$22,011	\$1,348,593
WESTMINSTER	\$344,090	\$21,801,902
YORBA LINDA	\$254,477	\$15,608,285
COUNTY UNINCORPORATED	\$1,021,902	\$54,774,877
TOTAL M2 FUNDS	\$12,626,874	\$822,990,435

<sup>\*</sup> Only includes disbursed funds.

### Withheld funds are listed below.

ENTITY	1ST QUARTER FY 2025-26	FUNDS TO DATE
BUENA PARK	\$381,499	\$2,900,807
HUNTINGTON BEACH	\$805,217	\$2,250,514
TOTAL M2 FUNDS WITHHELD	\$1,186,716	\$5,151,321

<sup>\*\*</sup> On May 28, 2024, the Board determined the City of Buena Park ineligible to receive net M2 revenues for five years pursuant to Section 10.4 of the M2 Ordinance. Disbursements of net M2 revenues have been suspended until the City of Buena Park reestablishes eligibility.

<sup>\*\*\*</sup> On May 12, 2025, the Board determined the City of Huntington Beach ineligible to receive net M2 revenues for five years pursuant to Section 10.4 of the M2 Ordinance. Disbursements of net M2 revenues have been suspended until the City of Huntington Beach reestablishes eligibility.



Green = Forecast milestone meets or exceeds plan

Yellow = Forecast milestone is one to three months later than plan

Red = Forecast milestone is over three months later than plan

Non-bolded = Planned/Baseline

	Cost			edule	
Capital Projects	Baseline/Forecast	2 1/		orecast	2 11
	(millions)	Complete Environmental	Complete Design	Award Contract	Complete Construction
Freeway Projects:					
I-5, SR-55 to SR-57	\$38.1	Jun-13	Mar-17	Dec-17	Apr-21
Project A	\$38.9	Apr-15	Jun-17	Nov-18	Jan-21
I-5, I-405 to Yale Avenue	\$280.6	Aug-18	May-24	Feb-26	Sep-29
Project B	\$388.1	Jan-20	Nov-24	Jan-26	Aug-29
I-5, Yale Avenue to SR-55	\$238.3	Aug-18	Feb-25	Mar-26	Sep-29
Project B	\$327.9	Jan-20	Aug-24	Jan-26	Nov-29
I-5, Pico to Vista Hermosa	\$113.0	Dec-11	Oct-13	Dec-14	Aug-18
Project C	\$83.6	Oct-11	Oct-13	Dec-14	Aug-18
I-5, Vista Hermosa to Pacific Coast Highway	\$75.6	Dec-11	Feb-13	Dec-13	Mar-17
Project C	\$75.3	Oct-11	May-13	Jun-14	Jul-17
I-5, Pacific Coast Highway to San Juan Creek Road	\$70.7	Dec-11	Jan-13	Oct-13	Sep-16
Project C	\$74.3	Oct-11	Jan-13	Dec-13	Jul-18
I-5, SR-73 to Oso Parkway	\$151.9	Jun-14	Jan-18	Dec-18	Apr-25
Project C & D	\$229.4	May-14	Aug-18	Dec-19	Jul-25
I-5, Oso Parkway to Alicia Parkway	\$196.2	Jun-14	Jun-17	Jun-18	Nov-23
Project C & D	\$230.3	May-14	Dec-17	Mar-19	Dec-24
I-5, Alicia Parkway to El Toro Road	\$133.6	Jun-14	Jun-18	May-19	Oct-24
Project C	\$227.3	May-14	May-19	Sep-20	Aug-25
I-5, SR-73 to El Toro Road (Landscape)	TBD	N/A	N/A	N/A	N/A
Project C	\$12.4	N/A	Oct-24	May-25	Dec-26
I-5, I-5/El Toro Road Interchange	TBD	Apr-26	TBD	TBD	TBD
Project D	TBD	Apr-27	TBD	TBD	TBD

<sup>\*</sup>Status through September 2025. For detailed project information, please refer to the individual project section within this report.

Green = Forecast milestone meets or exceeds plan

Yellow = Forecast milestone is one to three months later than plan

Red = Forecast milestone is over three months later than plan

Non-bolded = Planned/Baseline

Capital Projects	Cost Baseline/Forecast			edule forecast	
oupitui i rojecto	(millions)	Complete Environmental	Complete Design	Award Contract	Complete Construction
I-5, I-5/Ortega Interchange	\$90.9	Jun-09	Nov-11	Aug-12	Sep-15
Project D	\$79.8	Jun-09	Dec-11	Aug-12	Jan-16
I-5, I-5/Ortega Interchange (Landscape)	N/A	N/A	N/A	N/A	N/A
Project D	N/A	N/A	Oct-14	Sep-15	Sep-16
SR-55, I-405 to I-5	\$410.9	Nov-13	Apr-20	May-22	Feb-27
Project F	\$505.7	Aug-17	Apr-20	May-22	Mar-27
SR-55, I-5 to SR-91	\$131.3	Jan-20	Jul-25	Jul-26	Oct-29
Project F	\$202.1	Mar-20	Dec-25	Apr-27	Jul-30
SR-57 Northbound (NB), Orangewood Avenue to Katella Avenue	\$71.8	Dec-18	Jul-24	Nov-25	Jun-28
Project G	\$135.4	Mar-19	Aug-24	Oct-25	Jun-28
SR-57 (NB), Katella Avenue to Lincoln Avenue	\$78.7	Jul-09	Nov-10	Aug-11	Sep-14
Project G	\$38.0	Nov-09	Dec-10	Oct-11	Apr-15
SR-57 (NB), Katella Avenue to Lincoln Avenue (Landscape)	N/A	N/A	N/A	N/A	N/A
Project G	N/A	N/A	Jul-10	Sep-17	Jun-18
SR-57 (NB), Orangethorpe Avenue to Yorba Linda Boulevard	\$80.2	Dec-07	Dec-09	Oct-10	May-14
Project G	\$52.3	Dec-07	Jul-09	Oct-10	Nov-14
SR-57 (NB), Yorba Linda Boulevard to Lambert Road	\$79.3	Dec-07	Dec-09	Oct-10	Sep-14
Project G	\$54.1	Dec-07	Jul-09	Oct-10	May-14
SR-57 (NB), Orangethorpe Avenue to Lambert Road (Landscape)	N/A	N/A	N/A	N/A	N/A
Project G	N/A	N/A	Aug-17	Feb-18	Apr-19
SR-57 (NB), Lambert Road to Tonner Canyon	TBD	TBD	TBD	TBD	TBD
Project G	TBD	Mar-29	TBD	TBD	TBD

<sup>\*</sup>Status through September 2025. For detailed project information, please refer to the individual project section within this report.



Green = Forecast milestone meets or exceeds plan

Yellow = Forecast milestone is one to three months later than plan Red = Forecast milestone is over three months later than plan

Non-bolded = Planned/Baseline

0.2510.054	Cost Baseline/Forecast			edule orecast	
Capital Projects	(millions)	Complete Environmental	Complete Design	Award Contract	Complete Construction
SR-91 Westbound (WB), I-5 to SR-57	\$78.1	Apr-10	Feb-12	Nov-12	Apr-16
Project H	\$59.2	Jun-10	Apr-12	Jan-13	Jun-16
SR-91 Westbound (WB), I-5 to SR-57 (Landscape)	N/A	N/A	N/A	N/A	N/A
Project H	N/A	N/A	Aug-16	Mar-17	Nov-17
SR-91, SR-55 to Lakeview Avenue (Segment 1)	\$108.6	Oct-18	Jan-23	Feb-24	Mar-28
Project I	\$140.7	Jun-20	Mar-23	Jan-25	Mar-28
SR-91, La Palma Avenue to SR-55 (Segment 2)	\$208.4	Oct-18	Jul-23	Jul-24	Mar-28
Project I	\$380.7	Jun-20	Jan-25	Jun-26	Sep-30
SR-91, Acacia Street to La Palma Ave (Segment 3)	\$147.7	Oct-18	Apr-24	Apr-25	Sep-28
Project I	\$257.5	Jun-20	Oct-24	Sep-25	Apr-29
SR-91 (WB), Tustin Interchange to SR-55	\$49.9	Jul-11	Mar-13	Oct-13	Jul-16
Project I	\$42.5	May-11	Feb-13	Oct-13	Jul-16
SR-91, SR-55 to SR-241	\$128.4	Jul-09	Jan-11	Sep-11	Dec-12
Project J	\$79.7	Apr-09	Aug-10	May-11	Mar-13
SR-91, SR-55 to SR-241 (Landscape)	N/A	N/A	N/A	N/A	N/A
Project J	N/A	N/A	Feb-13	Oct-13	Feb-15
SR-91 Eastbound, SR-241 to SR-71	\$104.5	Dec-07	Dec-08	Jul-09	Nov-10
Project J	\$57.8	Dec-07	Dec-08	Aug-09	Jan-11
SR-91 EB Corridor Operations Project (SR-241 to SR-71)	TBD	N/A	N/A	N/A	N/A
Project J	TBD	Feb-26	TBD	TBD	TBD
I-405, SR-55 to I-605 (Design-Build)	\$2,160.0	Mar-13	Nov-15	Nov-16	Feb-24
Project K	\$2,160.0	May-15	Nov-15	Nov-16	Feb-24

<sup>\*</sup>Status through September 2025. For detailed project information, please refer to the individual project section within this report.

Green = Forecast milestone meets or exceeds plan

Yellow = Forecast milestone is one to three months later than plan Red = Forecast milestone is over three months later than plan

Non-bolded = Planned/Baseline

Comital Businests	Cost Baseline/Forecast			edule Forecast	
Capital Projects	(millions)	Complete Environmental	Complete Design	Award Contract	Complete Construction
I-405, I-5 to SR-55	TBD	Jul-18	TBD	TBD	TBD
Project L	TBD	Aug-18	TBD	TBD	TBD
I-605, I-605/Katella Interchange	\$29.0	Nov-18	Mar-23	Feb-24	Jul-27
Project M	\$53.0	Oct-18	Jan-23	Apr-25	Jul-27
Grade Separation Projects:					
Raymond Avenue Railroad Grade Separation	\$77.2	Nov-09	Aug-12	May-13	Aug-18
Project O	\$126.2	Nov-09	Dec-12	Feb-14	May-18
State College Boulevard Railroad Grade Separation (Fullerton)	\$73.6	Jan-11	Aug-12	May-13	May-18
Project O	\$99.6	Apr-11	Feb-13	Feb-14	Mar-18
Placentia Avenue Railroad Grade Separation	\$78.2	May-01	Mar-10	Jun-11	Nov-14
Project O	\$64.5	May-01	Jun-10	Jul-11	Dec-14
Kraemer Boulevard Railroad Grade Separation	\$70.4	Sep-09	Jul-10	Aug-11	Oct-14
Project O	\$63.8	Sep-09	Jul-10	Sep-11	Dec-14
Orangethorpe Avenue Railroad Grade Separation	\$117.4	Sep-09	Dec-11	May-12	Sep-16
Project O	\$105.9	Sep-09	Oct-11	Jan-13	Oct-16
Tustin Avenue/Rose Drive Railroad Grade Separation	\$103.0	Sep-09	Dec-11	Aug-12	May-16
Project O	\$96.6	Sep-09	Jul-11	Feb-13	Oct-16
Lakeview Avenue Railroad Grade Separation	\$70.2	Sep-09	Oct-11	May-13	Mar-17
Project O	\$110.9	Sep-09	Jan-13	Nov-13	Jun-17
17th Street Railroad Grade Separation	TBD	Jun-16	TBD	TBD	TBD
Project R	TBD	Nov-17	TBD	TBD	TBD
Sand Canyon Avenue Railroad Grade Separation	\$55.6	Sep-03	Jul-10	Feb-11	May-14
Project R	\$61.9	Sep-03	Jul-10	Feb-11	Jan-16

<sup>\*</sup>Status through September 2025. For detailed project information, please refer to the individual project section within this report.



Green = Forecast milestone meets or exceeds plan

Yellow = Forecast milestone is one to three months later than plan

Red = Forecast milestone is over three months later than plan

Non-bolded = Planned/Baseline

Conital Presidents	Cost Baseline/Forecast			edule Forecast	
Capital Projects	(millions)	Complete Environmental	Complete Design	Award Contract	Complete Construction
Transit Projects:					
Rail-Highway Grade Crossing Safety Enhancement	\$94.4	Oct-08	Sep-08	Aug-09	Dec-11
Project R	\$90.4	Oct-08	Sep-08	Aug-09	Dec-11
San Clemente Beach Trail Safety Enhancements	\$6.0	Jul-11	Apr-12	Oct-12	Jan-14
Project R	\$5.0	Jul-11	Jun-12	May-13	Mar-14
Emergency Track Stabilization at MP206.8	N/A	N/A	N/A	N/A	N/A
Project R	\$23.3	N/A	N/A	Oct-22	Aug-23
Placentia Metrolink Station and Parking Structure	\$34.8	May-07	Jan-11	TBD	TBD
Project R	\$40.1	May-07	Feb-11	TBD	TBD
Anaheim Canyon Station	\$27.9	Dec-16	May-19	Nov-19	Jan-23
	\$34.2	Jun-17	Oct-20	Mar-21	Jan-23
Orange Station Parking Expansion	\$33.2	Dec-12	Apr-13	Nov-16	Feb-19
	\$30.9	May-16	Apr-16	Jun-17	Feb-19
Fullerton Transportation Center - Elevator Upgrades	\$3.5	N/A	Dec-13	Sep-14	Mar-17
	\$4.2	N/A	Dec-13	Apr-15	May-19
Laguna Niguel/Mission Viejo Station ADA Ramps	\$3.5	Jan-14	Aug-14	Jan-15	Apr-17
	\$5.2	Feb-14	Jul-15	Oct-15	Sep-17
OC Streetcar	\$671.4	Mar-12	Sep-17	Aug-18	Mar-26
Project S	\$671.4	Mar-15	Nov-17	Sep-18	Mar-26
Anaheim Regional Transportation Intermodal Center	\$227.4	Feb-11	Feb-12	Jul-12	Nov-14
Project R & T	\$232.2	Feb-12	May-12	Sep-12	Dec-14

<sup>\*</sup>Status through September 2025. For detailed project information, please refer to the individual project section within this report.


This Page Intentionally Left Blank



Americans with Disabilities Act	ADA
Anaheim Regional Transportation Intermodal Center	ARTIC
Annual Eligibility Review	AER
Board of Directors	Board
BNSF Railway Company	BNSF
California Department of Transportation	Caltrans
Conservation Properties	Preserves
Construction and Maintenance	C&M
Coronavirus	COVID-19
Comprehensive Transportation Funding Program	CTFP
Early Action Plan	EAP
Environmental Cleanup Allocation Committee	ECAC
Environmental Cleanup Program	ECP
Environmental Document	ED
Environmental Mitigation Program	EMP
Environmental Oversight Committee	EOC
Fire Management Plan	FMP
Fiscal Year	FY
Freeway Service Patrol	FSP
High-Occupancy Vehicle	HOV
Interstate 5	I-5
Interstate 405	I-405
Interstate 605	I-605
Local Fair Share	LFS
Los Angeles – San Diego – San Luis Obispo	LOSSAN
Maintenance and Storage Facility	MSF
Measure M	M1
Measure M2 or Renewed Measure M	M2
Metrolink Service Expansion Program	MSEP
Mile Post	MP
Next 10 Delivery Plan	Next 10 Plan
Natural Community Conservation Plan/Habitat Conservation Plan	Conservation Plan



Orange County Flood Control District	OCFCD
Orange County Transportation Authority	OCTA
Orange County Unified Transportation Trust	OCUTT
Ordinance No. 3	M2 Ordinance
Overhead Contact System	OCS
Pacific Coast Highway	PCH
Program Management Office	PMO
Project Study Report-Project Development Support	PSR-PDS
Project Report	PR
Regional Capacity Program	RCP
Regional Traffic Signal Synchronization Program	RTSSP
Resource Management Plan	RMP
Right-of-Way	ROW
Riverside County Transportation Commission	RCTC
Santa Ana Regional Transportation Center	SARTC
Senior Mobility Program	SMP
Senior Non-Emergency Medical Transportation	SNEMT
Interregional Transportation Improvement Plan	ITIP
State Route 22	SR-22
State Route 55	SR-55
State Route 57	SR-57
State Route 71	SR-71
State Route 74	SR-74
State Route 91	SR-91
State Route 241	SR-241
Southern California Regional Rail Authority	Metrolink
Taxpayer Oversight Committee	TOC
To Be Determined	TBD
Transit and Intercity Rail Capital Program	TIRCP
Transportation Investment Plan	Plan

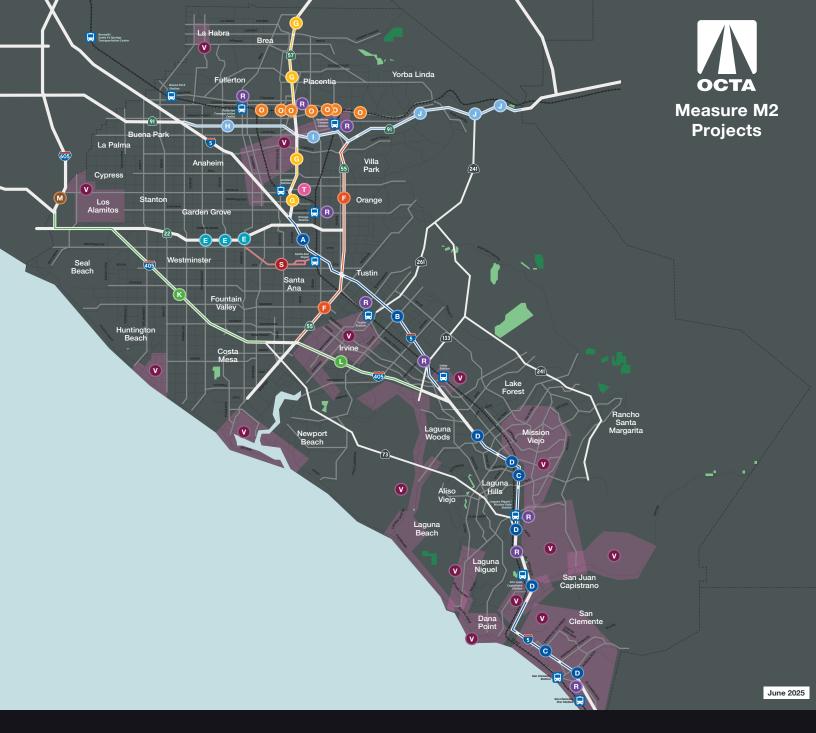

### **Freeway Improvement Program**

### Interstate 5 (I-5) Projects

- A SR-55 to SR-57
- B I-405 to SR-55
- C SR-73 to El Toro Road
- C Avenida Pico to San Juan Creek Road
- D Highway Interchanges

### State Route 22 (SR-22) Projects

E Access Improvements

### State Route 55 (SR-55) Projects

- 1-405 to 1-5
- I-5 to SR-91

- Northbound, Katella Avenue to Lincoln Avenue

### State Route 57 (SR-57) Projects

- Northbound, Orangewood Avenue to Katella Avenue
- Northbound, Orangethorpe Avenue to Lambert Road
- G Northbound, Lambert Road to Tonner Canyon Road

### State Route 91 (SR-91) Projects

- Westbound, I-5 to SR-57
- SR-57 to SR-55
- SR-55 to Riverside County Line

### Interstate 405 (I-405) Projects

- K SR-73 to I-605
- 1-5 to SR-55

### Interstate 605 (I-605) Projects

M Katella Avenue Interchange Improvements

### Freeway Mitigation Program

- Restoration Projects (Part of Projects A-M)
- Acquisition Projects (Part of Projects A-M)

### **Streets & Roads**

- O Grade Separation Program
- Signal Synchronization Project Corridors

## Metrolink Rail Line

Rail

Metrolink Station

### **Transit Projects**

- R Grade Separation and Station Improvement Projects
- S Transit Extensions to Metrolink
- Metrolink Station Conversion to accept Future High-Speed Rail Systems
- Community Based Transit/Circulators

### **Other Projects Not Shown**

### Project N:

Project O:
• Regional Capacity Program

Project Q:
Local Fair Share Program

Project R:
Grade Crossing & Trail Safety Enhancements
Metrolink Service Expansion Program

# Project U: • Senior Mobility Program

- Senior Non-Emergency Medical Transportation Program
- Fare Stabilization Program

Project W:
• Safe Transit Stops

Project X:
• Environmental Cleanup Program
