



Update on State Route 55 Improvement Project from Interstate 405 to Interstate 5


Project Limits and Background



- Borders cities of Irvine, Santa Ana, and Tustin (Cities)
- Partnership with California Department of Transportation and Cities
- Project F in Measure M2
- Average daily traffic is expected to grow five percent from 261,700 to 274,800 by 2040


Project Improvements

Existing

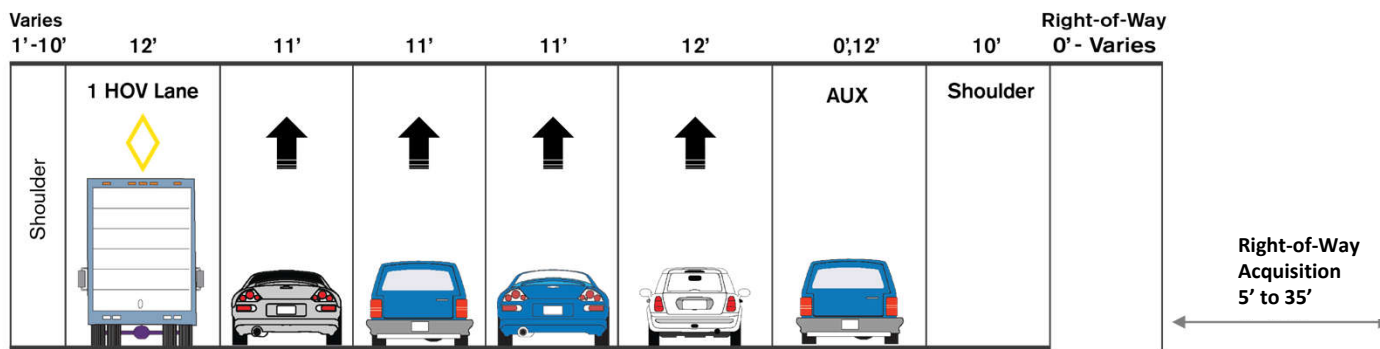

Project Improvements

- Add one high-occupancy vehicle lane in each direction
- Add one general purpose lane in each direction
- Add auxiliary lanes at certain locations

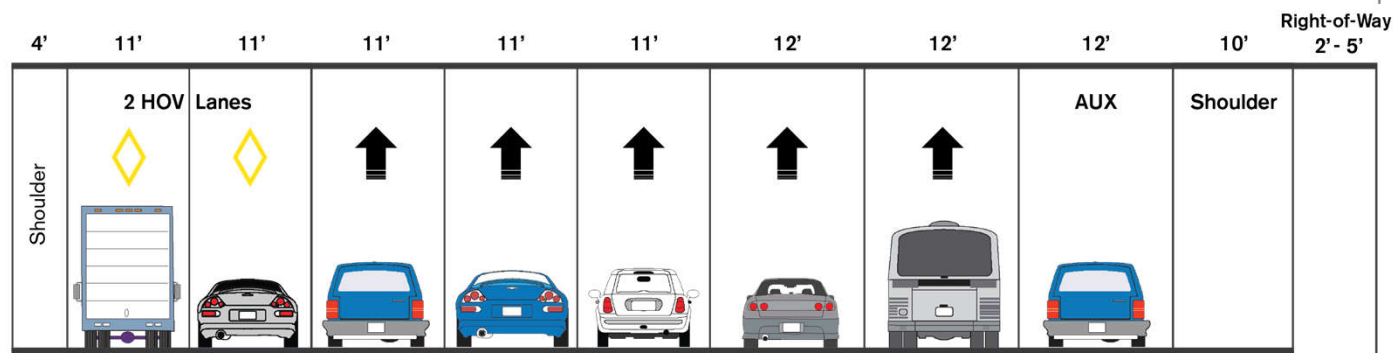

Design

- Project design is 95 percent complete
- Design anticipated to be fully complete by early 2020

Right-of-Way (ROW)

- 32 parcels impacted (24 commercial, 3 residential, 5 public agencies)
- Appraisals were initiated in early 2019
- Property acquisition to commence in December 2019

Utility

- 12 utility companies impacted
- Utility relocation coordination was initiated in early 2018

Project Schedule



	2017	2018	2019	2020	2021	2022	2023	2024
Complete Environmental Phase	✓	September 2017						
Initiate 35 percent Design, ROW Need and Utility Conflicts	✓	September 2017						
Complete 35 percent Design		✓ April 2018						
Initiate ROW Appraisal Maps		✓ June 2018						
Complete 65 percent Plans, Specifications, and Estimates (PS&E)			✓ January 2019					
Initiate ROW Appraisals			✓ February 2019					
Complete 95 percent PS&E			✓ July 2019					
Initiate First Offers to Property Owners			★ December 2019					
Submit 100 percent PS&E				★ January 2020				
ROW Certification				★ October 2020				
Ready To List				★ October 2020				
Construction				Mid-2021 to end-2024				



Next Steps



Activity/Milestone	Date
ROW	
ROW Appraisals	February 2019 to May 2020
Utility Agreements	April 2019 to April 2020
First Offers to Property Owners	December 2019 to June 2020
Obtain ROW Certification	October 2020
Design and Construction	
Complete Design	Early 2020
Obtain Ready to List	Late 2020
Advertise for Construction	Early 2021
Start Construction	Mid-2021

Public Outreach

- Stakeholder ascertainment/briefings
- City Council presentations
- Civic organization briefings
- Business/school outreach
- Community events
- Collateral development
- Construction alerts
- Social media
- Closures/detours map

