

OC Streetcar Project Quarterly Update

Construction—Segment 1



- Pacific Electric Right-of-Way (PEROW)
 - Ongoing installation of overhead contact system (OCS) pole foundations, communication duct banks, and three soundwalls
 - Fairview Street at-grade crossing completed, work began for Fifth Street at-grade crossing which is delayed due to utility conflicts

Westminster and Santa Ana River Bridges



- Bridges substantially complete, preparing for fixed rail installation, ballasted track installation between bridges

Station Stops



Fairview Street Crossing and Station Stop




Raitt Station Stop

Maintenance and Storage Facility (MSF)



- Ongoing installation of on-site utilities, foundation slab, wheel truing, and service and inspection pits
- MSF yard utilities and car wash building slab completed

Construction—Segments 2 Through 5

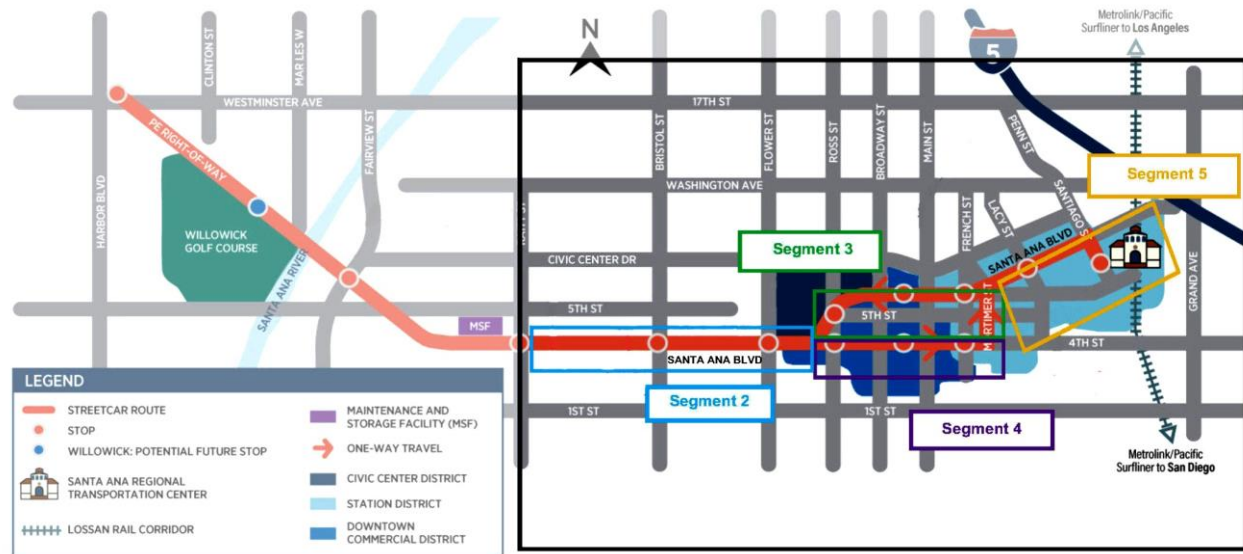

- Completed eastbound and westbound track on Santa Ana Boulevard between Bristol Street and Raitt Street, westbound track from Spurgeon Street to just west of Broadway Street, and a short portion west of Ross Street
- Westbound Santa Ana Boulevard track under construction from Bristol Street to Flower Street
- Curved track completed at Mortimer and Fourth Street
- System installation is on-going

Track and System Installation



Track Installation (cont.)



Upcoming Construction Milestones

- In-street embedded track
- PEROW ballasted track
- OCS and traffic signal pole foundations
- MSF slabs and walls
- Station stop platforms

Vehicles

- Cars 1-7 of the eight S-700 streetcar vehicles are undergoing final equipping of remaining vehicle components
- Car 8 is in final assembly and then will proceed to static and dynamic testing
- Negotiations are ongoing with Siemens Mobility, Inc., regarding options for vehicle storage to align with the availability of the project infrastructure needed to accept and test the vehicles



Outreach

- Bilingual Door Hanger Notices
- Field Meetings
- Downtown Business Associations
- Eat Shop Play Program
- Segment 2B Virtual Meeting

Virtual Community Open House

OC STREETCAR CONSTRUCTION UPDATES

Please visit us02web.zoom.us/j/81701717916 at 6:00 p.m. on September 8 to join the virtual open house. The virtual open house will be held in both English and Spanish.

Call 1-669-900-6833 Meeting ID: 817 0171 7916#) if you prefer to join the meeting by phone.

**September 8,
6:00 - 7:30 p.m.**

A&M Metals

EAT SHOP PLAY

Turn your metal scraps into CASH at A&M Metals!

(714) 384-6006 | www.aandmmetal.com
2301 W 5th St, Santa Ana, CA 92703

OCSTREETCAR
octa.net/eatshopplay

CONSTRUCTION ALERT

WHAT: Current ongoing lane closures will shift to the north side of Santa Ana Boulevard. One lane on the south side will be opened to traffic.

WHEN: The lane closure shift will begin as early as September 4. The work hours will be from 7 a.m. to 4 p.m. but the traffic control will be in place 24/7.

WHERE: On Santa Ana Boulevard from Parton Street to Mortimer Street.

Access to businesses will be maintained. Advance notice will be provided if driveway restrictions or intersection closures are necessary.

This work may be loud. The schedule is subject to change due to inclement weather or unforeseen operational issues.

Legend/Leyenda:
Closed southbound lanes / carriles cerrados en la dirección sur
Open southbound lanes / carriles abiertos en la dirección sur

OCstreetcar.com
OCstreetcar@octa.net
1(844) 7GO-OCSC or 1(844) 746-6272
Facebook.com/OCstreetcar
@OCstreetcar
@OCstreetcar

Naughty Panda

Munchies Vegan Diner

OCSTREETCAR
EAT SHOP PLAY

Grab your favorite plant-based bites
@OCVeganFest on 8/21!
octa.net/eatshopplay
