Update on Measure M2 Project C and D (Interstate 5 Improvement Project Between State Route 73 and El Toro Road)
















Project Background



- Measure M2
 - Project C Interstate 5 (I-5) Between State Route 73 (SR-73) and El Toro Road
 - Portion of Project D Two Local Interchange (IC) Upgrades
- Included in Updated 2024 Next 10 Delivery Plan approved by the Board of Directors
- Delivered in three Segments:
 - Segment 1: From SR-73 to Oso Parkway including Avery Parkway IC
 - Segment 2: From Oso Parkway to Alicia Parkway including La Paz Road IC
 - Segment 3: From Alicia Parkway to El Toro Road

Project Overview



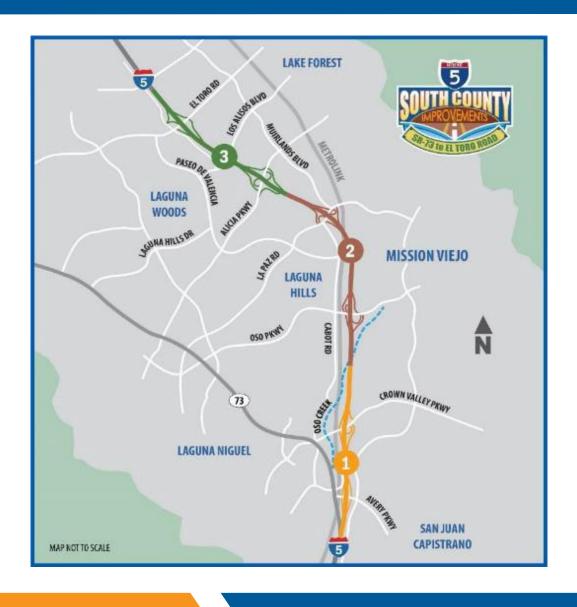

Segment 1

State Route 73 to Oso Parkway

Segment 2

Oso Parkway to Alicia Parkway

Segment 3

Alicia Parkway to El Toro Road

Total length: 6.5 miles

Total Estimated Cost: \$664 million











Major Project Improvements



- New regular lane in both directions from Avery Parkway to Alicia Parkway
- Extend second carpool lane to Alicia Parkway, restripe for continuous access
- New Avery Parkway and La Paz Road interchanges and Los Alisos Boulevard bridge
- Reestablish and add auxiliary lanes
- Realign and/or improve on- and off-ramps


Estimated Construction Schedule




Segment	Estimated Schedule
Segment 1 State Route 73 to Oso Parkway	February 2020 – Early 2025 Under Construction
Segment 2 Oso Parkway to Alicia Parkway	May 2019 – December 2024 Construction is Complete
Segment 3 Alicia Parkway to El Toro Road	January 2021 – Early 2025 Under Construction

Avery Parkway



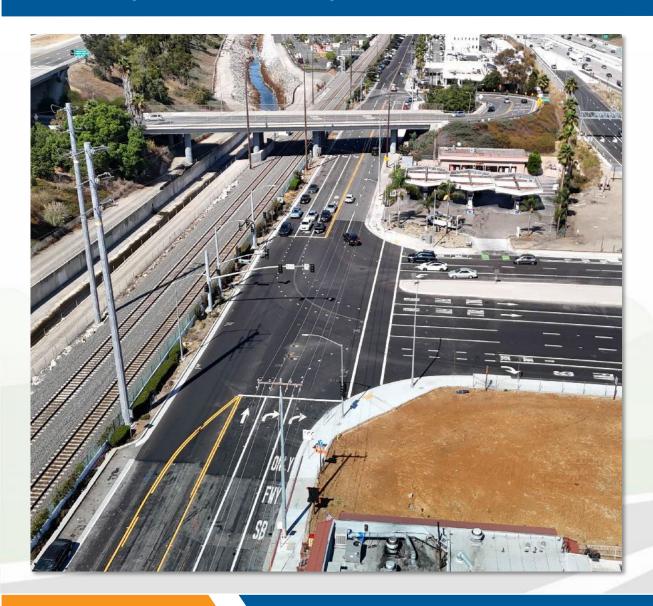


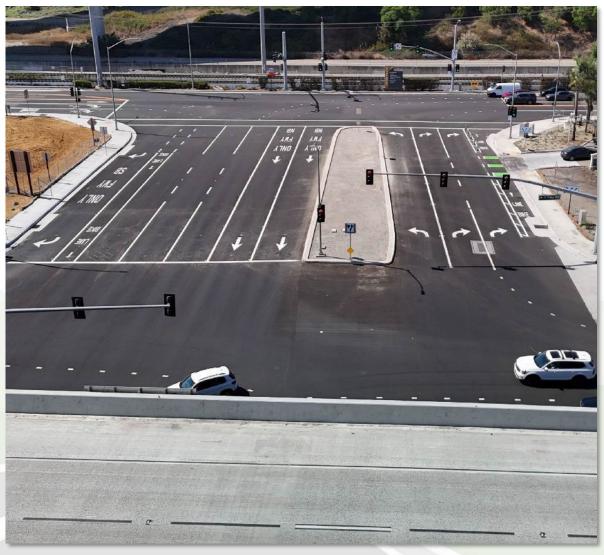

Crown Valley Parkway Ramps






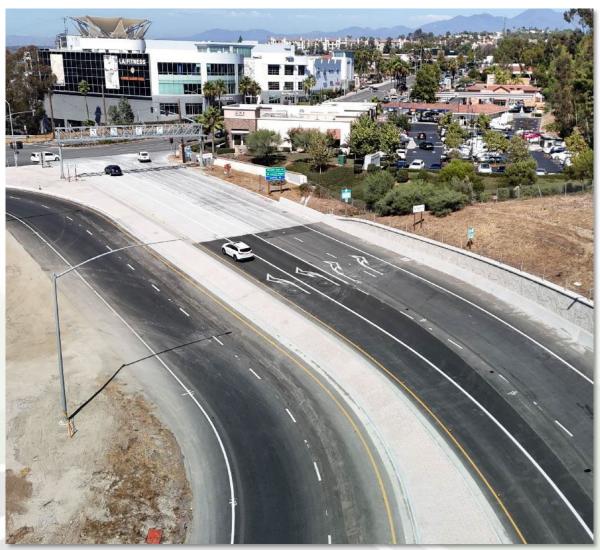

Interstate 5 at La Paz Road



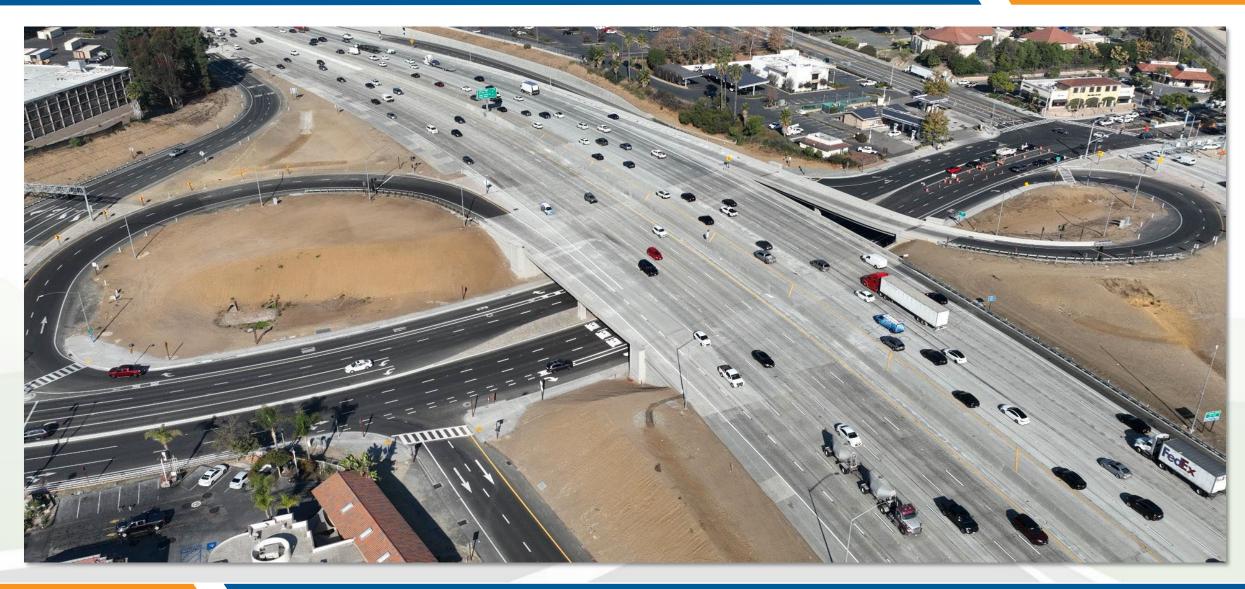

Alicia Parkway Ramps








Interstate 5 at El Toro Road



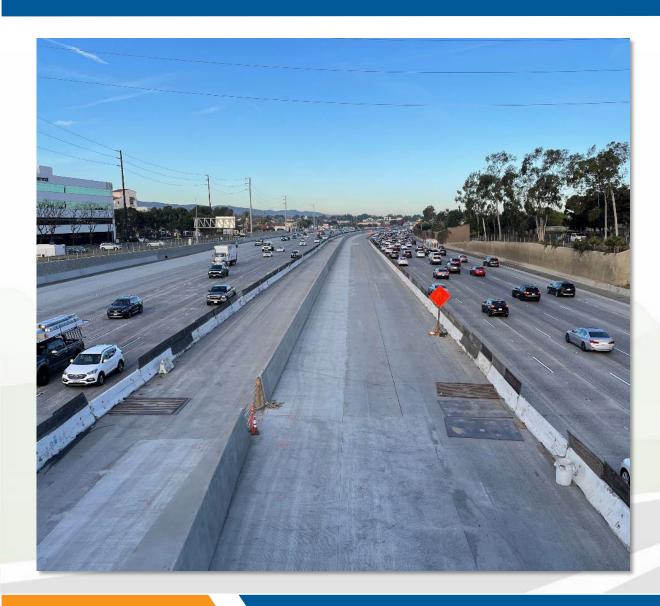



Community Engagement





A PROJECT OF THE ORANGE COUNTY TRANSPORTATION AUTHORITY
AND CALTRANS DISTRICT 12



Special Update - Dec. 19, 2024

THIS WEEK'S CONSTRUCTION

Be Aware, Keep Moving


FULL SOUTHBOUND I-5 FREEWAY CLOSURE AND WEEKEND CLOSURE OF NORTHBOUND I-5 EL TORO ROAD LOOP ON-RAMP ANTICIPATED DEC. 20

A full directional closure of southbound I-5 between El Toro Road and Alicia Parkway for overhead sign installation is anticipated as early as 11 p.m. Friday Dec. 20 to 7 a.m. Saturday, Dec. 21.

Additionally, a weekend closure of the northbound I-5 El Toro Road loop onramp for pavement work is anticipated as early as 11 p.m. Friday, Dec. 20 to 6 a.m. Sunday, Dec. 22.

Detour Maps



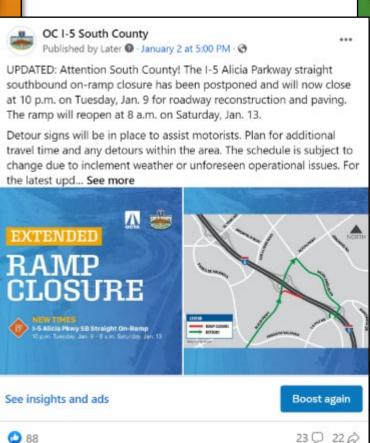

Comment

Like



I-5 El Toro Road Southbound Off-Ramp Closed

Dear Neighbor,

The I-5 El Toro Roed southbound off-ramp will be closed for roadway reconstruction starting Friday, Jan. 19. The ramp will be closed over the weekend and will reopen Monday morning, Jan. 22.

WHEN

I-5 El Toro Road southbound off-ramp closed

11 p.m. Friday, Jan. 19 -5 a.m. Monday, Jan. 22

WHAT TO EXPECT:

Plan for additional travel time through the area.

Detour signs will be in place to assist motorists.

The schedule is subject to change due to inclement weather or unforeseen operational issues.





For additional project information, please visit octa.net/15southcounty

STAY INFORMED



Share







Outreach Team Contact Information





octa.net/i5SouthCounty



i5SouthCounty@octa.net



@OCi5SouthCounty



Facebook.com/OCi5SouthCounty

